


Sumter County Rural Build – RDOF & ARPA Grant Projects – March 2023

Addresses

- Rural Digital Opportunity Fund build (in blue) Complete – 305
- ARPA – Sumter Contract Complete – 180
- March 2023 schedule – 695
- 2nd Quarter 2023, RDOF and ARPA – 202
- 3rd Quarter 2023, RDOF and ARPA – 646
- 4th Quarter 2023, RDOF and ARPA – 1,635
- Total Completions – Year End: 2023 – 3,663
- Remainder projected in 2024
- Construction is in general working from the south to the north of Sumter County

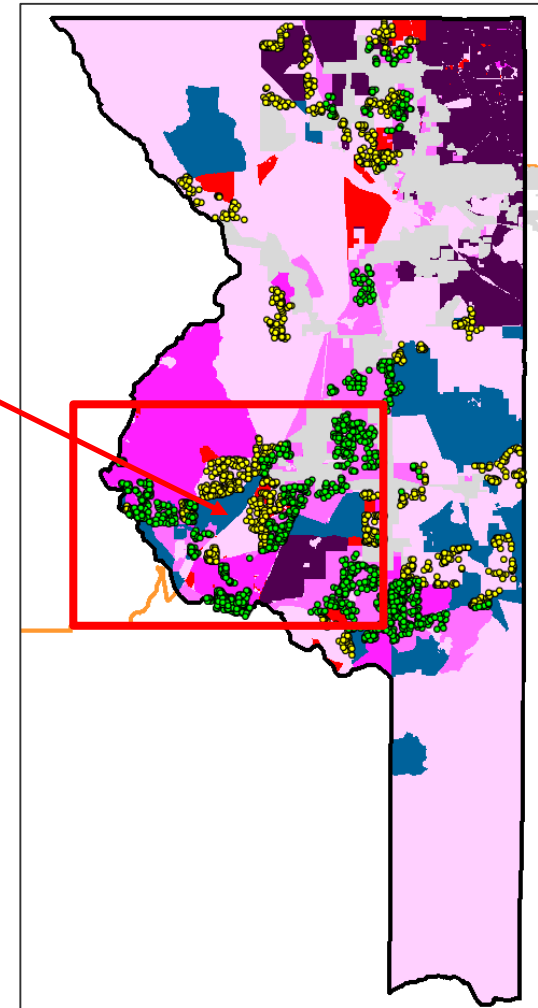

Sumter County – Broadband Opportunity Program - Grant Project

Coming Soon!

- Pending award of 2,418 locations from State Broadband Opportunity Program as all challenges have been rescinded. Please note there is no overlap of RDOF or ARPA funds for this grant project.

