


Sumter County Rural Build – RDOF & ARPA Grant Projects – June 2023

Addresses

- Rural Digital Opportunity Fund build (in blue) Complete – 937
- ARPA – Sumter Contract Complete – 180
- June 2023 schedule – 275
- 2nd Quarter 2023, RDOF and ARPA – 484
- 3rd Quarter 2023, RDOF and ARPA – 1,084
- 4th Quarter 2023, RDOF and ARPA – 1,220
- Total Completions – Year End: 2023 – 3,725
- Remainder projected in 2024
- Construction is in general working from the south to the north of Sumter County

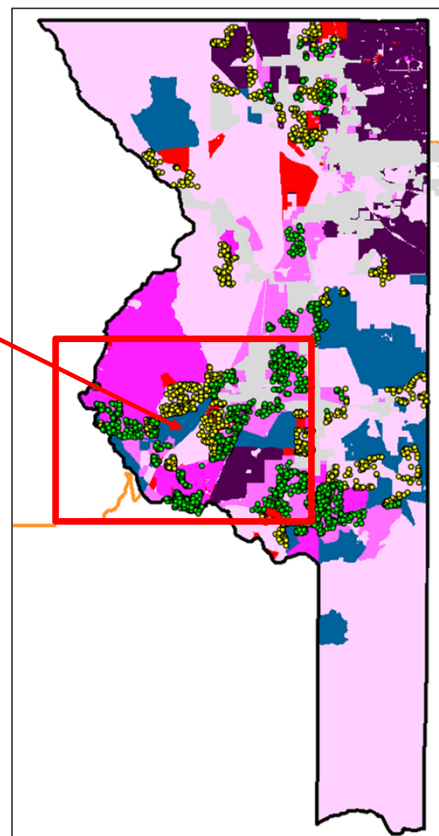

Sumter County – Broadband Opportunity Program - Grant Project

Coming Soon!

- Charter Communications was awarded 2,418 locations in Sumter County from the State Broadband Opportunity Program (Round One).
- Please note there is no overlap of RDOF or ARPA funds for this grant project.
- Anticipate contract with the Florida Department of Economic Opportunity being executed by the end of June or early July.
- Once the contract is executed, Charter Communications can share details regarding timing of activations.

