SUMTER COUNTY BOARD OF COUNTY COMMISSIONERS
MEETING DATE – MARCH 9, 2010
FACILITIES DEVELOPMENT PROJECTS

INDEX PAGE:

1) PROJECT FINANCIAL STATUS REPORT
2) MASTER BUILDING PROJECTS SCHEDULE

SUMTER COUNTY BOARD OF COUNTY COMMISSIONERS
MEETING DATE – MARCH 9, 2010
FACILITIES DEVELOPMENT PROJECTS

TAB 1) PROJECT FINANCIAL STATUS REPORT

Last printed 3/3/2010 8:59:00 AM
PREPARED BY DOUGLAS L. CONWAY

PROJECT FINANCIAL STATUS REPORT
COUNTY BUILDING PROJECTS
PREPARED BY DOUGLAS L CONWAY
SCBOCC MEETING DATE MARCH 9, 2010

LINE ITEM #	SQUARE FEET	% COMP	PROJECT DESCRIPTION	CIP	RECOMMENDED CIP ADJUSTMENT(S)	REVISED CIP TOTALS	PAYMENT TO DATE	ORIGINAL CONTRACT(S) AMOUNT	CHANGE ORDERS	ANTICIPATED FUTURE ITEMS	REVISED CONTRACT(S) AMOUNT	GAIN OR (LOSS)	COST PER SQ FT	PROJECT STATUS
			BUSHNELL CAMPUS RENOVATIONS :											
1	22,000	2%	JUDICIAL CENTER RENOVATIONS 1ST FL	$3,236,111	$0	$3,236,111	$72,020	$74,520	$0	$3,161,591	$3,236,111	$0	$147	SCHEMATIC DESIGN
2	11,916	6%	HISTORIC COURTHOUSE - 1ST FLOOR -- STATE ATTORNEY	$1,308,577	$0	$1,308,577	$82,415	$132,216	$0	$1,176,361	$1,308,577	$0	$109.82	DESIGN - CONSTRUCTION DOCUMENTS
3	16,000	0%	HISTORIC COURTHOUSE 2ND FLOOR	$720,000	$0	$720,000	$0	$41,760	$0	$678,240	$720,000	$0	$45	DESIGN PHASE
4	16,000	0%	HISTORIC COURTHOUSE 3RD FLOOR	$720,000	$0	$720,000	$0	$43,506	$0	$676,494	$720,000	($0)	$45.00	DESIGN PHASE
5	45,000	0%	HISTORIC COURTHOUSE EXTERIOR ENVELOP	$500,000	$0	$500,000	$0	$6,450	$0	$493,550	$500,000	$0	$11	DESIGN PHASE
6	5,000	21%	COURTHOUSE SECURITY VESTIBULE \ RESTROOMS AND SECURITY DOORS FOR BOTH FACILITIES	$1,665,997	$0	$1,665,997	$349,386	$1,482,007	$0	$183,990	$1,665,997	($0)	$333	CONST. PHASE - VERTICAL CAST IN PLACE CONCRETE
	33,916		**BUSHNELL CAMPUS RENOVATIONS TOTAL**	**$8,150,685**	**$0**	**$8,150,685**	**$503,821**	**$1,780,459**	**$0**	**$6,370,226**	**$8,150,685**	**($0)**	$240	
			JAIL EXPANSION PROJECT FACILITIES											**CONTRACT CLOSE - OUT PHASE - 02 26 2010**
7	N/A		JAIL SITEWORK	$1,646,935	$0	$1,646,935	$1,613,358	$1,670,012	$0	$0	$1,670,012	($23,077)		SWFWMD APPROVED
8	29,335		IMMEDIATE NEEDS FACILITY	$5,242,156	$0	$5,242,156	$4,910,065	$4,900,037	$0	$0	$4,900,037	$342,119	$167	CERTIFICATE OF OCCUPANCY - 08 10 2009
9	19,052		180 BED HOUSING FACILITY	$2,572,500	$0	$2,572,500	$2,491,549	$2,462,137	$0	$0	$2,462,137	$110,363	$129	CERTIFICATE OF OCCUPANCY - 08 10 2009
10	5,521		KITCHEN FACILITY	$603,089	$0	$603,089	$1,136,461	$1,133,427	$0	$0	$1,133,427	($530,338)	$205	CERTIFICATE OF OCCUPANCY - 08 03 2009
11	44,699		INTAKE AND RELEASE FACILITY	$7,998,000	$0	$7,998,000	$7,733,335	$7,644,268	$0	$0	$7,644,268	$353,732	$171	CERTIFICATE OF OCCUPANCY - 12 03 2009
12	1,955		VIDEO VISITATION	$358,530	$0	$358,530	$585,619	$582,321	$0	$0	$582,321	($223,791)	$298	CERTIFICATE OF OCCUPANCY - 08 03 2009
			EQUIP - VIDEO CARRELS - LAUNDRY & KITCHEN - BEDS	$718,680	$0	$718,680	$718,680	$718,680	$0	$0	$718,680	$0		
			JAIL CONST. MGT FEE	$2,256,575	$0	$2,256,575	$2,256,575	$2,256,575	$0	$0	$2,256,575	$0		
			PROJECT CONTINGENCY PER GMP	$603,535	$0	$603,535	$0	$0	$0	$399,495	$399,495	$204,040		
			AMENDMENT # 1	$0	$0	$0	$442,919	$442,919	$0	$0	$442,919	($442,919)	$0	
			AMENDMENT # 1 - REVISED	$255,850	$0	$255,850	$162,300	$162,300	$0	$0	$162,300	$93,550		
			AMENDMENT # 2 - 1988 FIRE ALARM SYSTEM	$295,063	$0	$295,063	$74,135	$74,135	$0	$0	$74,135	$220,928		
			AMENDMENT # 3 - OWNER DIRECT PURCHASE	($5,332,500)	$0	($5,332,500)	($5,332,500)	($5,332,500)	$0	$0	($5,332,500)	$0		
	100,562		A D MORGAN - GMP TOTAL	$17,218,413	$0	$17,218,413	$16,792,496	$16,714,311	$0	$399,495	$17,113,806	$104,607	$170	
			JAIL ARCHITECT - ENGINEER FEES	$2,134,000	$0	$2,134,000	$2,208,087	$2,134,000	$104,606	$0	$2,238,606	($104,607)		
			CITY OF BUSHNELL - UTILITIES	$157,303	$0	$157,303	$157,303	$157,303	$0	$0	$157,303	$0		
			OWNER DIRECT PURCHASE MATERIALS & EQUIP -SCBOCC	$5,332,500	$0	$5,332,500	$5,332,500	$5,332,500	$0	$0	$5,332,500	$0		
	100,562	99%	**JAIL EXPANSION TOTAL**	**$24,842,216**	**$0**	**$24,842,216**	**$24,490,386**	**$24,338,114**	**$104,606**	**$399,495**	**$24,842,215**	**$0**	$247	
13			MAIN JAIL (1988) RENOVATIONS	$1,500,000	$0	$1,500,000	$0	$0	$0	$1,500,000	$1,500,000	$0		RFP FOR ARCHITECT AND ENGINEER DUE 0 08 2010
14	45,941	10%	THE VILLAGES SUMTER COUNTY SERVICE CENTER & LIBRARY	$8,000,000	$0	$8,000,000	$839,229	$6,117,418	$20,412	$1,862,170	$8,000,000	$0	$174	FIRST FLOOR STRUCTURAL STEEL
			FIRE STATION PROJECTS											
15	5,850	12%	FIRE & RESCUE STATION 31 AT WILDWOOD - RENOVATION	$293,820	$0	$293,820	$36,561	$45,635	$0	$248,185	$293,820	$0	$50	PREPARING BID DOCUMENTS FOR GENERAL CONTRACTOR
16	5,355	11%	FIRE & RESCUE STATION 32 AT OXFORD - RENOVATION	$352,000	$0	$352,000	$37,786	$47,268	$0	$304,732	$352,000	$0	$66	PREPARING BID DOCUMENTS FOR GENERAL CONTRACTOR
17	6,500	5%	FIRE & RESCUE STATION 22 AT WEST BUSHNELL - PROTOTYPE	$1,001,409	$0	$1,001,409	$48,278	$70,432	$0	$930,977	$1,001,409	$0	$154	PREPARING BID DOCUMENTS FOR GENERAL CONTRACTOR
18	6,500	11%	FIRE & RESCUE STATION 33 AT COLEMAN - PROTOTYPE	$836,409	$0	$836,409	$89,558	$112,637	$0	$723,772	$836,409	$0	$129	PREPARING BID DOCUMENTS FOR GENERAL CONTRACTOR
			FACILITIES MAINTENANCE PROJECTS											
			FEMA GROUNDHOG DAY GRANTS											
19		56%	LAKE PANASOFFKEE COMMUNITY CENTER - phase 1	$36,000	$12,000	$48,000	$27,000	$33,887	$0	$14,113	$48,000	$0		A/E DESIGN SUBMITTED TO STATE FOR REVIEW
20		15%	SHERIFF'S ADMINISTRATION OFFICE - BUSHNELL	$22,034	$7,345	$29,379	$4,500	$4,500	$0	$24,879	$29,379	$0		A/E DESIGN SUBMITTED TO STATE FOR REVIEW
21		29%	CENTER HILL CITY HALL - phase 1 only	$8,387	$2,795	$11,182	$3,200	$3,200	$0	$7,982	$11,182	$0		A/E DESIGN SUBMITTED TO STATE FOR REVIEW
22		69%	BUSHNELL COMMUNITY CENTER - phase 1 only	$12,750	$4,250	$17,000	$11,704	$11,704	$0	$5,296	$17,000	$0		A/E DESIGN SUBMITTED TO STATE FOR REVIEW
22	286,624		PROJECT TOTALS	$45,055,710	$26,390	$45,082,100	$26,092,023	$32,565,254	$125,018	$12,391,827	$45,082,100	($0)		

SUMTER COUNTY BOARD OF COUNTY COMMISSIONERS
MEETING DATE – MARCH 9, 2010
FACILITIES DEVELOPMENT PROJECTS

TAB 2) MASTER BUILDING PROJECTS SCHEDULE

Last printed 3/3/2010 9:00:00 AM
PREPARED BY DOUGLAS L CONWAY

ID	Task Name	Duration	Start	Finish	Predecessors
1					
2					
3					
4					
5	**JUDICIAL CENTER - RENOVATIONS 1ST FLOOR ONLY**	**1759 days**	**Wed 2/20/08**	**Fri 11/14/14**	
6	SPACE PROGRAM	75 days	Wed 2/20/08	Mon 6/2/08	
7	EVALUATE EXISTING BUILDING	75 days	Wed 2/20/08	Mon 6/2/08	
8	CONCEPTUAL DESIGN PHASE FOR OPTIONS & FEASIBILITY	225 days	Tue 6/3/08	Tue 5/19/09	
9	FINAL DESIGN - CONSTRUCTION DRAWINGS & SPECIFICATIONS -	90 days	Mon 12/2/13	Fri 4/4/14	
10	BIDDING AND CONSTRUCTION PHASE	160 days	Mon 4/7/14	Fri 11/14/14	9
11	**HISTORICAL COURTHOUSE RENOVATIONS 1ST FLOOR ONLY**	**705 days**	**Wed 2/20/08**	**Mon 11/1/10**	
12	SPACE PROGRAM	40 days	Wed 2/20/08	Mon 4/14/08	
13	EVALUATE EXISTING BUILDING	39 days	Wed 2/20/08	Fri 4/11/08	
14	CONCEPTUAL DESIGN PHASE FOR OPTIONS & FEASIBILITY	37 days	Mon 3/31/08	Tue 5/20/08	
15	SCBOCC APPROVAL OF FINAL DESIGN PHASE FEES	1 day	Tue 5/27/08	Tue 5/27/08	14
16	FINAL DESIGN - CONSTRUCTION DRAWINGS & SPECIFICATIONS	466 days	Wed 5/28/08	Wed 3/10/10	15
17	BIDDING PHASE	45 days	Mon 4/19/10	Fri 6/18/10	
18	CONSTRUCTION PHASE - SHALL BEGIN ONCE THE SECURITY VESTIBULE IS COMPLETE	120 days	Tue 5/18/10	Mon 11/1/10	26
19					
20					
21	**COURTHOUSE SECURITY VESTIBULE \ RESTROOMS AND SECURITY DOORS FOR BOTH FACILITIES**	**490 days**	**Tue 7/1/08**	**Mon 5/17/10**	
22	DESIGN	229 days	Tue 7/1/08	Fri 5/15/09	
23	PERMIT	5 days	Mon 5/18/09	Fri 5/22/09	22
24	BIDDING	55 days	Wed 7/29/09	Tue 10/13/09	22
25	CONSTRUCTION	135 days	Wed 11/4/09	Tue 5/11/10	24
26	FACILITY SET-UP & OCCUPANCY	4 days	Wed 5/12/10	Mon 5/17/10	25
27					

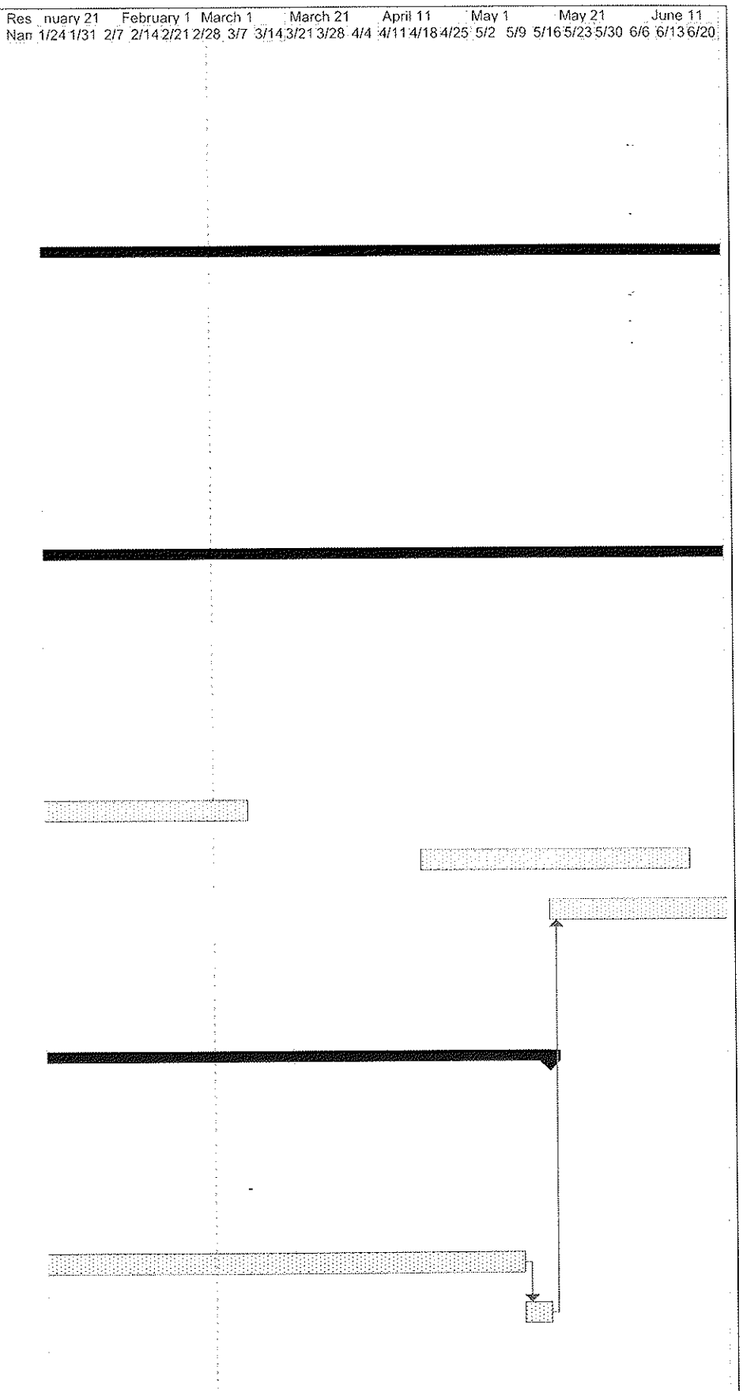

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors
28	**JAIL EXPANSION PROJECT INCLUDES THE FOLLOWING FACILITIES:**	539 days	Wed 10/10/07	Fri 10/30/09	
29	**SITEWORK - CONSTRUCTION**	434 days	Tue 8/14/07	Thu 4/9/09	
30					
31	**IMMEDIATE NEEDS POD FACILITY**	**521 days**	**Tue 8/14/07**	**Mon 8/10/09**	
32					
33	DESIGN	110 days	Tue 8/14/07	Mon 1/14/08	
34	BIDDING	34 days	Thu 1/10/08	Tue 2/26/08	
35	PERMITTING	44 days	Tue 1/15/08	Fri 3/14/08	
36	CONSTRUCTION	393 days	Thu 2/7/08	Fri 8/7/09	
37	FACILITY SET-UP & OCCUPANCY	1 day	Mon 8/10/09	Mon 8/10/09	36
38					
39	**180 BED HOUSING FACILITY**	**521 days**	**Tue 8/14/07**	**Mon 8/10/09**	
40	DESIGN	110 days	Tue 8/14/07	Mon 1/14/08	
41	PERMITTING	46 days	Mon 1/14/08	Sat 3/15/08	
42	BIDDING	34 days	Thu 1/10/08	Tue 2/26/08	
43	CONSTRUCTION	369 days	Wed 3/12/08	Fri 8/7/09	
44	FACILITY SET-UP & OCCUPANCY	1 day	Mon 8/10/09	Mon 8/10/09	43
45					
46	**KITCHEN FACILITY**	**516 days**	**Tue 8/14/07**	**Mon 8/3/09**	
47	DESIGN	110 days	Tue 8/14/07	Mon 1/14/08	
48	BIDDING	32 days	Mon 1/14/08	Tue 2/26/08	
49	PERMIT	74 days	Mon 1/14/08	Wed 4/23/08	
50	CONSTRUCTION	361 days	Sat 3/15/08	Fri 7/31/09	
51	FACILITY SET-UP & OCCUPANCY	1 day	Mon 8/3/09	Mon 8/3/09	
52	**INTAKE & RELEASE FACILITY**	**650 days**	**Tue 8/14/07**	**Fri 2/5/10**	
53	DESIGN	187 days	Tue 8/14/07	Tue 4/29/08	
54	PERMIT	15 days	Wed 4/30/08	Tue 5/20/08	53

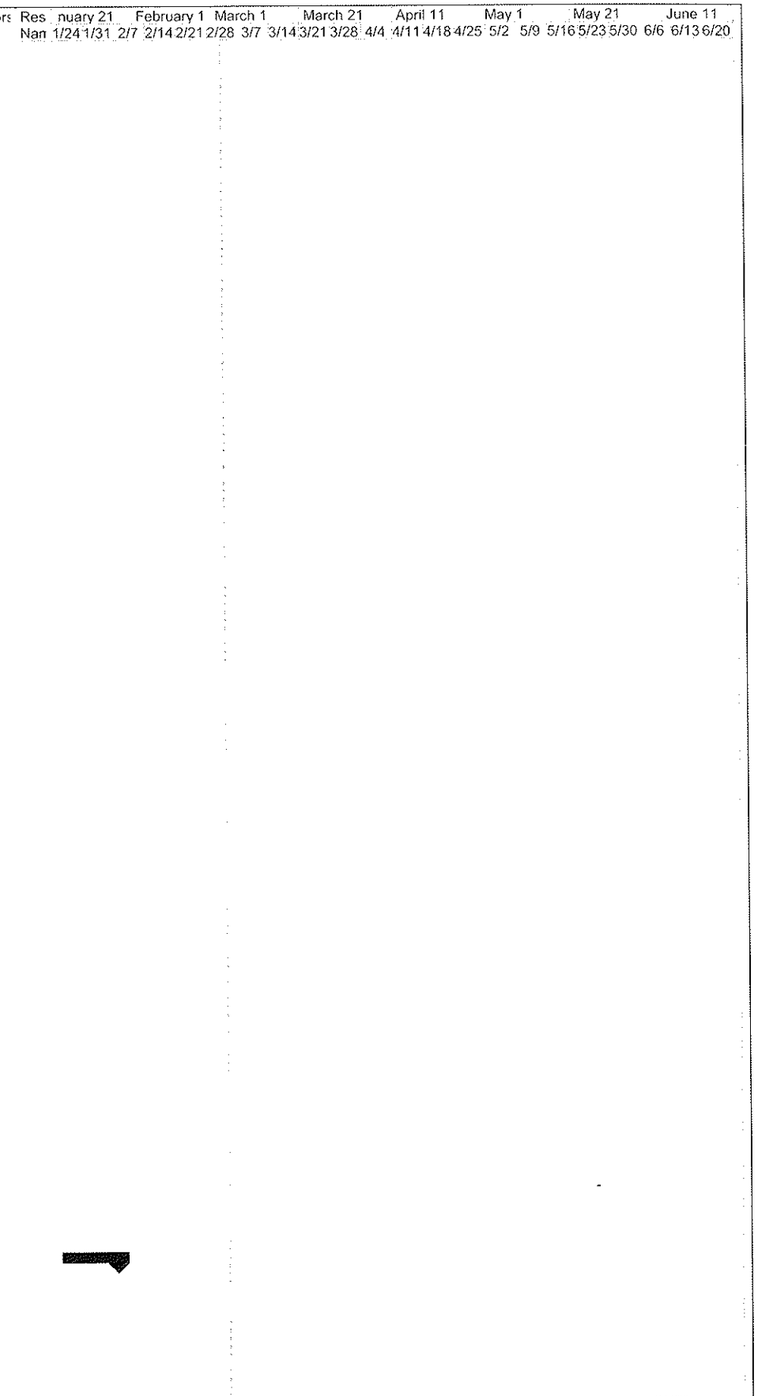

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors
55	BIDDING	47 days	Wed 4/30/08	Thu 7/3/08	53
56	CONSTRUCTION	411 days	Fri 7/4/08	Fri 1/29/10	55
57	FACILITY SET-UP & OCCUPANCY	5 days	Mon 2/1/10	Fri 2/5/10	56
58					
59	**VIDEO VISITATION**	**516 days**	**Tue 8/14/07**	**Mon 8/3/09**	
60	DESIGN - CONST. DOCUMENTS	255 days	Tue 8/14/07	Fri 8/1/08	
61	PERMIT	10 days	Mon 8/4/08	Fri 8/15/08	60
62	BIDDING	25 days	Wed 9/10/08	Tue 10/14/08	
63	CONSTRUCTION	150 days	Mon 1/5/09	Fri 7/31/09	62
64	FACILITY SET-UP & OCCUPANCY	1 day	Mon 8/3/09	Mon 8/3/09	63
65					
66	**1988 MAIN JAIL RENOVATION**	**282 days**	**Mon 1/18/10**	**Tue 2/15/11**	
67	RFP FOR A/E SERVICES	50 days	Mon 1/18/10	Fri 3/26/10	
68	SCBOCC AWARD A/E CONTRACT	1 day	Mon 3/29/10	Mon 3/29/10	67
69	DESIGN	60 days	Tue 3/30/10	Mon 6/21/10	68
70	RFP FOR GENERAL CONTRACTOR	45 days	Tue 6/22/10	Mon 8/23/10	69
71	SCBOCC AWARD CONTRACT	1 day	Tue 8/24/10	Tue 8/24/10	70
72	CONSTRUCTION PHASE	120 days	Wed 8/25/10	Tue 2/8/11	71
73	FACILITY SET-UP AND OCCUPANCY	5 days	Wed 2/9/11	Tue 2/15/11	72
74					
75	**THE VILLAGES SUMTER COUNTY SERVICE CENTER & LIBRARY FACILITY**	**584.5 days**	**Mon 5/26/08**	**Fri 8/20/10**	
76	PRELIM - STAFF PROGRAM	110 days	Mon 5/26/08	Fri 10/24/08	
77	A/E RFP	52 days	Mon 2/16/09	Tue 4/28/09	76
78	A/E PROGRAM	15 days	Wed 4/29/09	Tue 5/19/09	77
79	SECHEMATIC DESIGN	20 days	Wed 5/20/09	Tue 6/16/09	78
80	DESIGN DEVELOPMENT	30 days	Wed 6/17/09	Tue 7/28/09	79
81	CONSTRUCTION DRAWINGS AND SPECS	60 days	Wed 7/29/09	Tue 10/20/09	80

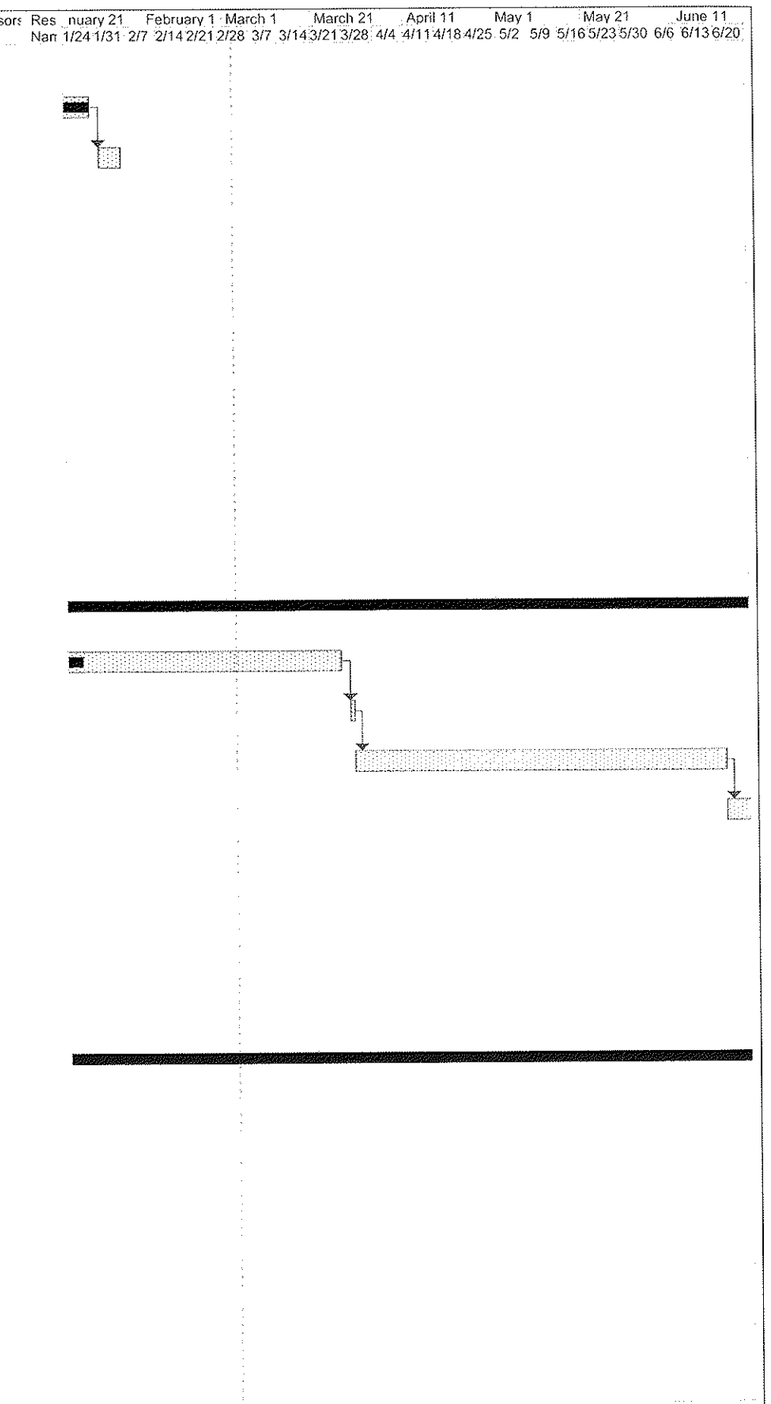

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors
82	PERMIT	15 days	Wed 10/21/09	Tue 11/10/09	81
83	BIDDING	22 days	Fri 10/30/09	Tue 12/8/09	82
84	CONSTRUCTION	178 days	Tue 12/8/09	Fri 8/13/10	83
85	FACILITY SET-UP & OCCUPANCY	5 days	Fri 8/13/10	Fri 8/20/10	84
86					
87	**FIRE STATION # 22 BUSHNELL - PROTOTYPE**	**301 days**	**Tue 8/18/09**	**Tue 10/12/10**	
88	RFP FOR A/E SERVICES	35 days	Tue 8/18/09	Mon 10/5/09	
89	SELECTION COMMITTEE REVIEW TO SHORT LIST	1 day	Tue 10/13/09	Tue 10/13/09	
90	A/E PRESENTATIONS	1 day	Fri 10/23/09	Fri 10/23/09	89
91	SCBOCC APPROVE NEGOTIATION	1 day	Tue 10/27/09	Tue 10/27/09	90
92	STAFF CONTRACT NEGOTIATIONS	5 days	Wed 10/28/09	Tue 11/3/09	91
93	SCBOCC APPROVE CONTRACT	1 day	Tue 11/10/09	Tue 11/10/09	
94	NOTICE TO PROCEED	1 day	Wed 11/11/09	Wed 11/11/09	93
95	DESIGN PHASE	78 days	Thu 11/12/09	Mon 3/1/10	94
96	BID PHASE FOR GENERAL CONTRACTOR	30 days	Wed 3/10/10	Tue 4/20/10	
97	SELECTION COMMITTEE REVIEW	5 days	Wed 4/21/10	Tue 4/27/10	96
98	SCBOCC CONTRACT APPROVAL	1 day	Tue 3/9/10	Tue 3/9/10	
99	CONSTRUCTION PHASE	150 days	Wed 3/10/10	Tue 10/5/10	98
100	FACILITY SET - UP AND OCCUPANCY	5 days	Wed 10/6/10	Tue 10/12/10	99
101					
102					
103	**FIRE STATION # 31 WILDWOOD - RENOVATION**	**301 days**	**Tue 8/18/09**	**Tue 10/12/10**	
104	RFP FOR A/E SERVICES	35 days	Tue 8/18/09	Mon 10/5/09	
105	SELECTION COMMITTEE REVIEW TO SHORT LIST	1 day	Tue 10/13/09	Tue 10/13/09	
106	A/E PRESENTATIONS	1 day	Fri 10/23/09	Fri 10/23/09	
107	SCBOCC APPROVE NEGOTIATION	1 day	Tue 10/27/09	Tue 10/27/09	
108	STAFF CONTRACT NEGOTIATIONS	5 days	Wed 10/28/09	Tue 11/3/09	107

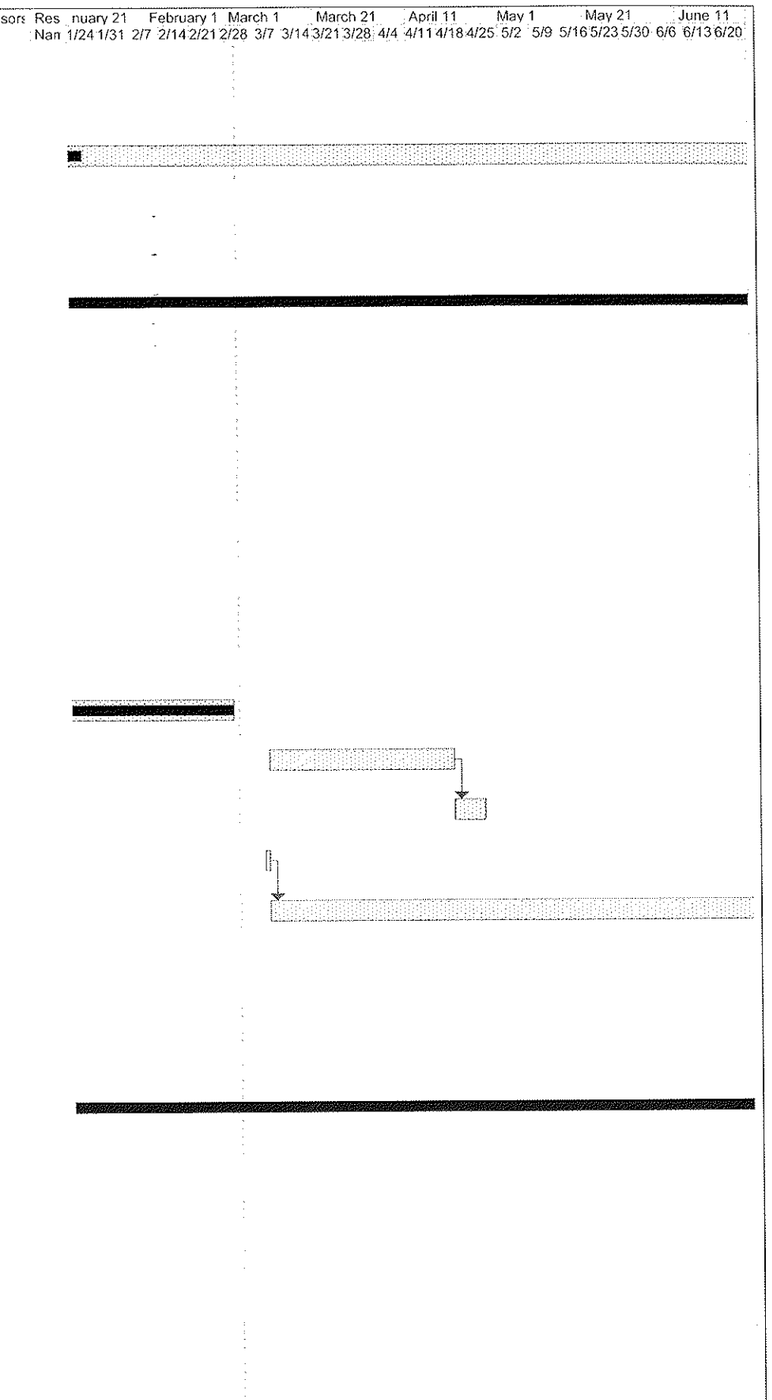

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors
109	SCBOCC APPROVE A/ ECONTRACT	1 day	Tue 11/10/09	Tue 11/10/09	
110	NOTICE TO PROCEED	1 day	Wed 11/11/09	Wed 11/11/09	109
111	DESIGN PHASE	78 days	Thu 11/12/09	Mon 3/1/10	110
112	BID PHASE FOR GENERAL CONTRACTOR	30 days	Wed 3/10/10	Tue 4/20/10	
113	SELECTION COMMITTEE REVIEW	5 days	Wed 4/21/10	Tue 4/27/10	112
114	SCBOCC CONTRACT APPROVAL	1 day	Tue 3/9/10	Tue 3/9/10	
115	CONSTRUCTION PHASE	150 days	Wed 3/10/10	Tue 10/5/10	114
116	FACILITY SET - UP AND OCCUPANCY	5 days	Wed 10/6/10	Tue 10/12/10	115
117					
118	**FIRE STATION # 32 OXFORD - RENOVATION**	**301 days**	**Tue 8/18/09**	**Tue 10/12/10**	
119	RFP FOR A/E SERVICES	35 days	Tue 8/18/09	Mon 10/5/09	
120	SELECTION COMMITTEE REVIEW TO SHORT LIST	1 day	Tue 10/13/09	Tue 10/13/09	
121	A/E PRESENTATIONS	1 day	Fri 10/23/09	Fri 10/23/09	
122	SCBOCC APPROVE NEGOTIATION	1 day	Tue 10/27/09	Tue 10/27/09	
123	STAFF CONTRACT NEGOTIATIONS	5 days	Wed 10/28/09	Tue 11/3/09	122
124	SCBOCC APPROVE A/E CONTRACT	1 day	Tue 11/10/09	Tue 11/10/09	
125	NOTICE TO PROCEED	1 day	Wed 11/11/09	Wed 11/11/09	124
126	DESIGN PHASE	78 days	Thu 11/12/09	Mon 3/1/10	125
127	BID PHASE FOR GENERAL CONTRACTOR	30 days	Wed 3/10/10	Tue 4/20/10	126
128	SELECTION COMMITTEE REVIEW	5 days	Wed 4/21/10	Tue 4/27/10	127
129	SCBOCC GC CONTRACT APPROVAL	1 day	Tue 3/9/10	Tue 3/9/10	
130	CONSTRUCTION PHASE	150 days	Wed 3/10/10	Tue 10/5/10	129
131	FACILITY SET - UP AND OCCUPANCY	5 days	Wed 10/6/10	Tue 10/12/10	130
132					
133					
134	**FIRE STATION # 33 - COLEMAN - PROTOTYPE**	**337 days**	**Tue 8/18/09**	**Wed 12/1/10**	
135	RFP FOR A/E SERVICES	35 days	Tue 8/18/09	Mon 10/5/09	

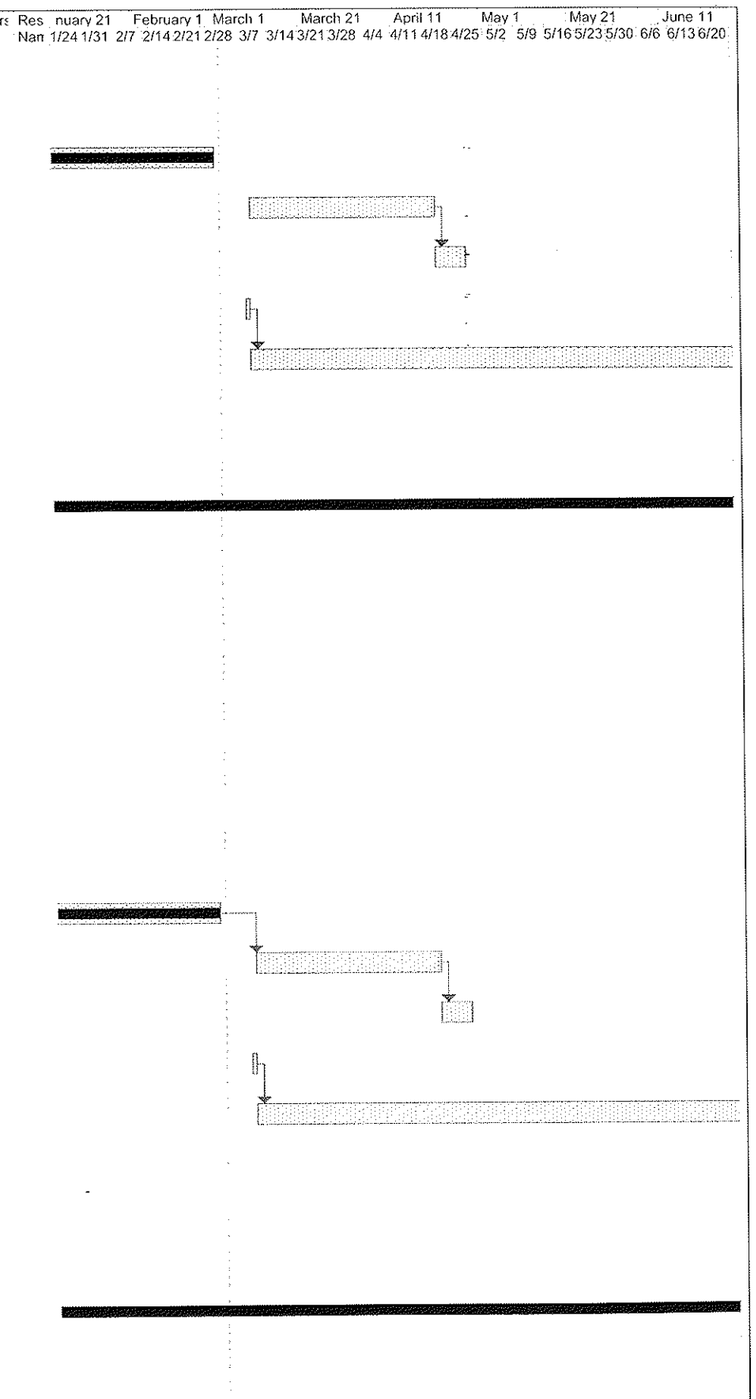

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors
136	SELECTION COMMITTEE REVIEW TO SHORT LIST	1 day	Tue 10/13/09	Tue 10/13/09	
137	A/E PRESENTATIONS	1 day	Fri 10/23/09	Fri 10/23/09	
138	SCBOCC APPROVE NEGOTIATION	5 days	Tue 10/27/09	Mon 11/2/09	137
139	STAFF CONTRACT NEGOTIATIONS	1 day	Wed 10/28/09	Wed 10/28/09	
140	SCBOCC APPROVE A\E CONTRACT	1 day	Tue 11/10/09	Tue 11/10/09	139
141	NOTICE TO PROCEED	1 day	Wed 11/11/09	Wed 11/11/09	140
142	DESIGN PHASE	78 days	Thu 11/12/09	Mon 3/1/10	141
143	BID PHASE FOR GENERAL CONTRACTOR	30 days	Wed 3/10/10	Tue 4/20/10	142
144	SELECTION COMMITTEE REVIEW	5 days	Wed 4/21/10	Tue 4/27/10	143
145	SCBOCC CONTRACT APPROVAL	1 day	Wed 4/28/10	Wed 4/28/10	144
146	CONSTRUCTION PHASE	150 days	Thu 4/29/10	Wed 11/24/10	145
147	FACILITY SET - UP AND OCCUPANCY	5 days	Thu 11/25/10	Wed 12/1/10	146

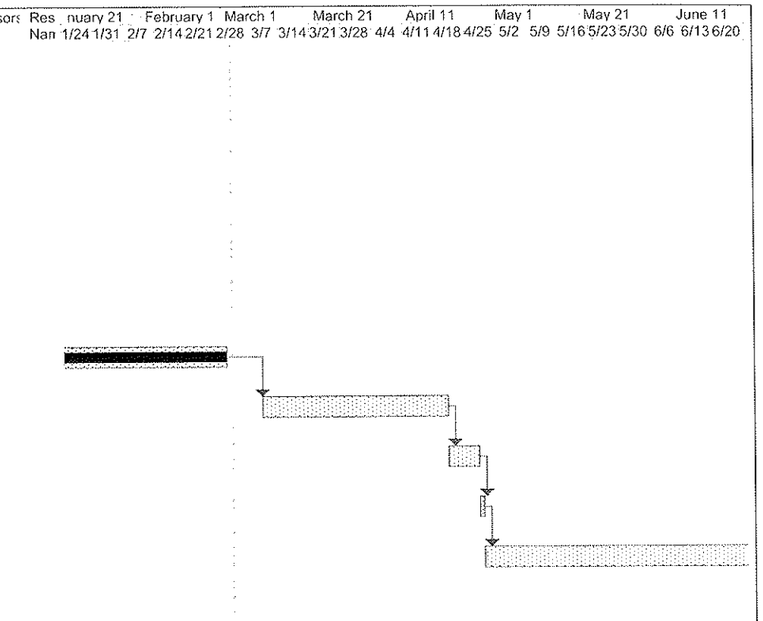

Project: JUDICIAL SCHEDULE
Date: Wed 3/3/10

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
