



SUMTER COUNTY FIRE AND RESCUE STATIONS




RFQ 138-0-2009 / AT

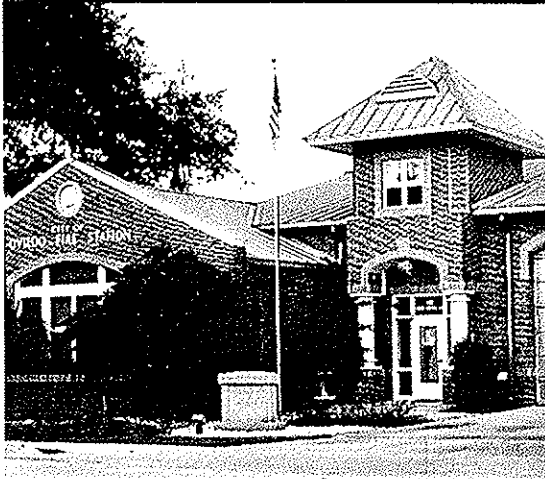

Baker
Barrios

Agendas

- Team
- Experience
- Schedule / Process
- Quality Control
- Construction Administration
- Budget / Cost Control
- Fire Station Design
- Case Study
- Concluding Remarks

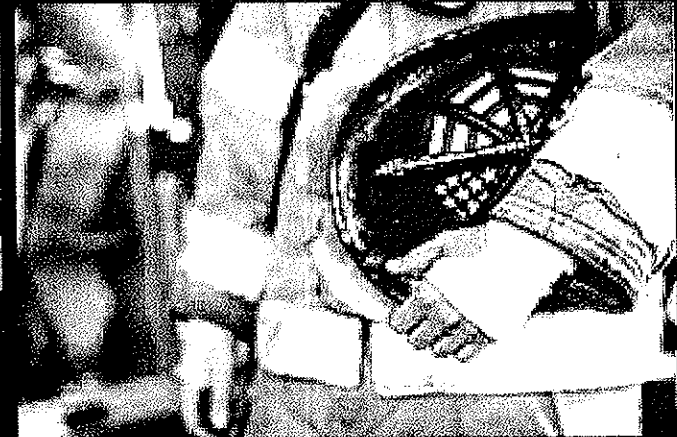

Team:



BAKER BARRIOS ARCHITECTS, INC.

Carlos Barrios, AIA
Principal-In-Charge / QA / QC

Mike Houseman, AIA, LEED AP
Project Manager

Shanna Hanson, NCIDQ
Interior Designer

MECHANICAL ENGINEERS Mechanical/Electrical/Plumbing

Brian Hessinger, PE, LEED AP
Mechanical Engineer

David Green, PE
Electrical Engineer

Phil Rohm, Sr
Sr. Plumbing Engineer

STRUCTURAL ONE Structural Engineering

Dan Engebretson, PE
Project Manager
Structural Engineer

TECHNOLOGY RESEARCH & CONSULTING Technology and Low-Voltage

Larry J. Trobough, RCDD
Technology Manager

GRIFFEY ENGINEERING Civil Engineering & Surveying

Donald A. Griffey, PE
Project Manager

George S. Horton, PE
Civil Engineering



**Baker
Barrios**

Experience:

Fire Stations




Baker
Barrios

Experience: **fire stations**

Cobb County Fire Station 5

- Two Story Prototype
- 9,600 SF
- \$2.4 million total construction cost

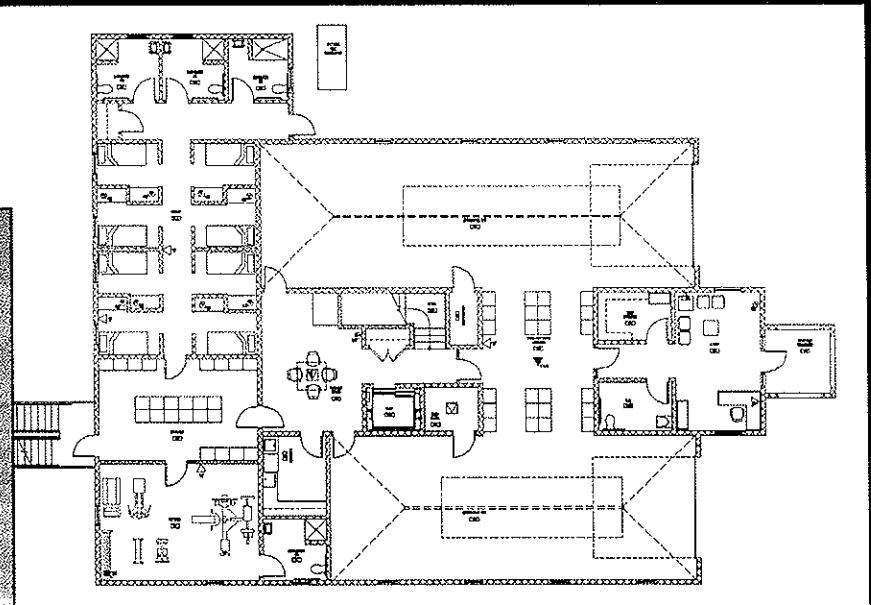

"Your firm has provided extraordinary architecture and interior design services for the Cobb County Fire Station 5 project. We have thoroughly enjoyed the collaborative design process and the degree of personal attention and service we have received from your firm."

Allen Kronenberger
Property Manager
Cobb County Property Management




Baker
Barrios

Experienced fire stations

Jacksonville Beach Fire Station 2

- One Story Fire Station
- 5,540 SF
- \$701,874 total construction cost

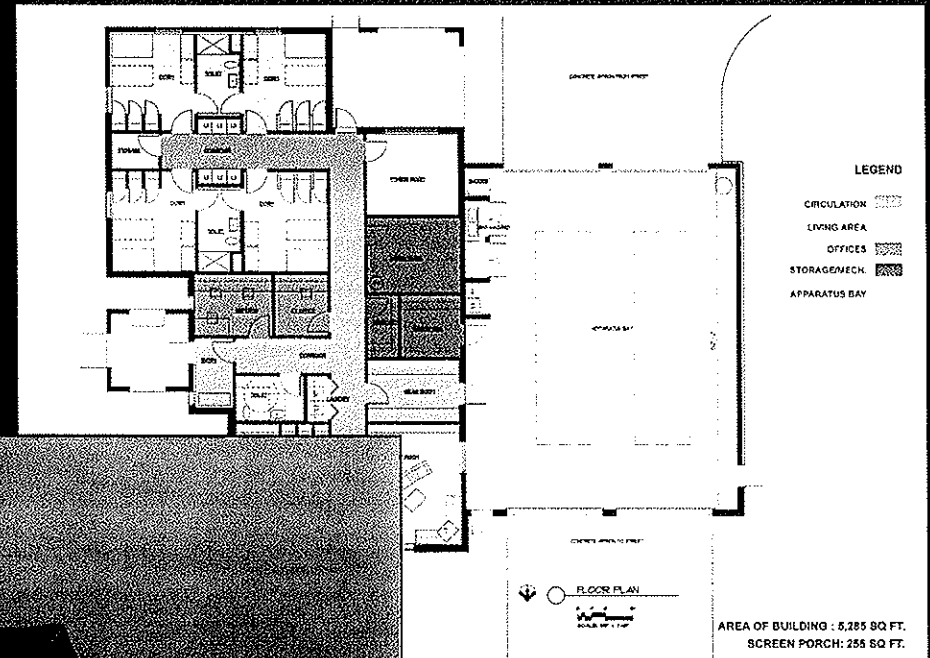



Baker
Barrios

ARCHITECTS

Experiences **fire stations**

Reedy Creek Fire Station 4 & Emergency Services

- One Story Fire Station
- 19,468 SF
- \$3.5 million total construction cost

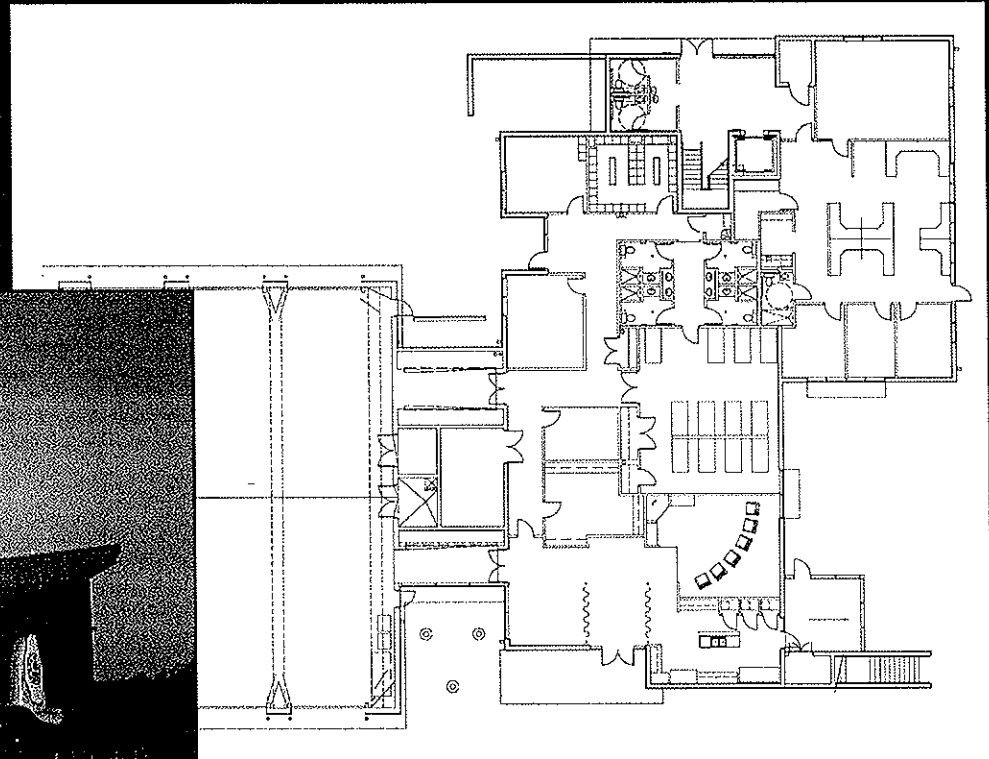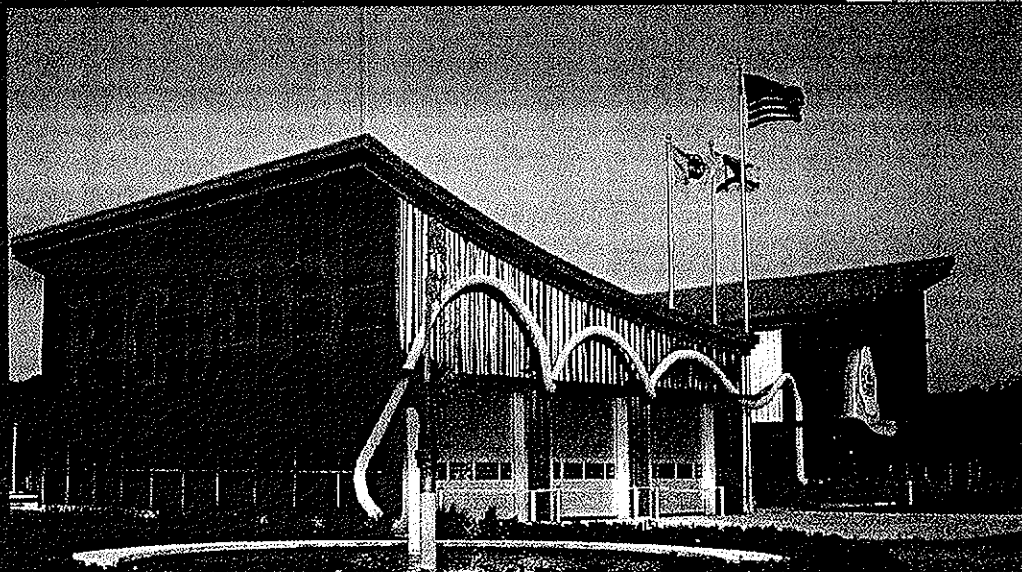

Baker
Barrios

fire stations

Orange County Fire Station 84

- Two Bay Covered Apparatus Structures





**Baker
Barrios**

Experience: **fire stations**

Reedy Creek Fire Station 2



- One Story Fire Station
- 10,000 SF
- \$1.04 million total construction cost

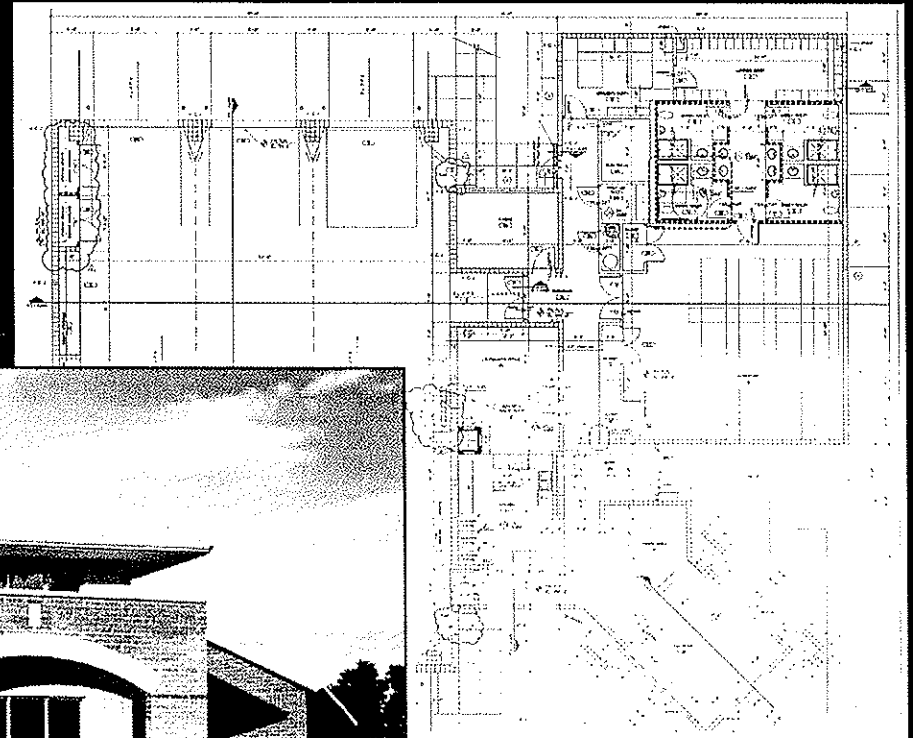

Baker
Barrios

Experienced fire stations

Prototype Studies

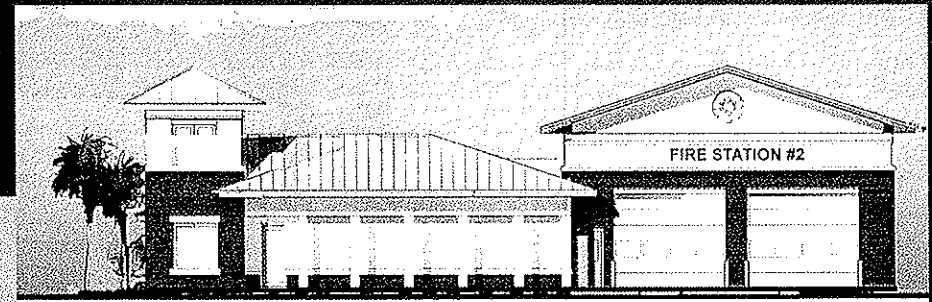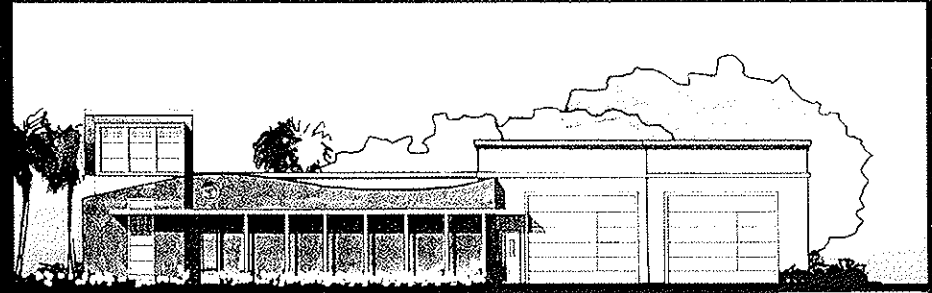


Baker
Barrios

ARCHITECT

Experiences: fire stations

Oviedo Fire Station 2

- One Story Fire Station
- 10,000 SF
- \$1.04 million total construction cost

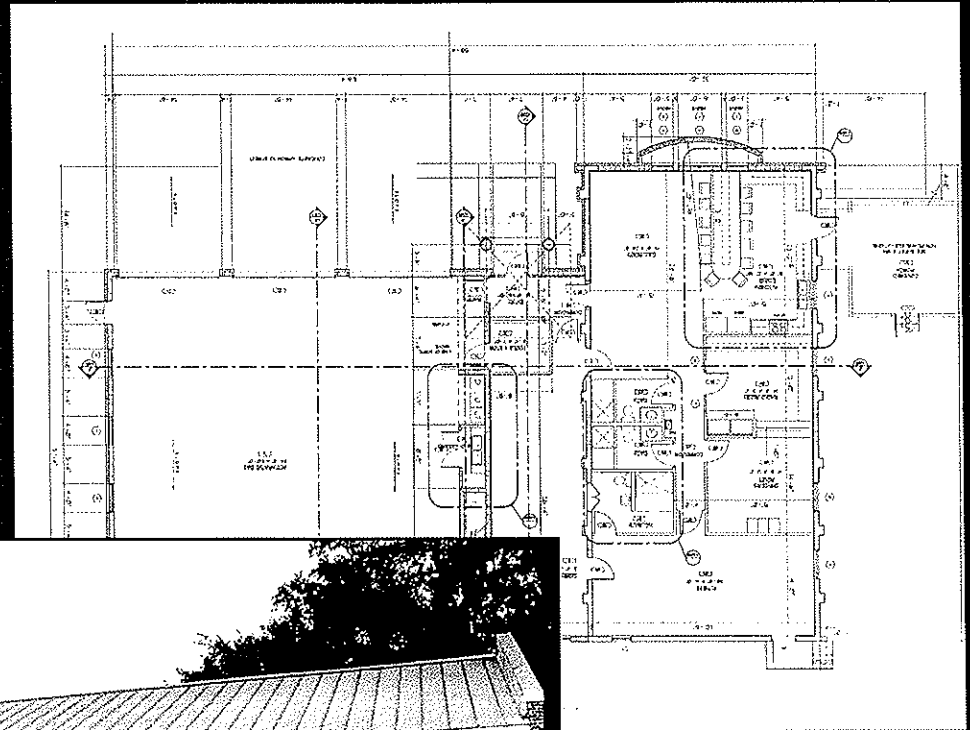

Baker
Barrios

Experience

Renovations






**Baker
Barrios**

Experience: **renovations**

Orange County Sheriff's Complex

- Two Story Emergency Operations / Sheriff's Complex
- 200,000 SF
- \$7.4 million total construction cost

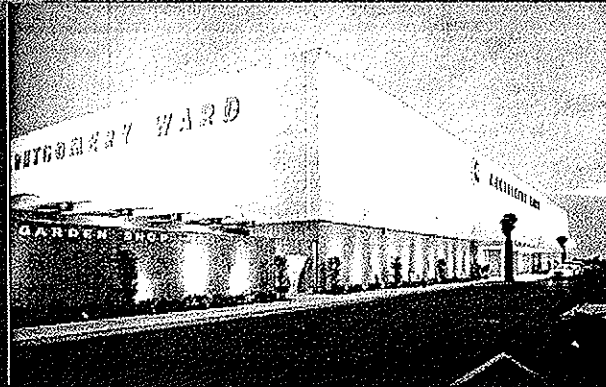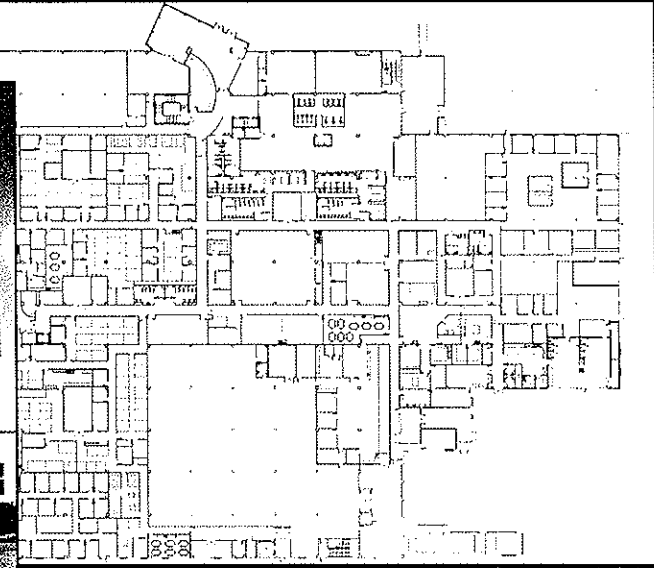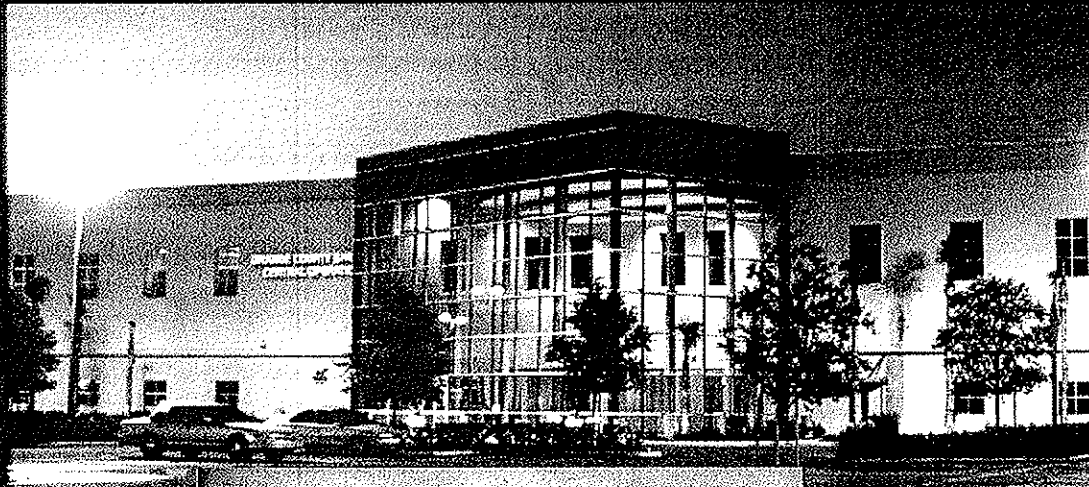

"During all three phases we have been able to rely on Baker Barrios Architects to develop solutions to our space problems and provide us with functional and attractive space to serve the needs of the Citizens and guests of Orange County."

Kevin Beary
Former Orange County Sheriff




Baker
Barrios

Experience renovations

250 Park Avenue

- Six Story Mixed Use Office Complex
- 120,000 SF
- \$6.5 million total construction cost

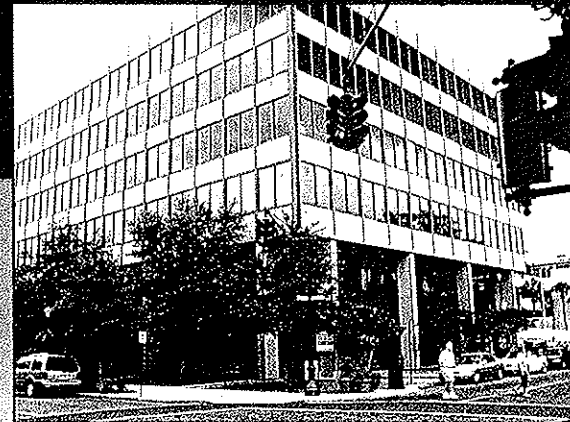

Excellence in Construction Award
Associated Builders Contractors

Judges Award
Southeast Construction Magazine



Baker
Barrios

Experience: **renovations**

Cornerstone Renovation

- Four Story Mixed Use Commercial
- 94,800 SF
- \$2.1 million total construction cost



**Baker
Barrios**

Workshops

A Collaborative Approach:

- Includes a Series of Workshops
- Interactive Sessions involving all stakeholders

Goals:

- Discuss – “What will Make These Projects A Success?”
- Confirm Program & Owner Requirements
- Discuss Existing Conditions & Utilities
- Review and Discuss Budget

Deliverables:

- Building Programs
- Site Plan & Analysis
- Design Documents
- Cost Estimates

TeamWorks

a collaborative design process

Conceptual Design

Workshop 1

Day 1
Day 2
Day 3




Workshop 2

Day 1
Day 2
Day 3



Workshop 3

Day 1
Day 2
Day 3



Workshop 4

Day 1
Day 2
Day 3



Workshop 5

Day 1
Day 2
Day 3



Production Begins

50% Deliverables

100% Deliverables



Schematic Design Design Development Construction Documents




Schedule / Process

Workshops

Schematic Workshop - Day One

8:00 am - 11:00 am

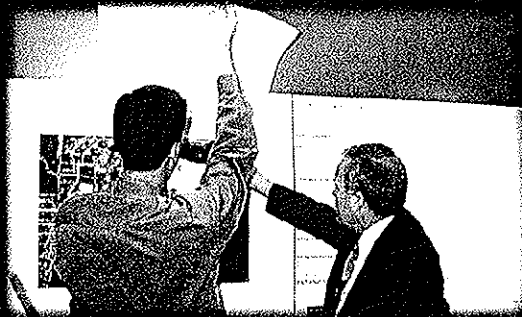

Project Kickoff!

- Identify keys to a successful project
- Review Program for all four facilities
- Prepare master list of program spaces for each fire station
- Confirm Schedule & Deliverables
- Review project budget

12:00 pm - 5:00 pm



Design Team Work Session

- Develop Concept Plans & Diagrams
- Summarize program information
- Prepare site analysis
- Develop Exterior Elevations



**Baker
Barrios**

Workshops

Schematic Workshop - Day Two

8:00 am - 10:00 am

What We've Learned!

- Review Site Analysis
- Review Program Information
- Review Initial Concept Plans
- Comparison of Program to Budget

10:00 am - 2:00 pm

Design Team Work Session

- Refine Program & Incorporate Comments
- Revise Concept Plans and Diagrams

2:00 pm - 5:00 pm

Building Committee Session

- Review Revised Concepts
- Finalize Program
- Confirm Direction




**Baker
Barrios**



- ## 6. Empowerment and accountability of Project Manager and each team member



Construction Administration

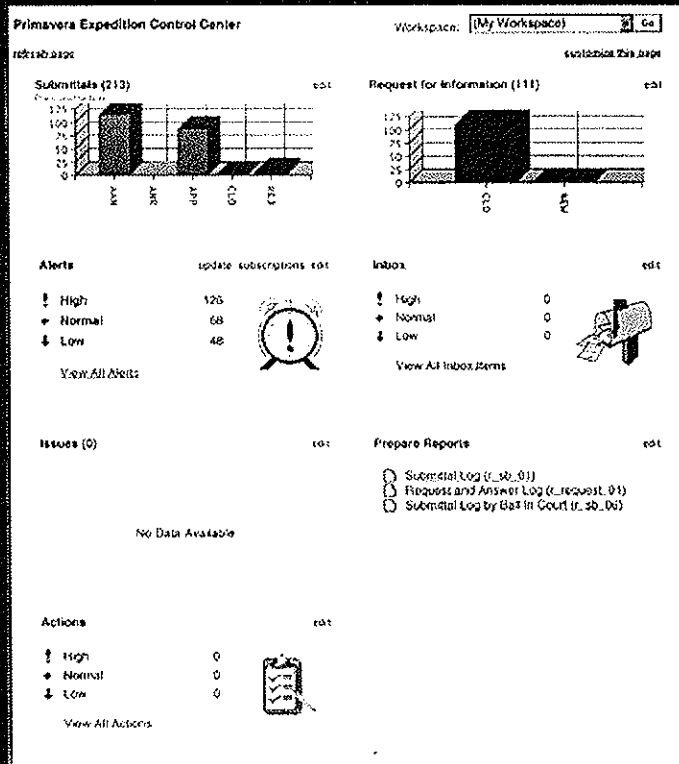



"Hands On" Approach

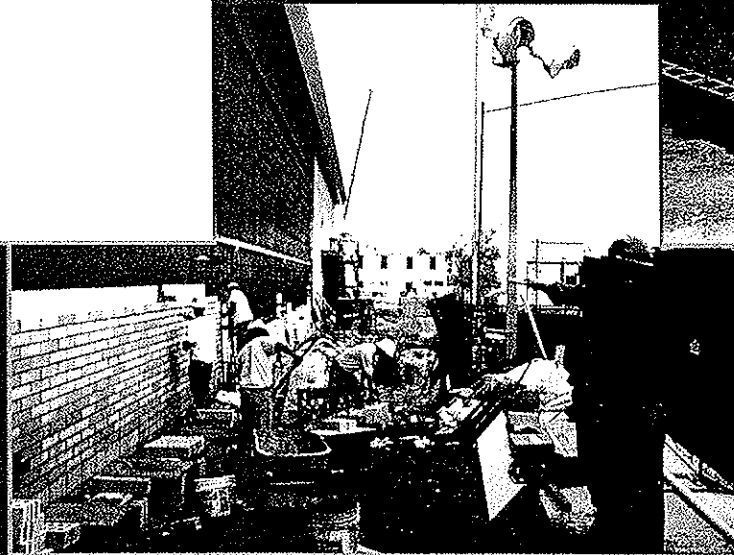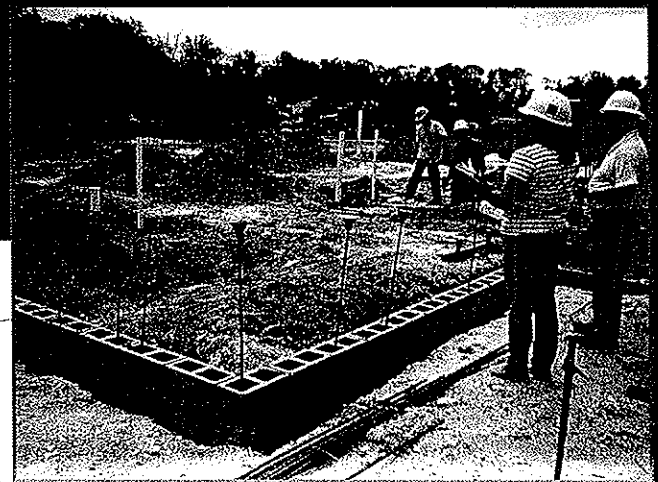

Baker
Barrios

Construction Administration

ProActive

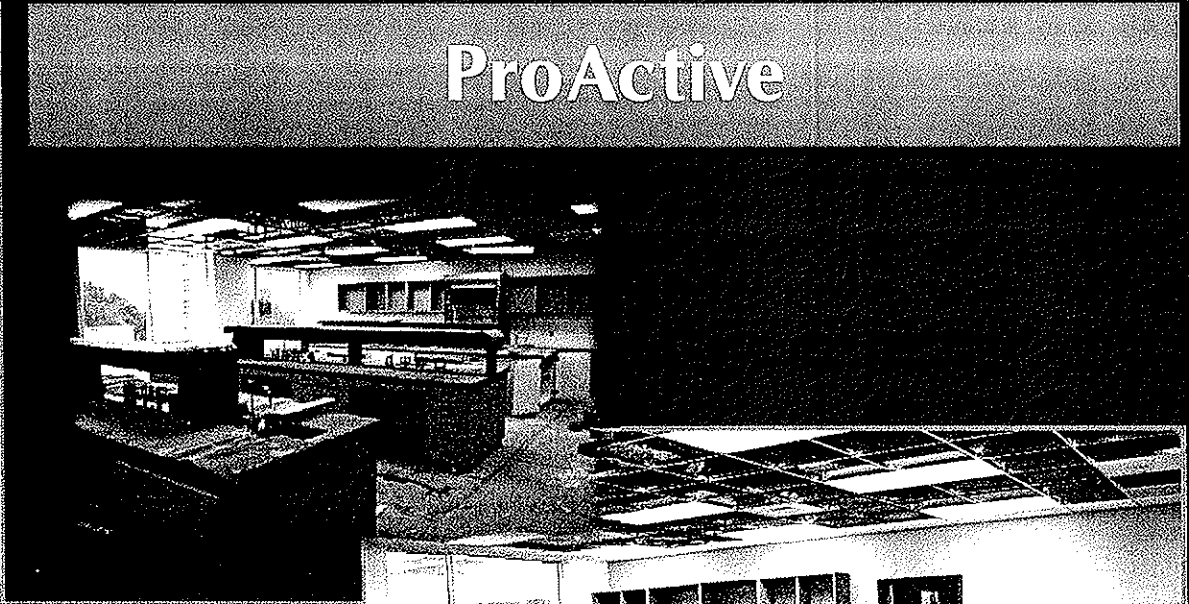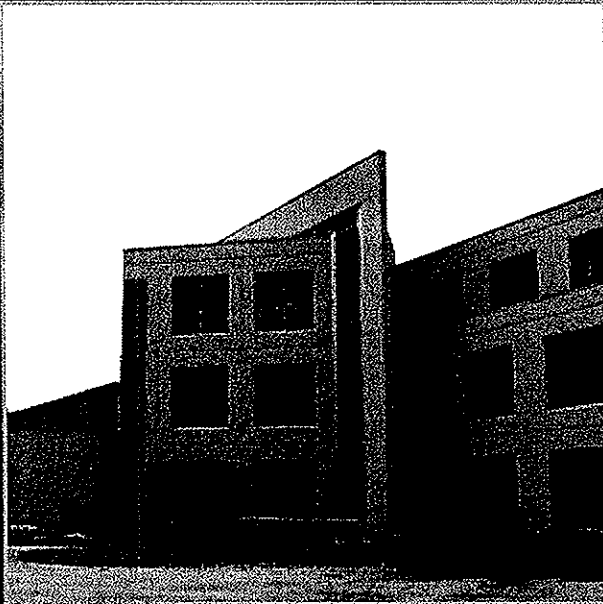

Baker
Barrios

Architect

Workshop 7: Cost Control

- Techniques Used During the Design Process
- Approach to Controlling the Project Budget
- Keeping Lines of Communication Open Regarding Budget

Item	Unit	Quantity	Unit Price	Total Price	Notes
CONSTRUCTION - BUILDING					
Site Preparation	sq ft	10,000	1.50	15,000	
Foundation	sq ft	10,000	2.00	20,000	
Framing	sq ft	10,000	3.00	30,000	
Roofing	sq ft	10,000	1.00	10,000	
Interior Finishes	sq ft	10,000	2.50	25,000	
Exterior Finishes	sq ft	10,000	1.50	15,000	
Landscaping	sq ft	10,000	1.00	10,000	
Total Construction				110,000	
CONSTRUCTION - PLUMBING					
Plumbing Fixtures	unit	10	1,000	10,000	
Plumbing Pipes	ft	100	100	10,000	
Plumbing Labor	hr	100	100	10,000	
Total Plumbing				30,000	
CONSTRUCTION - ELECTRICAL					
Electrical Panels	unit	10	1,000	10,000	
Electrical Wires	ft	100	100	10,000	
Electrical Labor	hr	100	100	10,000	
Total Electrical				30,000	
CONSTRUCTION - MECHANICAL					
HVAC Units	unit	10	1,000	10,000	
HVAC Ductwork	ft	100	100	10,000	
HVAC Labor	hr	100	100	10,000	
Total Mechanical				30,000	
CONSTRUCTION - TOTAL				200,000	
DESIGN - ARCHITECTURAL					
Architect Fees	hr	100	100	10,000	
Architect Labor	hr	100	100	10,000	
Total Architectural				20,000	
DESIGN - ENGINEERING					
Engineer Fees	hr	100	100	10,000	
Engineer Labor	hr	100	100	10,000	
Total Engineering				20,000	
DESIGN - TOTAL				40,000	
TOTAL PROJECT COST				240,000	

Conceptual Design Workshop 1 – Day 1

- Objectives for Charrette
- Identify Keys to Successful Project
- Prepare Master List of Program Spaces
- Interview User Groups
- Discussion About Master Plan Objectives
- Schedule
- Review Project Budget



Baker
Barrios

Conceptual
Workshop 1

Conceptual Design Workshop 1 – Day 2

Planning Committee for Building

- Review Site Analysis
- Review Program Information
- Review Functional Relationship Diagram

Planning Committee for Building

- Resolve List/Size of Building Program
- Comparison to Budget

Design Team Work Session

- Refine Program

Design Team Work Session

- Develop Master Plan Concept

Baker
Barrios

Budget / Cost Control

Baker Barrios Architects Budget Experience

Project Name	Project Budget	Project Size	Cost / SF
Jacksonville Beach Fire Station 4	\$701,874	5,540 SF	\$126.69/SF
Cobb County Fire Station 5	\$2,400,000	9,600 SF	\$250/SF
Reedy Creek Fire Station 4 & Emergency Services	\$3,500,000	19,468 SF	\$179.78/SF
Oviedo Fire Station 2	\$1,004,000	10,000 SF	\$100.40/SF

Sumter County Fire and Rescue Stations

Project Name	Project Budget	Project Size	Cost / SF
#22 at West Bushnell	\$1,135,000	6,500 SF	\$174.61/SF
#33 at Coleman	\$1,135,000	6,500 SF	\$174.61/SF
#31 at Wildwood	\$332,000	5,850 SF	\$56.75/SF
#32 at Oxford	\$352,000	5,355 SF*	\$65.73/SF



**Baker
Barrios**

Design Guidelines for Success



ORANGE COUNTY
FIRE / RESCUE DIVISION

Design / Build Criteria
PROTOTYPE FIRE STATION



Baker
Barrios


Case Study

Jacksonville Beach Fire Station 2



Baker
Barrios

Jacksonville Beach Fire Station 2

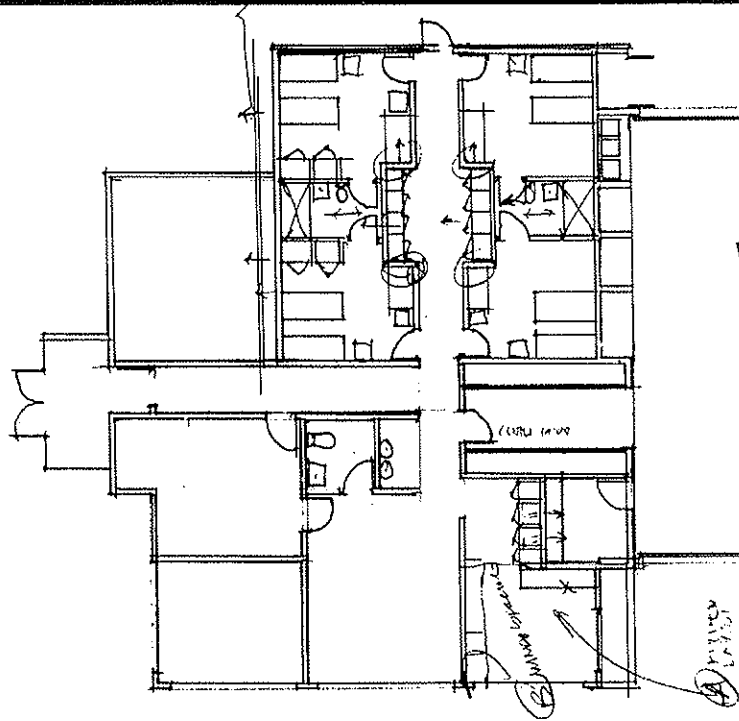

- 4 - AVOID DUAL FUNCTION SPACES.
- 5 - INDOOR AIR QUALITY - MOISTURE IN BUNK ROOM; LACK OF EXHAUST FANS.
- 6 - SATISFACTION -
- 7 - CONSERVE LAND
- 8 - STAY IN BUDGET
- 9 - HURR. RESISTANT
- 10 - CONCERN W/O
- 11 - SHOWER - ADA
- 12 - PUBLIC ADA
- 13 - ADA SHOWER
- 14 - ELEC PANEL -
- 15 - CHECKED & M. MANU
- 16 - CP & M. MANU
- 17 - NO FOUNT

AGENDA

1. INTRODUCTION
2. OBJECTIVES
3. KEY ISSUES
4. REVIEW
5. REVIEW FUNCTIONAL
6. SECURITY
7. INDIVIDUAL SPACE REQ.
8. LEVEL OF MAT. & FINISHES
9. SITE/PARKING
10. CHARACTER & STYLE
11. BUDGET
12. SCHEDULE

SUCCESS


1. EASY PERMITTING...
 - UPFRONT MTGS
 - TARGET 3-5 DAYS PERMITTING
 - COORDINATION OF DECS.
- 2.-MIX OCC.- CHALLENGE
 - SPRINKLED; MONITORED; FIRE ALARM.
- 3.-LOW MAINT.
 - PAINT; LEAKY WINDOWS; BUR.
- 4.- CERAMIC TILE..
4. USER FRIENDLY
 - ADIM; CLERICAL; BLOOD PRESS.
 - FENCE?
 - DOCK STYLE DORMS.
 - ALL ELEC. ; COMM. HOOD



Baker
Barrios


Case Study:

Jacksonville Beach Fire Station 2

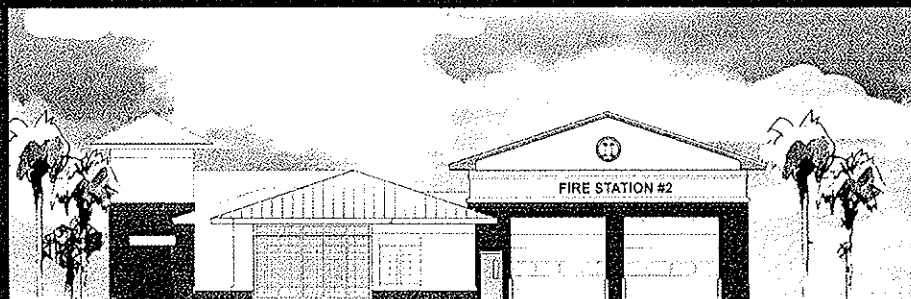

Baker
Barrios

Jacksonville Beach Fire Station 2

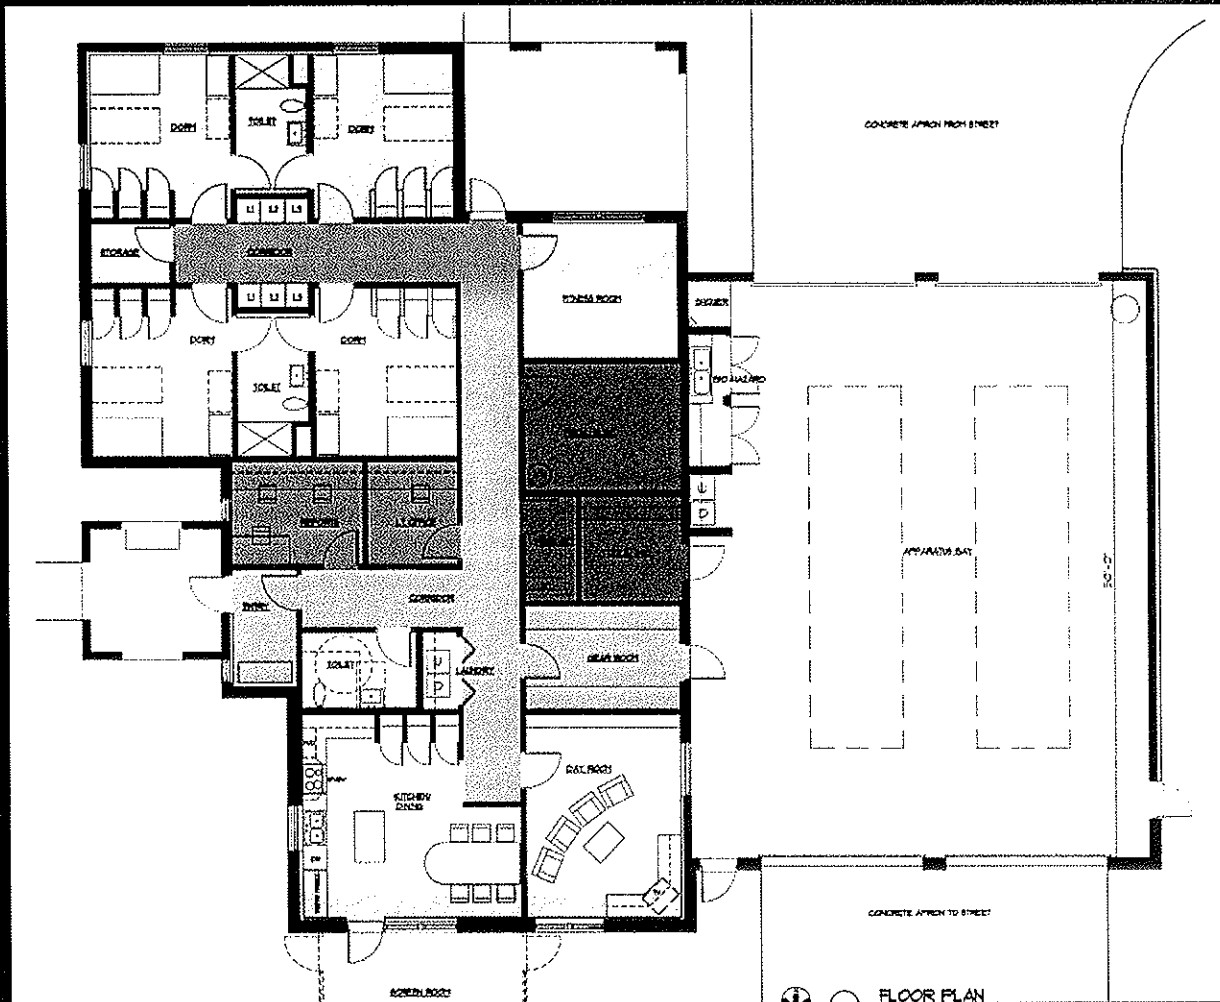

Baker
Barrios

Concluding Remarks

"Team is Ready to Go!"

"Budget Oriented"

"Client First" Approach

"Can Do" Attitude

"Our Business is Service"



**Baker
Barrios**



Architects

ARCHITECTURE
INTERIOR DESIGN

ORLANDO

189 S. Orange Avenue
Suite 1700
Orlando, FL 32801
Tel: 407.926.3000
Fax: 407.926.3390
AA0002981

SPECIALIZED MARKETS

Commercial
Corporate
Education
Entertainment
Health Care
Hospitality
Industrial
Mixed-use
Retail

WEB SITE

www.bakerbarrios.com

ORLANDO

TAMPA

ATLANTA

Table of Contents

A. Statement of Interest

Letter of Interest
RFQ Cover Page
Proposal Form
Vendor's Certification
Statement of Terms and Conditions
Drug Free Workplace Certification Form
Conflict of Interest Disclosure Form

B. Firm Profile: Form 1

State of Florida Professional Regulation License
State of Florida Corporate Charter
Insurance Certificates

C. Team Composition: Form 2

D. Lists of Outside Key Consultants/Associates: Form 3

E. Location: Form 4

F. Illustrative Work: Form 5

G. Volume of Work: Form 6

H. Additional Information: Form 7

Tab A



Architects

October 5, 2009

ARCHITECTURE
INTERIOR DESIGN

ORLANDO

189 S. Orange Avenue
Suite 1700
Orlando, FL 32801
Tel: 407.926.3000
Fax: 407.926.3390
AA0002981

SPECIALIZED MARKETS

Commercial
Corporate
Education
Entertainment
Health Care
Hospitality
Industrial
Mixed-use
Retail

WEB SITE

www.bakerbarrios.com

O R L A N D O

T A M P A

A T L A N T A

Ms. Amanda Taylor
Budget & Purchasing Department
Board of Sumter County Commissioners
910 North Main Street
Bushnell, Florida 33513

Re: A/E Design Services for Sumter County Fire and Rescue
Stations, RFQ 138-0-2009/AT

Dear Ms. Taylor and Selection Committee Members:

Baker Barrios Architects, Inc. is very pleased to submit our qualifications for design services for the Sumter County Fire and Rescue Stations.

Project Understanding... Our team understands that the Sumter County fire stations - #31 at Wildwood, #32 at Oxford, #33 at Coleman and #22 at West Bushnell – each have unique needs and requirements to fulfill. The Wildwood and Oxford stations are in need of renovation and expansion and the Coleman and West Bushnell fire stations will be new construction. With this economy we know how important it is for your project to come in below the budgeted amount. The design team will manage and design the fire stations with **utmost regard to cost, schedule and quality control**. Our firm and technical staff are **stringent in our compliance of current local, state, and federal codes, ADA and life safety issues**. Also, we are **intimately familiar with the general contractor method**.

Our unique design services for the Fire Services Department include:

- Efficient, safe circulation
- Compliance to Budget and Schedule
- Design for staff and operational efficiency
- Durable, economical and attractive materials
- 70% of our practice involves addition and renovation/ remodeling
- Fresh creative thinking and award winning solutions

Project Experience... Baker Barrios Architects, Inc. has a proven track record designing state-of-the-art facilities equipped to handle emergencies and to address challenges and opportunities of the future. Baker Barrios Architects and our sub-consultants bring to this project a breadth of current and recent similar experience in the planning and design of Fire Stations and Prototype Designs. We enjoyed a successful working relationship with the City of Oviedo on Fire Station No. 2, which was the result of the conversion and renovation of a Historic building into a 10,000 SF Fire Station with three drive-thru bays. Also, we completed a design / build project for the City of Jacksonville. The new 24 hour Fire Station house is equipped to handle all emergencies and is designed as living quarters with a kitchen, dining room, dorms, offices and a fitness room.

Ms. Amanda Taylor
Board of Sumter County Commissioners
Re: RFQ 138-0-2009/AT
October 5, 2009
Page 2 of 2

Additional relevant experience includes: Cobb County Fire Station No. 5 with Ingenuity Engineers as the MEP firm on the team; Fire Station No. 2 for the Reedy Creek Improvement District; Fire Station Prototype for Orange County that involved preparing Design and Specification Criteria as a basis of design and planning of all future Fire Stations for Orange County. Our renovation and conversions of fire stations include the re-skinning of Orange County Fire Station #71 that upgraded a 30-year old metal structure.

Baker Barrios Architects, Inc. will meet Sumter County Government's objectives and expectations in the design and construction of the four fire stations. Baker Barrios Architects has comprised a solid team of consultants that have been selected for their work on similar projects. Our workload is such that we can hit the ground running upon your notice to proceed. BBA's collaborative approach to design and delivery has been proven to maximize design quality, meet budget and schedule mandates.

Baker Barrios Architects, Inc. is a service and client oriented firm. In consort with our corporate philosophy, "**Our Business is Service,**" we believe a successful project is one that meets the client's goals and expectations, is functionally and economically efficient, instills pride and adds value to those who own, occupy and visit. I believe you will find us to be team players, responsive, creative and committed to quality.

Sincerely,


Baker Barrios Architects, Inc.

Mike Houseman, AIA, LEED AP
Principal

Enclosed

RFQ COVER PAGE

Name of Firm, Entity or Organization: Baker Barrios Architects, Inc.Federal Employer Identification Number (FEIN): **59-3444163**State of Florida License Number (If Applicable): **AA0002981**Name of Contact Person: **Mike Houseman, AIA, LEED AP**Title: **Principal**E-Mail Address: mhouseman@bakerbarrios.comMailing Address: **189 S. Orange Avenue, Suite 1700**

Street Address (if different):

City, State, Zip: **Orlando, FL 32801**Telephone: **407.926.3000**Fax: **407.926.3390**

Organizational Structure – Please Check One:

Corporation ☒ Partnership ☐ Proprietorship ☐ Joint Venture ☐ Other ☐


If Corporation:

Date of Incorporation: **5/5/1997**State of Incorporation: **Florida**

States Registered in as Foreign Corporation:

Authorized Signature:**Print Name:** Mike Houseman, AIA, LEED AP**Signature:** **Title:** Principal**Phone:** 407.926.3000*This document must be completed and returned with your Submittal.*

**PROPOSAL FORM FOR
BOARD OF SUMTER COUNTY COMMISSIONERS**




Name of Firm Submitting Qualifications Baker Barrios Architects, Inc.

Name of Person Submitting Qualifications Mike Houseman, AIA, LEED AP

PROPOSER ACKNOWLEDGMENT

"The undersigned hereby declares that he/she has informed himself/herself fully in regard to all conditions to the work to be done, and that he/she has examined the RFQ and Specifications for the work and comments hereto attached. The Vendor proposes and agrees, if this submission is accepted, to contract with the Board of Sumter County Commissioners, to furnish all necessary materials, equipment, labor and services necessary to complete the work covered by the RFQ and Contract Documents for this Project. The Vendor agrees to accept in full compensation for each item the prices named in the schedules incorporated herein."

CONSULTANT'S FEE SCHEDULE MUST BE ATTACHED TO THIS PROPOSAL FORM




Signature


10.01.09
Date

[☐] Check if exception(s) or deviation(s) to Specifications. Attach separate sheet(s) detailing reason and type for the exception or deviation.

This document must be completed and returned with your Submittal

VENDOR'S CERTIFICATION

Submit To: Sumter County Board of County Commissioners 910 North Main Street Bushnell, Florida, 33513 Phone 352-793-0200 Fax 352-793.0207		SUMTER COUNTY BOARD OF COUNTY COMMISSIONERS REQUEST FOR QUALIFICATIONS (RFQ) CERTIFICATION AND ADDENDA ACKNOWLEDGMENT	
DUE DATE: October 5, 2009		DUE TIME: 10:00am	
RFQ 138-0-2009/AT			
TITLE: INFORMATION TECHNOLOGY CONSULTANT			
VENDOR NAME: Baker Barrios Architects, Inc.		PHONE NUMBER: 407.926.3000	
VENDOR MAILING ADDRESS: 189 S. Orange Avenue, Suite 1700		FAX NUMBER: 407.926.3390	
CITY/STATE/ZIP: Orlando, FL 32801		E-MAIL ADDRESS: mhouseman@bakerbarrios.com	
<p>"I, the undersigned, certify that I have reviewed the addenda listed below (list all addenda received to date). I understand that timely commencement will be considered in award of this RFQ and that cancellation of award will be considered if commencement time is not met, and that untimely commencement may be cause for assessment of liquidated damages claims. I further certify that the services will meet or exceed the RFQ requirements. I, the undersigned, declare that I have carefully examined the RFQ, specifications, terms and conditions as applicable for this Request, and that I am thoroughly familiar with all provisions and the quality and type of coverage and services specified. I further declare that I have not divulged, discussed, or compared this RFQ with any other Offeror and have not colluded with any Offerors or parties to an RFQ whatsoever for any fraudulent purpose."</p>			
<u>1</u> Addendum #	<u>2</u> Addendum #	<u>3</u> Addendum #	<u>4</u> Addendum #
			<u>5</u> Addendum #
<p>"I certify that this quote is made without prior understanding, agreement, or connection with any corporation, firm, or person submitting an RFQ for the same material, supplies, equipment or services and is in all respects fair and without collusion or fraud. I agree to abide by all conditions of this RFQ and certify that I am authorized to sign this response and that the offer is in compliance with all requirements of the RFQ, including but not limited to certification requirements. In conducting offers with the Sumter County Board of County Commissioners, respondent agrees that if this proposal is accepted, the respondent will convey, sell, assign, or transfer to the County all rights, title and interest in and to all causes of action it may now or hereafter acquire under the anti-trust laws of the United States for price fixing relating to the particular commodities or services purchased or acquired by the County. At the County's discretion, such assignment shall be made and become effective at the time the purchasing agency renders final payment to the respondent."</p>			
<u>Mike Houseman, AIA, LEED AP</u> Authorized Agent Name, Title (Print)		 Authorized Signature	
		<u>October 1, 2009</u> Date	
<i>This form must be completed and returned with your Submittal</i>			



BOARD OF SUMTER COUNTY COMMISSIONERS
910 NORTH MAIN STREET
BUSHNELL, FLORIDA 33513
PHONE: (352) 793-0200 * FAX: (352) 793-0207
E-mail: amanda.taylor@sumtercountyfl.gov

Addendum #1 RSQ 138-0-2009/AT for Sumter County Architectural / Engineering Design Services for Fire and Rescue Stations Renovation of #32 at Oxford, FL and #31 at Wildwood, FL; New Construction Prototype Fire Station at #22 West Bushnell, FL and #33 at Coleman, FL.


- A. Notice to Contractors: Whenever a conflict appears between this addendum and the initial solicitation, or plans, this addendum shall prevail, and as such shall constitute a binding portion of the contract documents. All provisions of the original specifications shall remain in force, except as specifically modified or changed herein.
- B. Additions, Deletions, and/or Clarifications: This addendum forms a part of the Contract Documents and modified the original Quote Documents as noted below and supersedes all contrary information and requirements. Contractors shall acknowledge receipt of this Addendum.

Clarification 1: Times and locations were not included on Page 2 on the Calendar of Events / RFQ Timeline please see below for clarification:

Clarification 2: Non-Mandatory Pre Bid Meeting on Wednesday, September 9, 2009 @ 9:00am will be held in Room 142.

Proposals will be opened Monday, October 5, 2009 @ 10:05am in Room 142.

Selection Review Committee Meeting on Tuesday, October 13, 2009 will be at 1:00pm in Room 142.




BOARD OF SUMTER COUNTY COMMISSIONERS
910 NORTH MAIN STREET
BUSHNELL, FLORIDA 33513
PHONE: (352) 793-0200 * FAX: (352) 793-0207
E-mail: amanda.taylor@sumtercountyfl.gov

Addendum #2 RSQ 138-0-2009/AT for Sumter County Architectural / Engineering Design Services for Fire and Rescue Stations Renovation of #32 at Oxford, FL and #31 at Wildwood, FL; New Construction Prototype Fire Station at #22 West Bushnell, FL and #33 at Coleman, FL.

- A. Notice to Contractors: Whenever a conflict appears between this addendum and the initial solicitation, or plans, this addendum shall prevail, and as such shall constitute a binding portion of the contract documents. All provisions of the original specifications shall remain in force, except as specifically modified or changed herein.
- B. Additions, Deletions, and/or Clarifications: This addendum forms a part of the Contract Documents and modified the original Quote Documents as noted below and supersedes all contrary information and requirements. Contractors shall acknowledge receipt of this Addendum.

Clarification 1: Correction to room location for the Selection Review Committee Meeting on Tuesday, October 13, 2009 at 1:00pm

Clarification 2: The meeting has been moved from Room 142 to the Supervisor of Elections Conference Room.




BOARD OF SUMTER COUNTY COMMISSIONERS
910 NORTH MAIN STREET
BUSHNELL, FLORIDA 33513
PHONE: (352) 793-0200 * FAX: (352) 793-0207
E-mail: amanda.taylor@sumtercountyfl.gov

Addendum #3 RSQ 138-0-2009/AT for Sumter County Architectural / Engineering Design Services for Fire and Rescue Stations Renovation of #32 at Oxford, FL and #31 at Wildwood, FL; New Construction Prototype Fire Station at #22 West Bushnell, FL and #33 at Coleman, FL.

- A. Notice to Vendors: Whenever a conflict appears between this addendum and the initial solicitation, or plans, this addendum shall prevail, and as such shall constitute a binding portion of the contract documents. All provisions of the original specifications shall remain in force, except as specifically modified or changed herein.
- B. Additions, Deletions, and/or Clarifications: This addendum forms a part of the Contract Documents and modified the original Quote Documents as noted below and supersedes all contrary information and requirements. Contractors shall acknowledge receipt of this Addendum.

Clarification 1: Clarification of FS 287.055 in relation to Fee Structure from submitting firms.

Clarification 2: Sumter County will maintain there will not be a request for the Fee Structure until after the Selection Committee makes a recommendation to the BOCC once Contract Negotiations have begun.




BOARD OF SUMTER COUNTY COMMISSIONERS
910 NORTH MAIN STREET
BUSHNELL, FLORIDA 33513
PHONE: (352) 793-0200 * FAX: (352) 793-0207
E-mail: amanda.taylor@sumtercountyfl.gov

Addendum #4 RSQ 138-0-2009/AT for Sumter County Architectural / Engineering Design Services for Fire and Rescue Stations Renovation of #32 at Oxford, FL and #31 at Wildwood, FL; New Construction Prototype Fire Station at #22 West Bushnell, FL and #33 at Coleman, FL.

- A. Notice to Vendors: Whenever a conflict appears between this addendum and the initial solicitation, or plans, this addendum shall prevail, and as such shall constitute a binding portion of the contract documents. All provisions of the original specifications shall remain in force, except as specifically modified or changed herein.
- B. Additions, Deletions, and/or Clarifications: This addendum forms a part of the Contract Documents and modified the original Quote Documents as noted below and supersedes all contrary information and requirements. Contractors shall acknowledge receipt of this Addendum.

Clarification 1: Clarification of amount of proposals to be submitted and proposal packet requirements.

Clarification 2: A total of five (5) packets must be submitted, one (1) marked original and the other four (4) marked copy. Requirements are listed on Page 8-9 and again on Page 25 relating to forms that must be provided. All of the requirements listed in the bid will be taken into consideration when scoring is completed. It is up to the vendor to decide how much/little information is provided for each requested item.



BOARD OF SUMTER COUNTY COMMISSIONERS
910 NORTH MAIN STREET
BUSHNELL, FLORIDA 33513
PHONE: (352) 793-0200 * FAX: (352) 793-0207
E-mail: amanda.taylor@sumtercountyfl.gov

Addendum #5 RSQ 138-0-2009/AT for Sumter County Architectural / Engineering Design Services for Fire and Rescue Stations Renovation of #32 at Oxford, FL and #31 at Wildwood, FL; New Construction Prototype Fire Station at #22 West Bushnell, FL and #33 at Coleman, FL.

- A. Notice to Vendors: Whenever a conflict appears between this addendum and the initial solicitation, or plans, this addendum shall prevail, and as such shall constitute a binding portion of the contract documents. All provisions of the original specifications shall remain in force, except as specifically modified or changed herein.
- B. Additions, Deletions, and/or Clarifications: This addendum forms a part of the Contract Documents and modified the original Quote Documents as noted below and supersedes all contrary information and requirements. Contractors shall acknowledge receipt of this Addendum.

Clarification 1: Clarification on the "Delivery" Section of the Statement of Terms and Conditions page 38 of 41 in the proposal packet

Clarification 2: See attached corrected form that should be used stating that the FOB Destinations is Sumter County, Florida.

STATEMENT OF TERMS AND CONDITIONS

This document must be completed and returned with your Submittal

PUBLIC ENTITY CRIME: A person or affiliate who has been placed on the convicted vendor list following a conviction for a public entity crime may not submit a Proposal/Bid on a contract to provide any goods or services to a public entity, for the construction or repair of a public building, or public work, may not submit Proposals/Bids on leases of real property to a public entity, may not be awarded or perform work as a contractor, supplier, subcontractor, or consultant under a contract with any public entity, and may not transact business with any public entity in excess of the threshold amount provided in Section 287.017, for CATEGORY TWO for a period of 36 months from the date of being placed on the convicted vendor list.

INDEMNIFICATION: The Contractor agrees to indemnify and hold harmless Board of Sumter County Commissioners, and their elected officials, employees and volunteers from and against all claims, losses and expenses, including legal costs, arising out of or resulting from, the performance of this contract, provided that any such claims, damage, loss of expenses is attributed to bodily injury, sickness, disease, personal injury or death, or to injury to or destruction of tangible property including the loss or loss of use resulting there from and is caused in whole or in part by any negligent act or omission of the tenant.

PROHIBITION OF LOBBYING: During the black out period which is, the period between the time the submittals for Invitation to Bid or the Request for Proposal, or Qualifications, or Information, as applicable, are received at Contracts / Purchasing and the time the Board awards the contract, no proposer, no lobbyist, principal, or other person may lobby, on behalf of a competing party in a particular procurement matter, any member of the Board, or any Board employee other than the Budget & Purchasing Manager. Violation of this provision may result in disqualification of violating party. All questions regarding this Request for Proposal (RFP) or Invitation to Bid (BID) must be submitted in writing to the Board's Budget & Purchasing Manager.

ANTI TRUST LAWS: By submission of a signed RFP or BID, the successful Vendor acknowledges compliance with all antitrust laws of the United States and the State of Florida, in order to protect the public from restraint of trade, which illegally increases prices.

CONFLICT OF INTEREST: The award of the contract hereunder is subject to the provisions of Chapter 112 of the Florida Statutes. Vendors shall disclose the names of any Officer, Director, Partner, Associate, or Agent who is also an Officer, Appointee, or Employee of any of the Boards at the time of the RFP or BID, or at the time of occurrence of the Conflict of Interest thereafter.

INTERPRETATION, CLARIFICATIONS AND ADDENDA: No oral interpretations will be made to any vendor as to the meaning of the RFP/BID Contract Documents. Any inquiry or request for interpretation received by the Budget & Purchasing Manager before the date listed herein will be given consideration. All such changes or interpretations will be made in writing in the form of an addendum and, if issued, will be distributed at or after the Pre-Proposal/Pre-Bid Conference, mailed or sent by available or electronic means to all attending prospective Submitters prior to the established RFP/BID opening date. Each Vendor shall acknowledge receipt of such addenda in the space provided. In case any Proposer/Bidder fails to acknowledge receipt of such addenda or addendum, his offer will nevertheless be construed as though it had been received and acknowledged and the submission of his bid will constitute acknowledgment of the receipt of same. All addenda are a part of the RFP/BID FORMS and each Proposer/Bidder will be bound by such addenda, whether or not received by him. It is the responsibility of each Proposer/Bidder to verify that he has received all addenda issued before RFP's/BID's are opened. In the case of unit price items, the quantities of work to be done and materials to be furnished under this RFP/BID Contract are to be considered as approximate only and are to be used solely for the comparison of RFP's/BID's received. The Board and/or his CONSULTANT do not expressly or by implication represent that the actual quantities involved will correspond exactly therewith; nor shall the Vendor plead misunderstanding or deception because of such estimates or quantities of work performed or material furnished in accordance with the Specifications and/or Drawings and other Proposal/Bid Documents, and it is understood that the quantities may be increased or diminished as provided herein without in any way invalidating any of the unit or lump sum prices bid.

GOVERNING LAWS AND REGULATIONS: The vendor is required to be familiar with and shall be responsible for complying with all federal, state and local laws, ordinances, rules and regulations that in any manner affect the work.

PROPRIETARY/CONFIDENTIAL INFORMATION: Vendors are hereby notified that all information submitted as part of, or in support of RFP's/BID's, will be available for public inspection ten days after opening of the RFP's/BID's or until a short list is recommended whichever comes first. In compliance with Chapter 119, and 287 of the Florida Statutes. Any person wishing to view the RFP's/BID's must make an appointment by calling the Budget & Purchasing Manager at (352) 793-0200. All RFP's/BID's submitted in response to this solicitation become the property of the Board. Unless information submitted is proprietary, copy written, trademarked, or patented, the Board reserves the right to utilize any or all information, ideas, conceptions, or portions of any RFP/BID, in its best interest.

TAXES: The Board of Sumter County Commissioners is exempt from any taxes imposed by the State and/or Federal Government. Exemption certificates will be provided upon request.

NON-COLLUSION DECLARATION: By signing this RFP/BID, all Vendors shall affirm that they shall not collude, conspire, connive or agree, directly or indirectly, with any other Proposer, firm, or person to submit a collusive or sham Proposal in connection with the work for which their RFP/BID has been submitted; or to refrain from bidding in connection with such work; or have in any manner, directly or indirectly, sought by person to fix the price or prices in the RFP/BID or of any other Bidder, or to fix any overhead, profit, or cost elements of the RFP/BID price or the RFP/BID price of any other Bidder, or to secure through any collusion, conspiracy, connivance, or unlawful agreement any advantage against any other Bidder, or any person interested in the proposed work.

PROPOSER RESPONSIBILITY: Invitation by the Boards to vendors is based on the recipient's specific request and application to DemandStar by Onvia at www.DemandStar.com [(800) 711-1712] or as the result of response by the public to the legal advertisements required by State law. Firms or individuals submit their responses on a voluntary basis, and therefore are not entitled to compensation of any kind.

OWNERSHIP OF SUBMITTALS: All responses, inquiries or correspondence relating to or in reference to this RFP/BID, and all other reports, charts, displays, schedules, exhibits and other documentation submitted by the vendors will become the property of the Board. Reference to literature submitted with a previous RFP/BID will not relieve the Bidder from including any required documents with this RFP/BID.

EXAMINATION OF BID DOCUMENTS: Each Bidder shall carefully examine the RFP/BID Document to ensure all pages have been received, all drawings and/or Specifications and other applicable documents are included, and shall inform himself thoroughly regarding any and all conditions and requirements that may in any manner affect cost, progress or performance of the work to be performed under the Contract. Ignorance on the part of the CONTRACTOR will in no way relieve him of the obligations and responsibilities assumed under the Contract.

VENDOR RESPONSIBILITY: Vendors are fully and completely responsible for the labeling, identification and delivery of their submittals. The Budget & Purchasing Manager will not be responsible for any mislabeled or misdirected submissions nor those handled by delivery persons, couriers, or the US Postal Service.

DRUG FREE WORKPLACE: All Proposers/Bidders shall submit the enclosed, duly signed and notarized form entitled "Drug Free Workplace Certificate". The Drug Free Workplace Vendor shall have the burden of demonstrating that his program complies with Section 287.067 of the Florida Statutes, and any other applicable state law.

BOARD OF SUMTER COUNTY COMMISSIONERS, are political subdivisions of the State of Florida, and reserve the right to reject any and/or all submittals, reserve the right to waive any informalities or irregularities in the examination process, and reserve the right to award contracts and/or in the best interest of the Boards. Submittals not meeting stated minimum terms and qualifications may be rejected by the Boards as non-responsive. The Boards reserve the right to reject any or all submittals without cause. The Boards reserves the right to reject the submission of any Vendor in arrears or in default upon any debt or contract to the Boards, or who has failed to perform faithfully any previous contract with the Boards or with other governmental agencies.

PUBLIC RECORDS LAW: Correspondence, materials and documents received pursuant to this RFP/BID become public records subject to the provisions of Chapter 119, Florida Statutes.

VERIFICATION OF TIME: Next time is hereby established as the Official Time of the Boards.

PREPARATION OF PROPOSALS/BIDS:

Signature of the Bidder: The Bidder must sign the RFP/BID FORMS in the space provided for the signature. If the Proposer/Bidder is an individual, the words "doing business as _____" must appear beneath such signature. In the case of a partnership, the signature of at least one of the partners must follow the firm name and the words "Member of the Firm" should be written beneath such signature. If the Proposer/Bidder is a corporation, the title of the officer signing the RFP/BID on behalf of the corporation must be stated and evidence of his authority to sign the RFP/BID must be submitted. The Proposer/Bidder shall state in the RFP/BID FORMS the name and address of each person interested therein.

Basis for Bidding: The price proposed for each item shall be on a lump sum or unit price basis according to specifications on the RFP/BID FORM. The proposed prices shall remain unchanged for the duration of the Contract and no claims for cost escalation during the progress of the work will be considered, unless otherwise provided herein.

Total Proposed Price/Total Contract Sum Proposed: If applicable, the total price bid for the work shall be the aggregate of the lump sum prices proposed and/or unit prices multiplied by the appropriate estimated quantities for the individual items and shall be stated in figures in the appropriate place on the RFP/BID FORM. In the event that there is a discrepancy on the RFP/BID FORM due to unit price extensions or additions, the corrected extensions and additions shall be used to determine the project bid amount.

TABULATION: Those wishing to receive an official tabulation of the results of the opening of this RFP/BID are to submit a self-addressed, stamped business size (No. 10) envelope, prominently marked on the front lower left side, with the RFP identification. Tabulation requested by telephone, fax or electronic media will not be accepted.

OBLIGATION OF WINNING BIDDER: The contents of the RFP/BID of the successful proposer/bidder will become contractual obligations if acquisition action ensues. Failure of the successful Proposer/Bidder to accept these obligations in a contract may result in cancellation of the award and such vendor may be removed from future participation.

AWARD OF BID: It is the Boards' intent to select a vendor within sixty (60) calendar days of the deadline for receipt of Proposals/Bids. However, Proposals/Bids must be firm and valid for award for at least thirty (30) calendar days after the deadline for receipt of the RFP/BID.

ADDITIONAL REQUIREMENTS: The firms shall furnish such additional information as the Boards may reasonably require. This includes information which indicates financial resources as well as ability to provide the services. The Boards reserve the right to make investigations of the qualifications of the firm as it deems appropriate.

PREPARATION COSTS: The Boards shall not be obligated or be liable for any costs incurred by Proposers/Bidders prior to issuance of a contract. All costs to prepare and submit a response to this RFP/BID shall be borne by the Proposer/Bidder.

TIMELINESS: All work will commence upon authorization from the Boards' representative (Budget & Purchasing Manager). All work will proceed in a timely manner without delays. The Contractor shall commence the work UPON RECEIPT OF NOTICE TO PROCEED and/or ORDER PLACED (PURCHASE ORDER PRESENTED), and shall deliver in accordance to the terms and conditions outlined and agreed upon herein.

DELIVERY: All prices shall be FOB Destination, Sumter County, Florida, inside delivery unless otherwise specified.

ADDITIONAL SERVICES/PURCHASES BY OTHER PUBLIC AGENCIES ("PIGGY-BACK"): The Vendor by submitting a Bid acknowledges that other Public Agencies may seek to "Piggy-Back" under the same terms and conditions, during the effective period of any resulting contract - services and/or purchases being offered in this Bid, for the same prices and/or terms proposed. Vendor has the option to agree or disagree to allow contract Piggy-Back on a case-by-case basis. Before a Public Agency is allowed to Piggy-Back any contract, the Agency must first obtain the vendor's approval - without the vendor's approval, the seeking Agency cannot Piggy-Back.

PLANS, FORMS & SPECIFICATIONS: Bid Packages are available from the Budget & Purchasing Manager. These packages are available for pickup or by mail. If requested to mail, the Proposer/Bidder must supply a courier account number (UPS, FedEx, etc). Proposers/Bidders are required to use the official RFP/BID FORMS, and all attachments itemized herein, are to be submitted as a single document. Any variation from the minimum specifications must be clearly stated on the RFP/BID FORM and/or Exceptions/Deviations Sheet(s). Only one set of plans, forms, and specifications will be furnished each company or corporation interested in submitting a proposal/bid. RFP/BID FORM documents for this project are free of charge and are available on-line and are downloadable (vendor must pay any DemandStar fees or any shipping).


MANUFACTURER'S NAME AND APPROVED EQUIVALENTS: Any manufacturer's names, trade names, brand names, information and/or catalog numbers listed in a specification are for information and not intended to limit competition unless otherwise indicated. The Proposer/Bidder may offer any brand for which he is an authorized representative, which meets or exceeds the RFP/BID specification for any item(s). If RFP's/BID's are based on equivalent products, indicate on the RFP/BID FORM the manufacturer's product name and literature, and/or complete specifications. Reference to literature submitted with a previous RFP/BID will not satisfy this provision. The Proposer/Bidder shall explain in detail the reason(s) why the proposed equivalent will meet the specifications and not be considered an exception thereto. RFP's/BID's which do not comply with these requirements are subject to rejection. RFP's/BID's lacking any written indication of intent to quote an alternate brand will be received and considered in complete compliance with the specifications as listed on the RFP/BID FORM. The Budget & Purchasing Manager is to be notified, in writing, of any proposed changes in materials used, manufacturing process, or construction. However, changes shall not be binding upon the Boards unless evidenced by a Change Notice issued and signed by the Budget & Purchasing Manager, or designated representative.

QUANTITIES: The quantities as specified in this RFP/BID are estimates only and are not to be construed as guaranteed minimums.

SAMPLES: Samples of items, when called for, shall be furnished free of expense, and if not destroyed may, upon request, be returned at the Proposer's/Bidder's expense. Each sample shall be labeled with the Proposer's/Bidder's name, manufacturer brand name and number, RFP/BID number and item reference. Samples of successful Proposer's/Bidder's items may remain on file for the term of the contract. Request for return of samples shall be accompanied by instructions which include shipping authorization and must be received at time of opening. Samples not returned may be disposed of by the Boards within a reasonable time as deemed appropriate.

DOCUMENT RE-CREATION: Vendor may choose to re-create any document(s) required for this solicitation, but must do so at his own risk. All required information in the original Board format must be included in any re-created document. Submittals may be deemed non-responsive if required information is not included in any re-created document.

ACKNOWLEDGE


(Signature and Date)

10.01.09

DRUG FREE WORKPLACE CERTIFICATE

I, the undersigned, in accordance with Florida Statute 287.087, hereby certify that,

Baker Barrios Architects, Inc.

(print or type name of firm)

- Publishes a written statement notifying that the unlawful manufacture, distribution, dispensing, possession or use of a controlled substance is prohibited in the workplace named above, and specifying actions that will be taken against violations of such prohibition.
- Informs employees about the dangers of drug abuse in the work place, the firm's policy of maintaining a drug free working environment, and available drug counseling, rehabilitation, and employee assistance programs, and the penalties that may be imposed upon employees for drug use violations.
- Gives each employee engaged in providing commodities or contractual services that are under proposal or bid, a copy of the statement specified above.
- Notifies the employees that as a condition of working on the commodities or contractual services that are under proposal or bid, the employee will abide by the terms of the statement and will notify the employer of any conviction of, please or guilty or nolo contendere to, any violation of Chapter 1893, or of any controlled substance law of the State of Florida or the United States, for a violation occurring in the work place, no later than five (5) days after such conviction, and requires employees to sign copies of such written (*) statement to acknowledge their receipt.
- Imposes a sanction on, or requires the satisfactory participation in, a drug abuse assistance or rehabilitation program, if such is available in the employee's community, by any employee who is so convicted.
- Makes a good faith effort to continue to maintain a drug free work place through the implementation of the drug free workplace program.
- "As a person authorized to sign this statement, I certify that the above named business, firm or corporation complies fully with the requirements set forth herein".

Authorized Signature

10.01.09

Date Signed

State of: Florida

County of: Orange

Sworn to and subscribed before me this 1ST day of Oct., 2009

Personally known ☒ or Produced Identification _____
(Specify Type of Identification)

Signature of Notary

ATHENA P. STURNO
MY COMMISSION # DD571423
My Commission Expires: July 5, 2010
(407) 398-0153 Florida Notary Service.com

(seal)

This document must be completed and returned with your Submittal

Conflict of Interest Disclosure Form

I HEREBY CERTIFY that

2. I (printed name) Carlos Barrios am the
(title) Principal and the duly authorized representative of the firm of (Firm
Name) Baker Barrios Architects, Inc. whose address is
189 S. Orange Ave., Suite 1700, Orlando, FL 32801
, and that I possess the legal

authority to make this affidavit on behalf of myself and the firm for which I am acting; and,

2. Except as listed below, no employee, officer, or agent of the firm have any conflicts of interest, real or apparent, due to ownership, other clients, contracts, or interests associated with this project; and,


3. This bid proposal is made without prior understanding, agreement, or connection with any corporation, firm, or person submitting a bid proposal for the same services, and is in all respects fair and without collusion or fraud.

EXCEPTIONS (List)

Signature: Printed Name: Carlos BarriosFirm Name: Baker Barrios Architects, Inc.Date: 10/1/09Sworn to and subscribed before me this 1ST day of October 2009Personally Known ☒

OR Produced Identification _____, Type of Identification _____

My Commission Expires



(Printed, typed or stamped commissioned name of notary)

THIS FORM MUST BE COMPLETED AND RETURNED WITH YOUR QUALIFICATIONS PACKAGE

Tab B

FORM 1

FIRM PROFILE

Proposed Discipline: **Architectural/Engineering Services**

<p>1. Firm (or joint venture) Name & Address</p> <p>Baker Barrios Architects, Inc. 189 S. Orange Avenue, Suite 1700 Orlando, FL 32801</p>	<p>1c. Licensed to do business in the State of Florida <u> X </u> Yes <u> </u> No</p> <hr/> <p>1d. Name, Title & Telephone Number of Principal to Contact</p> <p>Mike Houseman, AIA, LEED AP Principal Studio Director 407.926.3000 <u>mhouseman@bakerbarrios.com</u></p>
<p>1a. Firm is <u> </u> National <u> </u> Regional <u> X </u> Local</p> <p>FEIN # <u> 59-344163 </u></p>	<p>1e. Address of office to perform work, if different from Item 1</p> <p>N/A</p>
<p>1b. Firm is a Certified Minority Business Enterprise <u> X </u> Yes <u> </u> No</p>	

2. Please list the number of people by discipline that your firm/joint venture will commit to the County's project.

The strength of every firm is in its people. Our highly-trained staff draws upon the resources of over 60 professionals with active registrations in 18 states. Our professional designers, architects, interior designers, CAD specialists, drafters and support staff have the level of expertise, diversity, resources and depth of experience to deliver the best architectural and design product for the client's needs. Baker Barrios Architects, Inc. attributes its success to a core philosophy that is carried throughout every aspect of the organization: **Our business is service.**

As a collaborative team environment, our firm is committed to using everyone as a resource on a project. Below is our list of employees at Baker Barrios Architects, Inc.

Architects -13
 Administrative – 6
 Construction Administration – 2
 Interior Designers – 9
 CADD Designers – 15
 Technical Quality Assurance / Control -1
 Concept Designers – 3
 Project Manager – 4
 Marketing/Development - 4
Managed Information Systems - 1
 Total Staff - 58

3. If submittal is by joint venture list participating firms and outline specific areas of responsibility (including administrative, technical, and financial) for each firm:

N/A

3a. Has this joint venture previously worked together? ____ Yes ____ No

State of Florida



Department of State

I certify the attached is a true and correct copy of the Articles of Amendment, filed on April 21, 2005, to Articles of Incorporation for FARMER BAKER BARRIOS ARCHITECTS, INC. which changed its name to BAKER BARRIOS ARCHITECTS, INC., a Florida corporation, as shown by the records of this office.

The document number of this corporation is P97000040142.

Given under my hand and the
Great Seal of the State of Florida
at Tallahassee, the Capitol, this the
Twenty-first day of April, 2005



CR2EO22 (2-03)

Glenda E. Hood

Glenda E. Hood
Secretary of State

AC# 4234461

STATE OF FLORIDA

DEPARTMENT OF BUSINESS AND PROFESSIONAL REGULATION
BOARD OF ARCHITECTURE & INTERIOR DESIGN

SEQ# L09012700561

DATE	BATCH NUMBER	LICENSE NBR
01/27/2009	080341215	AA0002981

The ARCHITECT CORPORATION

Named below IS CERTIFIED

Under the provisions of Chapter 481 FS.

Expiration date: FEB 28, 2011

BAKER BARRIOS ARCHITECTS, INC.
189 SOUTH ORANGE AVE
SUITE 1700
ORLANDO FL 32801

CHARLIE CRIST
GOVERNOR

CHARLES W. DRAGO
SECRETARY

DISPLAY AS REQUIRED BY LAW

ACORD™ CERTIFICATE OF LIABILITY INSURANCEDATE (MM/DD/YYYY)
11/14/08

PRODUCER
Suncoast Insurance Associates
 P.O. Box 22668
 Tampa, FL 33622-2668
 813-289-5200

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

INSURED
Baker Barrios Architects, Inc.
 189 S. Orange Avenue, Suite 1700
 Orlando, FL 32801

INSURERS AFFORDING COVERAGE

NAIC #

INSURER A: **XL Specialty Insurance Company**

37885

INSURER B:

INSURER C:

INSURER D:

INSURER E:

COVERAGES

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR ADD'L LTR	INSRD	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	LIMITS
		GENERAL LIABILITY <input type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS MADE <input type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC				EACH OCCURRENCE \$ DAMAGE TO RENTED PREMISES (Ea occurrence) \$ MED EXP (Any one person) \$ PERSONAL & ADV INJURY \$ GENERAL AGGREGATE \$ PRODUCTS - COMP/OP AGG \$
		AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> ALL OWNED AUTOS <input type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS <input type="checkbox"/> NON-OWNED AUTOS				COMBINED SINGLE LIMIT (Ea accident) \$ BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$
		GARAGE LIABILITY <input type="checkbox"/> ANY AUTO				AUTO ONLY - EA ACCIDENT \$ OTHER THAN EA ACC AGG \$
		EXCESS/UMBRELLA LIABILITY <input type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE DEDUCTIBLE RETENTION \$				EACH OCCURRENCE \$ AGGREGATE \$ \$ \$ \$
		WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? If yes, describe under SPECIAL PROVISIONS below				WC STATU-TORY LIMITS OTH-ER E.L. EACH ACCIDENT \$ E.L. DISEASE - EA EMPLOYEE \$ E.L. DISEASE - POLICY LIMIT \$
A		OTHER Professional Liability	DPR9617659	11/15/08	11/15/09	\$3,000,000 per claim \$5,000,000 annl aggr.

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES / EXCLUSIONS ADDED BY ENDORSEMENT / SPECIAL PROVISIONS
 Professional Liability is written on a claims made and reported basis.

CERTIFICATE HOLDER

FOR PROPOSAL PURPOSES

CANCELLATION

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, THE ISSUING INSURER WILL ENDEAVOR TO MAIL 30 DAYS WRITTEN NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO DO SO SHALL IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE INSURER, ITS AGENTS OR REPRESENTATIVES.

AUTHORIZED REPRESENTATIVE



ACORD CERTIFICATE OF LIABILITY INSURANCEOP ID ET
BAKEBAR

DATE (MM/DD/YYYY)

10/01/09

PRODUCER

BB&T - J Rolfe Davis Insurance
P.O. Box 4927
Orlando FL 32802-4927
Phone: 407-691-9600

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION
ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE
HOLDER. THIS CERTIFICATE DOES NOT AMEND, EXTEND OR
ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW.

INSURED

Baker Barrios Architects, Inc.
189 S. Orange Avenue, Ste #1700
Orlando FL 32801

INSURERS AFFORDING COVERAGE

NAIC

INSURER A: Hartford Casualty Insurance Co

29424

INSURER B: Zurich North American

INSURER C:

INSURER D:

INSURER E:

COVERAGES

THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING
ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR
MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH
POLICIES. AGGREGATE LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR ADD'L LTR INSRD	TYPE OF INSURANCE	POLICY NUMBER	POLICY EFFECTIVE DATE (MM/DD/YY)	POLICY EXPIRATION DATE (MM/DD/YY)	LIMITS	
A	GENERAL LIABILITY	21SBA UF6297	11/15/08	11/15/09	EACH OCCURRENCE	\$ 1000000
	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY				DAMAGE TO RENTED PREMISES (Ea occurrence)	\$ 1000000
	<input type="checkbox"/> CLAIMS MADE <input checked="" type="checkbox"/> OCCUR				MED EXP (Any one person)	\$ 10000
					PERSONAL & ADV INJURY	\$ 1000000
	GEN'L AGGREGATE LIMIT APPLIES PER				GENERAL AGGREGATE	\$ 2000000
	<input type="checkbox"/> POLICY <input type="checkbox"/> PRO- JECT <input checked="" type="checkbox"/> LOC				PRODUCTS - COMP/OP AGG	\$ 2000000
	AUTOMOBILE LIABILITY				COMBINED SINGLE LIMIT (Ea accident)	\$
	<input type="checkbox"/> ANY AUTO				BODILY INJURY (Per person)	\$
	<input type="checkbox"/> ALL OWNED AUTOS				BODILY INJURY (Per accident)	\$
	<input type="checkbox"/> SCHEDULED AUTOS				PROPERTY DAMAGE (Per accident)	\$
	<input type="checkbox"/> HIRED AUTOS					
	<input type="checkbox"/> NON-OWNED AUTOS					
	GARAGE LIABILITY				AUTO ONLY - EA ACCIDENT	\$
	<input type="checkbox"/> ANY AUTO				OTHER THAN EA ACC	\$
					AUTO ONLY AGG	\$
A	EXCESS/UMBRELLA LIABILITY	21SBA UF6297	11/15/08	11/15/09	EACH OCCURRENCE	\$ 5000000
	<input checked="" type="checkbox"/> OCCUR <input type="checkbox"/> CLAIMS MADE				AGGREGATE	\$ 5000000
	<input type="checkbox"/> DEDUCTIBLE					\$
	<input checked="" type="checkbox"/> RETENTION \$10000					\$
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY	WC0253005502	09/01/09	09/01/10	<input checked="" type="checkbox"/> WC STATU- TORY LIMITS <input type="checkbox"/> OTH- ER	
	E.L. EACH ACCIDENT				\$ 500000	
	E.L. DISEASE - EA EMPLOYEE				\$ 500000	
	E.L. DISEASE - POLICY LIMIT				\$ 500000	
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? If yes, describe under SPECIAL PROVISIONS below					
	OTHER					

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES / EXCLUSIONS ADDED BY ENDORSEMENT / SPECIAL PROVISIONS

The General Liability policy includes a blanket additional insured
endorsement for Certificate Holder if required by written contract.

CERTIFICATE HOLDER

CANCELLATION

SAMPLE

SAMPLE CERTIFICATE FOR
PROPOSAL PURPOSES ONLY

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION
DATE THEREOF, THE ISSUING INSURER WILL ENDEAVOR TO MAIL 10 DAYS WRITTEN
NOTICE TO THE CERTIFICATE HOLDER NAMED TO THE LEFT, BUT FAILURE TO DO SO SHALL
IMPOSE NO OBLIGATION OR LIABILITY OF ANY KIND UPON THE INSURER, ITS AGENTS OR
REPRESENTATIVES.

AUTHORIZED REPRESENTATIVE

Tab C

TEAM COMPOSITION

Name & Title: Carlos Barrios, AIA, Principal-In-Charge
Project assignment: Principal-In-Charge
Name of firm with which associated: Baker Barrios Architects, Inc.
Years experience: 31 years
With this firm <u>15 years</u> With other firms <u>16 years</u>
Education: Degree(s)/year/school/specialization: Master of Architecture, University of Florida, 1983 Bachelor of Design in Architecture, University of Florida, 1977
Active registration: Year first registered/discipline Registered Architect AR01512; NCARB Certified
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ Fire Station Prototype, Orange County, Florida - Prepared design and specification criteria as a basis of design and planning of all future Fire Stations for Orange County. ▪ Cobb County Fire Station 5 - \$2.34 million, 10,400 SF 2-story, 2-bay facility with a built-out basement level capable of housing a minimum of 74 feet of truck space lengthwise. ▪ GSFIC Cobb County Safety and Hero Unit Facility - 12,000 SF, \$3 million, facility that will serve as a joint use facility for the Georgia Department of Transportation (DOT) Highway Emergency Response Operators (HERO) Unit Facility and a Department of Public Safety (DPS) State Patrol Post. ▪ Orange County Sheriff Complex, Orlando, Florida - 220,000 SF, 2-story total conversion and renovation of an abandoned store. The \$7.4 million complex houses administrative offices, forensic laboratory, high security and training facility. ▪ RCID Fire Station No. 4 and Emergency Services Center, Lake Buena Vista, Florida - The \$3.5 million, 19,468 SF station includes a 11,968 SF fire station a sheriff's office, and information service dept which is totally self-sustaining and augments the district's 24-hour fire, rescue and emergency medical services. ▪ RCID Fire Station No. 2, Walt Disney World, Lake Buena Vista, Florida - \$1.04 million, 10,000 SF Fire Station. ▪ The Villages, Lake Sumter Landing, Florida - \$70 million, 28 mixed-use buildings consisting of commercial office, retail, restaurants and a movie theater. ▪ Jacksonville Beach Fire Station No. 2, Jacksonville Beach, Florida - \$701,874 Fire Station which includes a 24 hour call center, kitchen, sleep area, living room and fitness. ▪ Fire Station No. 2, City of Oviedo, Florida - 10,000 SF Fire Station with three drive-thru bays,\$1 million.

TEAM COMPOSITION

Name & Title: Tim Baker, Design Principal	
Project assignment: Design Principal	
Name of firm with which associated: Baker Barrios Architects, Inc.	
Years experience: 24 years	
With this firm <u>16 years</u>	With other firms <u>8 years</u>
Education: Degree(s)/year/school/specialization: Masters of Architecture / Ohio State University / 1987 Bachelor of Science in Architecture / Ohio State University / 1985	
Active registration: Year first registered/discipline Registered Architect AR0014098; NCARB Certified	
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ The Villages, Lake Sumter Landing, Florida - \$70 million, 28 mixed-use buildings consisting of commercial office, retail, restaurants and a movie theater. ▪ Jacksonville Beach Fire Station No. 2, Jacksonville Beach, Florida - \$701,874 Fire Station which includes a 24 hour call center, kitchen, sleep area, living room and fitness ▪ Fire Station No. 2, City of Oviedo, Florida - 10,000 SF Fire Station with three drive-thru bays,\$1 million. ▪ Fire Station Prototype, Orange County, Florida - Prepared design and specification criteria as a basis of design and planning of all future Fire Stations for Orange County. ▪ Cobb County Fire Station 5 - \$2.34 million, 10,400 SF 2-story, 2-bay facility with a built-out basement level capable of housing a minimum of 74 feet of truck space lengthwise. ▪ GSFIC Cobb County Safety and Hero Unit Facility - 12,000 SF, \$3 million, facility that will serve as a joint use facility for the Georgia Department of Transportation (DOT) Highway Emergence Response Operators (HERO) Unit Facility and a Department of Public Safety (DPS) State Patrol Post. ▪ Orlando Utilities Commission Plaza, Orlando, Florida - 127,000 SF office space, \$34 million new OUC administrative headquarters and corporate office building. The nine-story facility will also provide 400 parking spaces. LEED Gold. ▪ RCID Fire Station No. 4 and Emergency Services Center, Lake Buena Vista, Florida - The \$3.5 million, 19,468 SF station includes a 11,968 SF fire station a sheriff's office, and information service dept which is totally self-sustaining and augments the district's 24-hour fire, rescue and emergency medical services. ▪ RCID Fire Station No. 2, Walt Disney World, Lake Buena Vista, Florida - \$1.04 million, 10,000 SF Fire Station.□ 	

TEAM COMPOSITION

Name & Title: Scott Martin, LEED AP, Principal	
Project assignment: Concept Designer	
Name of firm with which associated: Baker Barrios Architects, Inc.	
Years experience: 15 years	
With this firm <u>5 years</u>	With other firms <u>10 years</u>
Education: Degree(s)/year/school/specialization: Graduate Certificate Community Design & Development / 2003 Master of Architecture / University of South Florida / 2002 Bachelor of Design / University of Florida / 1994	
Active registration: Year first registered/discipline LEED Accredited Professional	
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ Orlando Utilities Commission Plaza, Orlando, Florida - 127,000 SF office space, \$34 million new OUC administrative headquarters and corporate office building. The nine-story facility will also provide 400 parking spaces. LEED Gold. ▪ CW Bill Young Hall, University of South Florida, Tampa, Florida - Design / Build of a \$10 million, four-story, 53,709 SF building. The first and second floor will be lecture halls and smaller classrooms, the third floor is for the Joint Military Leadership, and the fourth floor is for offices and conference rooms. ▪ Army Lacrosse Facility, United States Military Academy, West Point, New York - The 2-story, 28,000 SF Lacrosse Training Facility will contain offices and support space for the Lacrosse Varsity Program as well as the adjacent Foley Athletic Center. ▪ Orlando Health Medical Office and Surgery Center, Orlando, Florida – Design/ Build of a Class “A” Office Building “shell,” including site planning, the structural framework, the building enclosure, the lobbies, and the core, shell and common areas, including toilet rooms, elevators, mechanical and electrical room and ceiling space. The five-story medical building will contain 153,664 SF medical office space and 3,471 SF of retail space. ▪ The Plaza, Orlando, Florida - \$76 million, major mixed-use development with 398,796 SF of office space, a 12-plex movie theater, 43,517 SF of retail and restaurant space as well as a 1,400 car parking garage. ▪ Phillips View Office Tower, Orlando, Florida - 15-story, 325,987 SF commercial office building with a 345 parking garage. ▪ Barona Administration Building and Tribal Center, Lakeside, California - 35,540 SF, \$6.9 million administration and tribal center will include tribal services, meeting room, human resources, purchasing department, accounting offices, tribal council offices, council chambers, and government relations. LEED Design. 	

TEAM COMPOSITION

Name & Title: Mike Houseman, AIA, LEED AP, Principal
Project assignment: Project Manager
Name of firm with which associated: Baker Barrios Architects, Inc.
Years experience: 14 years
With this firm <u>6 years</u> With other firms <u>8 years</u>
Education: Degree(s)/year/school/specialization: Bachelor of Architecture / University of Southern California / 1994
Active registration: Year first registered/discipline Registered Architect, Florida; LEED Accredited Professional
<p>Other experience and qualifications relevant to the proposed project:</p> <ul style="list-style-type: none"> ▪ 801 N Orange, Orlando, Florida - 264,413 SF, \$16.4 million, eight-story, mixed-use building with 95,000 SF of office space, 16,200 SF of retail and a 364 car parking garage. ▪ Belle Terre Office, Orlando, Florida - 60,00 SF, 3-story, \$5.2 million building consisting of office condos and retail space, including a restaurant, a bank and an auto showroom. The building has a 3-story atrium with glass elevators, bridges and a 40' waterfall. ▪ University of Central Florida <ul style="list-style-type: none"> ▪ Nanotechnology, Phase I - III, Orlando, Florida - The 30,000 SF phased project included classrooms, offices, cell culture labs, a clean room, bio and surface chemistry labs, and a laser room. \$3.5 million. ▪ Engineering Building II* - \$18 million 100,688 SF engineering building. ▪ Partnership II* - 91,000 SF \$20 million project serving the UCF and the Department of Defense. ▪ Morgridge International Reading Center, Phase I & II - 100,000 SF, two-building project that will house classrooms, lab spaces and multiple spaces to learn about education. LEED Silver. ▪ Northpoint 4 Office Building, Lake Mary, Florida* – 120,000 SF shell office ▪ K-12 Prototype School Designs* – Design concepts for Orange, Osceola, Seminole and Manatee ▪ La Prensa, Orlando, Florida - corporate headquarters with administrative offices and meeting space for the international spanish language periodical. ▪ University of North Florida, College of Education and Human Services, Jacksonville, Florida - 98,000 SF, \$21.4 million, classroom and office building, LEED Silver. <p style="text-align: right; margin-top: 20px;">* Previous firm experience.</p>


TEAM COMPOSITION

Name & Title: Jeffrey R. McComas, AIA, Associate	
Project assignment: Project Architect	
Name of firm with which associated: Baker Barrios Architects, Inc.	
Years experience: 24 years	
With this firm <u>6 years</u>	With other firms <u>18 years</u>
Education: Degree(s)/year/school/specialization: B.S. Architecture Technology / West Virginia State / 1985	
Active registration: Year first registered/discipline Registered Architect	
<p>Other experience and qualifications relevant to the proposed project:</p> <ul style="list-style-type: none"> ▪ 801 N Orange, Orlando, Florida - 264,413 SF, \$16.4 million, eight-story, mixed-use building with 95,000 SF of office space, 16,200 SF of retail and a 364 car parking garage. ▪ Belle Terre Office, Orlando, Florida - 60,00 SF, 3-story, \$5.2 million building consisting of office condos and retail space, including a restaurant, a bank and an auto showroom. The building has a 3-story atrium with glass elevators, bridges and a 40' waterfall. ▪ Northpoint 4 Office Building, Lake Mary, Florida* – 120,000 SF shell office ▪ K-12 Prototype School Designs* – Design concepts for Orange, Osceola, Seminole and Manatee ▪ Hewitt Associates Orlando Headquarters, Central Florida Research Park, Orlando, Florida* - Project Architect with involvement in building shell, interior design, and construction administration for a 6 story, 350,000 SF, single tenant office facility for Hewitt Associates, a large benefits company based in Lincolnshire Illinois. ▪ Multi Tenant Office Building, USF Research Park, Tampa, Florida* - Project Architect for development of 3 story, 120,000 SF, tilt-wall office building adjacent and connected to a lab facility to be utilized as a high tech business incubator at USF Research Park. ▪ West Point Foley Athletic Center, USMA, West Point, New York - Comprehensive architectural services for the \$12.2 million, 73,000 SF covered sports practice facility. ▪ Traditions, Port St. Lucie, Florida - Designed four mixed-use buildings in Traditions Square, the heart of Core Communities' expansive Traditions development. The center houses the Town Hall Building which serves as the square's anchor, surrounded by retail and office space. The town hall, designed. 	
* Previous firm experience.	

FORM 2**TEAM COMPOSITION**

Name & Title: Brian S. Hessinger, P.E., LEED AP – Chief Operating Officer
Project assignment: Sr. Mechanical Engineer
Name of firm with which associated: Ingenuity Engineers, Inc.
Years experience: 18 years
With this firm <u>5</u> With other firms <u>13</u>
Education: Degree(s)/year/school/specialization: Bachelor of Science / 1992 / University of Central Florida / Mechanical Engineering
Active registration: Year first registered/discipline 1998 / Professional Mechanical Engineer, Florida (and 11 other states) LEED Accredited Professional Active Member, American Society of Mechanical Engineers Active Member, National Fire Protection Association
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ Cobb County Fire Station #5, 10,400 SF, 2 bay, Marietta, GA ▪ City of Gainesville Public Administration Building (LEED Silver), Gainesville, FL ▪ West Melbourne City Hall, 2-story, 13,920 SF, West Melbourne, FL ▪ Moore Justice Center Expansion, Brevard County, FL ▪ Sanford City Hall Renovation, 17,200 SF, Sanford, FL ▪ Sumter County Public Works Break Room & Office Renovation, 3,000 SF, Sumter County, FL ▪ Jensen Beach Community Center, Martin County, FL ▪ Volusia County Continuing Services Contract, Volusia County, FL ▪ GSA, U.S. Citizenship and Immigration Services, Southeast Regional Office Renovation, 30,000 SF, Orlando, FL ▪ GSA, Secret Service Office Renovation, 10,000 SF, Orlando, FL ▪ U.S. Army Office Renovation and Expansio , 6,500 SF, Orlando, FL ▪ Veteran's Administration Renovation, 10,000 SF, Winter Park, FL

FORM 5



<u>1. Project Name & Location</u> Cobb County Fire Station #5 Cobb County, Georgia <u>Project Manager:</u> Brian S. Hessinger, P.E., LEED AP Senior Mechanical Engineer		Project Owners Name & Address Cobb County Marietta, Georgia 57 Waddell Street Marietta, Georgia 30060				
Completion Date (Actual or Estimated) 2008						
<u>Estimated Cost (In Thousands)</u> <table border="1"> <tr> <td>Entire Project</td> <td>Work for which firm was/is responsible</td> </tr> <tr> <td>\$2,340</td> <td>\$31.5</td> </tr> </table>		Entire Project	Work for which firm was/is responsible	\$2,340	\$31.5	<u>Project Owner's Contact Person, Title, & Telephone Number</u> Allen Kronenberger Project Manager (770) 528 -2187
Entire Project	Work for which firm was/is responsible					
\$2,340	\$31.5					
<u>Scope of Entire Project</u> Cobb County Fire Station #5 is a 10,400 square foot, single story, two bay "back-in" fire station building. The facility has a built-out basement level and is capable of housing 74-feet of truck space in each of the two bays. The building includes living quarters for 10 persons, a common area with cooking, dining, tv room and fitness room, administrative office areas, and mechanical spaces. The structure includes a 1,000 square foot community room with storage and toilets and shower facilities. Project was CM at Risk.						
<u>Nature of Firm's Responsibility in Project</u> Ingenuity Engineers provided mechanical, electrical, plumbing and fire protection engineering services associated with designing Cobb County Fire Station #5.						
<u>Firm's Personnel</u> David F. Green, Jr. - Senior Electrical Engineer; Phil Rohm, CPE, LEED AP – Senior Plumbing Engineer						

FORM 2

TEAM COMPOSITION

Name & Title: David F. Green, Jr. – President/CEO
Project assignment: Sr. Electrical Engineer
Name of firm with which associated: Ingenuity Engineers, Inc.
Years experience: 27 years
With this firm <u>5</u> With other firms <u>22</u>
Education: Degree(s)/year/school/specialization: Bachelor of Science / 1998 / Kennedy Western University, University of Dayton / Engineering
Active registration: Year first registered/discipline Illumination Engineering Society
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ Cobb County Fire Station #5, 10,400 SF, 2 bay, Marietta, GA ▪ ARFF (Air Rescue Fire Facility), 6 bay, Melbourne International Airport, Melbourne, FL* ▪ Cape Canaveral Fire Station, 6 Bay, Cape Canaveral, FL ▪ Sarasota Fire Station, Sarasota, FL* ▪ West Melbourne City Hall, 2-story, 13,920 SF, West Melbourne, FL ▪ Palm Bay Park Prototype, Palm Bay, FL* ▪ Brevard County Parks and Community Center Prototype, Brevard County, FL* ▪ Brevard County School Board Commissioning Contract, Brevard County, FL* ▪ Cocoa Civic Center, Brevard County, FL* ▪ Jensen Beach Community Center, Martin County, FL ▪ City of Gainesville Public Administration Building (LEED Silver), Gainesville, FL ▪ Moore Justice Center Expansion, Brevard County, FL ▪ Sanford City Hall Renovation, 17,200 SF, Sanford, FL
* Previous firm experience

FORM 5

<u>I. Project Name & Location</u> Public Administration Building Gainesville, Florida <u>Project Manager:</u> David F. Green, Jr. - Senior Electrical Engineer		Project Owners Name & Address City of Gainesville PO Box 490, Station 58, Gainesville, Florida 32602-0490
Completion Date (Actual or Estimated)		
Estimated Cost (In Thousands) Entire Project \$13,500		<u>Project Owner's Contact Person, Title, & Telephone Number</u> Teresa Scott, PE Director of Public Works (352) 334-2093
<u>Scope of Entire Project</u> Ingenuity Engineers, Inc., provided mechanical, electrical, plumbing, fire protection and LEED Silver engineering design services associated with designing this 18,000 square foot, hurricane-hardened municipal building which includes office areas, staging areas, and emergency operations center areas.		
 		
<u>Nature of Firm's Responsibility in Project</u> Mechanical, electrical, plumbing, fire protection and LEED Design services.		
<u>Firm's Personnel</u> Brian S. Hessinger, P.E., LEED AP - Senior Mechanical Engineer Phil Rohm, CPE, LEED AP – Senior Plumbing Engineer		

FORM 2

TEAM COMPOSITION

Name & Title: Philip J. Rohm, Jr., C.I.P.E., LEED AP - Principal
Project assignment: Sr. Plumbing Engineer
Name of firm with which associated: Ingenuity Engineers, Inc.
Years experience: 33 years
With this firm <u>5</u> With other firms <u>28</u>
Education: Degree(s)/year/school/specialization: Engineering Studies / 1977-1978 / Florida Junior College / Plumbing Engineering Engineering Studies / 1998-2000 / Valencia Community College / Plumbing Engineering
Active registration: Year first registered/discipline 1988 / C.I.P.E. (Certified In Plumbing Engineering) Active Member, American Society of Plumbing Engineers (ASPE)
Other experience and qualifications relevant to the proposed project: <ul style="list-style-type: none"> ▪ Cobb County Fire Station #5, 10,400 SF, 2 bay, Marietta, GA ▪ City of Gainesville Public Administration Building (LEED Silver), Gainesville, FL ▪ West Melbourne City Hall, 2-story, 13,920 SF, West Melbourne, FL ▪ Moore Justice Center Expansion, Brevard County, FL ▪ Sanford City Hall Renovation, 17,200 SF, Sanford, FL ▪ Sumter County Public Works Break Room & Office Renovation, 3,000 SF, Sumter County, FL ▪ Jensen Beach Community Center, Martin County, FL ▪ Volusia County Continuing Services Contract, Volusia County, FL ▪ GSA, U.S. Citizenship and Immigration Services, Southeast Regional Office Renovation, 30,000 SF, Orlando, FL ▪ GSA, Secret Service Office Renovation, 10,000 SF, Orlando, FL ▪ U.S. Army Office Renovation and Expansio , 6,500 SF, Orlando, FL ▪ Veteran's Administration Renovation, 10,000 SF, Winter Park, FL

FORM 2**TEAM COMPOSITION**

Brief resume of key persons, specialists and individual consultants shall be assigned to the project.
Utilize one sheet per person. (Additional information may be attached)

Name & Title: Dan Engebretson, President
Project assignment: Principle in Charge, Engineer of Record
Name of firm with which associated: Structures One
Years experience: With this firm <u>6</u> With other firms <u>20</u>
Education: Degree(s)/year/school/specialization: Master of Science in Engineering (Structures) University of South Florida Tampa, Florida Bachelor of Science in Business Administration University of Florida Gainesville, Florida
Active registration: Year first registered/discipline Florida PE (Structures), 2000
Other experience and qualifications relevant to the proposed project: Dan has been the Principle and/or Project Manager on projects totaling in the billions of dollars in construction costs. He has taught as an Adjunct Professor in Structures at the University of South Florida, and has served as a consulting engineer to the Florida Board of Professional Engineers. Dan is registered with NCEES the national engineer board and also holds a Threshold Inspectors license. Dan has designed multiple prototype structures including Elementary School, High Schools, and Post Offices in Hillsborough, Pasco, Pinellas, and Manatee County areas. Dan understand the specific design requirements and "big picture" items necessary to design a prototype project that can easily be build at multiple locations. Dan has also designed millions of square feet of renovations with the most notable being NETPARK which consisted of renovating an existing mall into a technical and medial office park. His knowledge and experience with prototypes and renovation will provide essential in making the renovation and prototype fire station projects a success.

FORM 2**TEAM COMPOSITION**


Brief resume of key persons, specialists and individual consultants shall be assigned to the project.
Utilize one sheet per person. (Additional information may be attached)

Name & Title: Scott Beresheim, Vice President
Project assignment: Project Manager
Name of firm with which associated: Structures One
Years experience: With this firm <u>6</u> With other firms <u>10</u>
Education: Degree(s)/year/school/specialization: Master of Science in Engineering (Structures) University of Florida Bachelor of Science in Civil Engineering University of Florida Minor in Business Administration University of Florida
Active registration: Year first registered/discipline Florida PE (Structures), 2004
Other experience and qualifications relevant to the proposed project: Scott's technical knowledge combined with his experience with design software and his desire to be a team player led him to be a successful project manager throughout his career. Scott also is registered with NCEES and is active in many organizations including SAME, Tampa Chamber of Commerce, and FES. Scott was the Project Manager and Engineer of Record of the bank prototypes for BB&T, M&I Banks, and 5/3 Banks. Scott successfully designed prototypes for each bank and successfully replicated the prototypes across the state for Florida over 50 times. Scott's experience with repeat/reuse project and ability to keep things organized will provide essential in making the renovation and prototype fire station projects a success. .

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> Multiple BB&T Banks <u>Project Manager, Engineer of Record:</u> Scott Beresheim P.E.		Project Owners Name & Address BB&T (multiple addresses) Winston Salem, NC
Completion Date (Actual or Estimated) 2006 - 2007		
Estimated Cost (In Thousands) Entire Project \$1.21 million		Project Owner's Contact Person, Title, & Telephone Number Peter Falk Project Manager T: (336) 777-3657
Work for which firm was/is responsible \$8,500/ project		
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible)		
Designed 17 BB&T Bank locations ranging in size from 3,500 to 5,000 square foot (3 prototypes). The bank designs included a Secure Design of a Vault along with drive through isles. These projects were located through out the State of Florida.		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible)		
Structures One provided structural engineering services including construction administrations and site visits for the BB&T Banks.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u>		
Dan Engebretson – Principle Scott Beresheim – Project Manager		

FORM 2

FIRM COMPOSITION

Brief resume of key persons, specialists and individual consultants shall be assigned to the project. Utilize one sheet per person. (Additional information may be attached)

Name & Title: Donald A. Griffey, P.E. / President
Project assignment: Project Manager / Civil Engineer
Name of firm with which associated: Griffey Engineering, Inc.
Years experience: With this firm <u>11</u> With other firms <u>17</u>
Education: Degree(s)/year/school/specialization: B.S.C.E. / 1981 / University of Florida
Active registration: Year first registered/discipline: Florida / 1986 / Civil Engineering Georgia / 2002 / Civil Engineering
Other experience and qualifications relevant to the proposed project: Mr. Griffey has been practicing Civil Engineering in Central Florida for over 26 years. The last 22 years he has worked in Lake County and has developed extensive knowledge of local conditions and challenges. Mr. Griffey has spent 3½ years working for local, Lake County engineering firms, nine years as the Engineering Director for Lake County, and the last 11 years as president of Griffey Engineering, Inc. He is familiar with all civil/site-engineering functions including design, permitting, construction, traffic engineering, and transportation impacts. Mr. Griffey has, in either public or private capacity, worked on innumerable projects both, large and small.

FORM 2

FIRM COMPOSITION

Brief resume of key persons, specialists and individual consultants shall be assigned to the project. Utilize one sheet per person. (Additional information may be attached)

Name & Title:

George S. Horton, P.E. / Senior Engineer

Project assignment:

Civil Engineering / Permitting

Name of firm with which associated:

Griffey Engineering, Inc.

Years experience:

With this firm 7

With other firms 1

Education: Degree(s)/year/school/specialization:

B.S.C.E. / 1999 / University of Florida

Active registration: Year first registered/discipline:

Florida / 2005 / Civil Engineering

Other experience and qualifications relevant to the proposed project:

Mr. Horton has been working in civil/site engineering for the last 8 years. Through his work experience and educational training, he has specialized in stormwater design and permitting with water management districts, FDOT, and local government agencies. In addition, Mr. Horton has been involved in full site plan development and project management including geometric layout, potable water distribution, wastewater collection systems, development review meetings, and construction services.

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

<u>4. Project Name & Location</u> Sumter Co. Tax Collector & Property Appraisor, Bushnell <u>Project Manager:</u> George Horton		<u>Project Owners Name & Address</u> Sumter County Board of County Commissioners 910 N. Main Street Bushnell, Florida 33513
<u>Completion Date (Actual or Estimated)</u> December 2008		<u>Project Owner's Contact Person, Title, & Telephone Number</u> Doug Conway, Administrative Division Project Manager (352) 793-0279
<u>Estimated Cost (In Thousands)</u> Entire Project \$	<u>Work for which firm was/is responsible</u> \$	
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Expansion of facility, Addition of new driveway access.		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Develop Civil site plan. Secure SWFWMD permitting / permit determination.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> George S. Horton / Project Manager Donald A. Griffey D. Michael King		

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

<u>4. Project Name & Location</u> Center Hill Fire Station <u>Project Manager:</u> George Horton		<u>Project Owners Name & Address</u> Sumter County Board of County Commissioners 910 N. Main Street Bushnell, Florida 33513
<u>Completion Date (Actual or Estimated)</u> December 2008		<u>Project Owner's Contact Person, Title, & Telephone Number</u> Doug Conway, Administrative Division Project Manager (352) 793-0279
<u>Estimated Cost (In Thousands)</u> Entire Project \$	<u>Work for which firm was/is responsible</u> \$	
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Expansion of facility, Addition of new driveway access.		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Develop Civil site plan. Secure SWFWMD permitting / permit determination.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> George S. Horton / Project Manager Donald A. Griffey D. Michael King		

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

<u>4. Project Name & Location</u> Lake Panasoffkee Community Library <u>Project Manager:</u> George Horton		<u>Project Owners Name & Address</u> Sumter County Board of County Commissioners 910 N. Main Street Bushnell, Florida 33513
<u>Completion Date (Actual or Estimated)</u> December 2008		<u>Project Owner's Contact Person, Title, & Telephone Number</u> Doug Conway, Administrative Division Project Manager (352) 793-0279
<u>Estimated Cost (In Thousands)</u> Entire Project \$	<u>Work for which firm was/is responsible</u> \$	
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Expansion of facility, Addition of new driveway access.		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Develop Civil site plan. Secure SWFWMD permitting / permit determination.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> George S. Horton / Project Manager Donald A. Griffey D. Michael King		

FORM 2

TEAM COMPOSITION

Brief resume of key persons, specialists and individual consultants shall be assigned to the project.

Utilize one sheet per person. (Additional information may be attached)

Name & Title:
Larry J. Trobough, Principal Consultant
Project assignment:
Design of technology and low-voltage systems.
Name of firm with which associated:
Technology Research & Consulting, Inc.
Years experience:
With this firm <u>8</u> With other firms <u>25</u>
Education: Degree(s)/year/school/specialization:
N/A
Active registration: Year first registered/discipline
N/A
Other experience and qualifications relevant to the proposed project:
BICSI Certified Registered Communications Distribution Designer (RCDD) since 1995

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> City of Orlando Fire Station #7 Orlando, Florida <u>Project Manager:</u> Abe Jardaneh, PE, City of Orlando		Project Owners Name & Address City of Orlando 400 South Orange Avenue Orlando, Florida 32801				
Completion Date (Actual or Estimated) Construction Completed in 2009						
Estimated Cost (In Thousands) <table border="1"> <tr> <td>Entire Project</td> <td>Work for which firm was/is responsible</td> </tr> <tr> <td>\$2,350,000.00</td> <td>\$2000.00</td> </tr> </table>		Entire Project	Work for which firm was/is responsible	\$2,350,000.00	\$2000.00	<u>Project Owner's Contact Person, Title, & Telephone Number</u> Miguel Sierra, Facility Engineer 407-836-9510
Entire Project	Work for which firm was/is responsible					
\$2,350,000.00	\$2000.00					
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Construction of a new Fire Station.						
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Design and Construction Administration services for Voice/Data Cable Infrastructure, TV Distribution, Dispatch/Paging, Audio/Video, and Access Control systems.						
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Larry J. Trobough, RCDD, Technology and Low-Voltage Consultant						

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> Orange County Fire Station #20 Zellwood, Florida <u>Project Manager:</u> Tim Groth/Jose Baerga, Orange County		Project Owners Name & Address Orange County Government 201 S. Rosalind Avenue Orlando, Florida 32801
Completion Date (Actual or Estimated) Construction completed in 2006		
Estimated Cost (In Thousands) Entire Project \$1,000,000.00	Work for which firm was/is responsible \$1,000.00	Project Owner's Contact Person, Title, & Telephone Number Miguel Sierra, Facility Engineer 407-836-9510
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Construction of a new Fire Station		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Design and Construction Administration services for Fire Alarm, Voice/Data Infrastructure, TV Distribution, and Dispatch/Paging systems.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Larry J. Trobough, RCDD, Technology and Low-Voltage Systems Consultant		

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> City of Orlando Fire Station #17 Orlando, Florida <u>Project Manager:</u> Abe Jardaneh, PE, City of Orlando		Project Owners Name & Address City of Orlando 400 South Orange Avenue Orlando, Florida 32801
Completion Date (Actual or Estimated) Construction completed in 2007		
Estimated Cost (In Thousands) Entire Project		Project Owner's Contact Person, Title, & Telephone Number Miguel Sierra, Facility Engineer 407-836-9510
\$2,350,00.00	Work for which firm was/is responsible \$2,325.00	
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Construction of a new Fire Station		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Design and Construction Administration services for Fire Alarm, Voice/Data Infrastructure, TV Distribution, and Dispatch/Paging systems.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Larry J. Trobough, RCDD, Technology and Low-Voltage Systems Consultant		

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> City of Orlando Fire Station #15 Orlando, Florida <u>Project Manager:</u> Abe Jardaneh, PE, City of Orlando		Project Owners Name & Address City of Orlando 400 South Orange Avenue Orlando, Florida 32801
Completion Date (Actual or Estimated) Construction completed in 2007		
Estimated Cost (In Thousands) Entire Project \$2,350,00.00		Project Owner's Contact Person, Title, & Telephone Number Miguel Sierra, Facility Engineer 407-836-9510
	Work for which firm was/is responsible \$2,325.00	
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Construction of a new Fire Station		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Design and Construction Administration services for Fire Alarm, Voice/Data Infrastructure, TV Distribution, and Dispatch/Paging systems.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Larry J. Trobough, RCDD, Technology and Low-Voltage Systems Consultant		

FORM 5

ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

1. <u>Project Name & Location</u> City of Orlando Fire Station #16 Orlando, Florida <u>Project Manager:</u> Abe Jardaneh, PE, City of Orlando		Project Owners Name & Address City of Orlando 400 South Orange Avenue Orlando, Florida 32801
Completion Date (Actual or Estimated) Construction completed in 2007		
Estimated Cost (In Thousands) Entire Project \$2,350,00.00	Work for which firm was/is responsible \$2,325.00	<u>Project Owner's Contact Person, Title, & Telephone Number</u> Miguel Sierra, Facility Engineer 407-836-9510
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Construction of a new Fire Station		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Design and Construction Administration services for Fire Alarm, Voice/Data Infrastructure, TV Distribution, and Dispatch/Paging systems.		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Larry J. Trobough, RCDD, Technology and Low-Voltage Systems Consultant		

Tab D

FORM 3**OUTSIDE KEY CONSULTANTS**

If respondent is not a joint venture, list outside key consultants/associates that shall be used for the proposed project. (Form may be reproduced if additional space is necessary.) Include resume of all individuals assigned to this project including projects they have worked on and contact names for each.

Company Name: Ingenuity Engineers, Inc.

Address of office proposed for this project: 4798 New Broad St, Orlando, FL 32814

Role (i.e. Civil Engineering, Environmental, Landscape Architectural...)	Projected % of Over-All Work on Entire Project	Name of Individual Assigned to this Project	Firm Worked with prime before (Yes or No)	Individual Worked with prime before (Yes or No)
Mechanical Engineering Plumbing Fire Protection	25%*	Brian Hessinger, P.E., LEED AP Chief Operating Officer Sr. Mechanical Engineer David Green, Jr. Electrical Engineer Phil Rohm, Sr. Principal Sr. Plumbing Engineer	Yes	Yes

Attach resume and projects.

Company Name: Structures One

Address of office proposed for this project: 1305 W. Linebaugh Ave., #102, Tampa, FL 33626

Role (i.e. Civil Engineering, Environmental, Landscape Architectural...)	Projected % of Over-All Work on Entire Project	Name of Individual Assigned to this Project	Firm Worked with prime before (Yes or No)	Individual Worked with prime before (Yes or No)
Structural Engineer	7%*	Dan Engebretson, PE Project Manager	Yes	Yes

Attach resume and projects.

Company Name: Griffey Engineering, Inc

Address of office proposed for this project: 33 N Center Street, Suite B, Eustis, FL 32726

Role (i.e. Civil Engineering, Environmental, Landscape Architectural...)	Projected % of Over-All Work on Entire Project	Name of Individual Assigned to this Project	Firm Worked with prime before (Yes or No)	Individual Worked with prime before (Yes or No)
Civil Engineering	5%*	Donald A. Griffey, PE Project Manager George S. Horton, PE Civil Engineering	No	No

Company Name: Technology Research & Consulting, Inc.

Address of office proposed for this project: 437 Gaston Foster Rd Orlando, FL 32807

Role (i.e. Civil Engineering, Environmental, Landscape Architectural...)	Projected % of Over-All Work on Entire Project	Name of Individual Assigned to this Project	Firm Worked with prime before (Yes or No)	Individual Worked with prime before (Yes or No)
Design of technology and low-voltage systems.	3%*	Larry J. Trobough, RCDD Technology Manager	Yes	Yes

Attach resume and projects.

** Projected % of work assigned are estimates at this time.*

Are there any contractual agreements between the respondent (prime consultant) and any of the proposed sub-consultants? ____ yes ☒ no

If the answer is yes, the respondent shall attach, with their submittal, information describing the contractual relationship including a copy of any written contractual agreement.

Not Applicable

Tab \bar{E}

FORM 4**LOCATION**

1. Specify address of Prime Consultant's designated office where the majority of work on this project will be performed:

**Baker Barrios Architects, Inc.
189 S. Orange Avenue, Suite 1700
Orlando, FL 32801**

2. Indicate percentage of total over-all project fees projected to be performed on this project by the Prime Consultant's office specified above. (Do not include percentage of fees anticipated to be performed on this project by sub-consultants)

60%

3. Specify address of Prime Consultant's other office(s) where any part of the work on this project will be performed (if applicable):

Not Applicable

4. Indicate percentage of total over-all fees projected to be performed on this project by the office specified above. Do not include percentage of fees anticipated to be performed on this project by sub-consultants.

Not Applicable


_____ %

5. Indicate percentage of total over-all fees projected to be performed on this project by firms located within Sumter County including the prime consultant and sub-consultants, utilizing information supplied above and on Form 2.


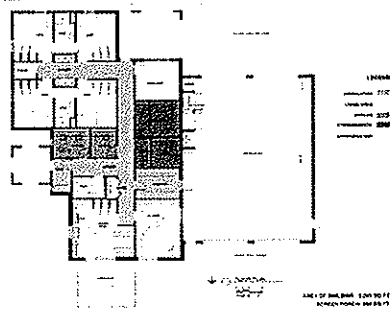
0%

Tals F


FORM 5

<p>1. <u>Project Name & Location</u></p> <p>Cobb County Fire Station #5 Cobb County, Georgia</p> <p><u>Project Manager:</u> Travis Vickers, AIA</p>		<p>Project Owners Name & Address</p> <p>Cobb County Marietta, Georgia 57 Waddell Street Marietta, Georgia 30060</p>				
<p>Completion Date (Actual or Estimated) 2008</p>						
<p>Estimated Cost (In Thousands)</p> <table border="1"> <tr> <td>Entire Project</td> <td>Work for which firm was/is responsible</td> </tr> <tr> <td>\$2,340</td> <td>\$2,340</td> </tr> </table>		Entire Project	Work for which firm was/is responsible	\$2,340	\$2,340	<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p> <p>Allen Kronenberger Project Manager (770) 528 -2187</p>
Entire Project	Work for which firm was/is responsible					
\$2,340	\$2,340					
<p><u>Scope of Entire Project</u></p> <p>Cobb County Fire Station #5 is a 10,400 square foot, single story, two bay "back-in" fire station building. The facility has a built-out basement level and is capable of housing 74-feet of truck space in each of the two bays. The building includes living quarters for 10 persons, a common area with cooking, dining, tv room and fitness room, administrative office areas, and mechanical spaces. The structure includes a 1,000 square foot community room with storage and toilets and shower facilities. Project was CM at Risk.</p>						
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>Master Planning, Programming, Architecture, Interior Design, Construction Administration and Construction Phase Services</p>						
<p><u>Firm's Personnel</u></p> <p>Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal David F. Green, Jr. - Senior Electrical Engineer (Ingenuity Engineers) Brian S. Hessinger, P.E., LEED AP - Senior Mechanical Engineer (Ingenuity Engineers) Phil Rohm, CPE, LEED AP – Senior Plumbing Engineer</p>						

FORM 5

<p>2. <u>Project Name & Location</u></p> <p>Jacksonville Beach Fire Station 2 Jacksonville Beach, Florida</p> <p><u>Project Manager:</u> Carlos Barrios, AIA</p>		<p>Project Owners Name & Address</p> <p>Jacksonville Beach Central Services Department 1460 A Shetter Avenue Jacksonville Beach, FL 32250</p>
<p>Completion Date (Actual or Estimated) 2000</p>		
<p>Estimated Cost (In Thousands)</p>		<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p> <p>Gary Frazer Project Manager (904) 247-6201</p>
<p>Entire Project</p> <p>\$701</p>	<p>Work for which firm was/is responsible</p> <p>\$701</p>	
<p><u>Scope of Entire Project</u></p> <p>Baker Barrios Architects, Inc. worked on a design /build fire station for the City of Jacksonville Beach. Designed to blend in with its surroundings, the two-story building is 5,051 SF and is designed to house a fitness room, dinning room, and five person dorm and administration offices.</p>		
 		
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>Master Planning, Programming, Architecture, Construction Administration and Construction Phase Services</p>		
<p><u>Firm's Personnel</u></p> <p>Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal</p>		


FORM 5

<u>3. Project Name & Location</u> Reedy Creek Fire Station No. 4 and Emergency Services Building Lake Buena Vista, Florida <u>Project Manager:</u> Carlos Barrios, AIA		Project Owners Name & Address Reedy Creek Improvement District 1900 Hotel Plaza Boulevard Lake Buena Vista, FL
Completion Date (Actual or Estimated) 2003		
<u>Estimated Cost (In Thousands)</u> Entire Project \$3,500		<u>Project Owner's Contact Person, Title, & Telephone Number</u> Mickey Shiver Deputy District Administrator (407) 828-2241
	Work for which firm was/is responsible \$3,500	
		
<u>Scope of Entire Project</u> Reedy Creek Fire Dept's Fire Station No. 4 and Emergency Services Building is fully equipped to handle the demands of Walt Disney World Resorts and the surrounding area. The 19,468 SF complex provides a centralized, state-of-the-art, 24-hour emergency services complex with a 2,050 SF Sheriff's Office, 5,432 Information Services Dept and an 11,968 SF fire station with a living quarters.		
<u>Nature of Firm's Responsibility in Project</u> Architect of Record		
<u>Firm's Personnel</u> Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal		



FORM 5

<p>4. <u>Project Name & Location</u></p> <p>Reedy Creek Fire Station No. 2 Lake Buena Vista, Florida</p> <p><u>Project Manager:</u> Carlos Barrios, AIA</p>		<p>Project Owners Name & Address</p> <p>Reedy Creek Improvement District 1900 Hotel Plaza Boulevard Lake Buena Vista, FL</p>				
<p>Completion Date (Actual or Estimated) 1999</p>						
<p><u>Estimated Cost (In Thousands)</u></p> <table border="1"> <tr> <td>Entire Project</td> <td>Work for which firm was/is responsible</td> </tr> <tr> <td>\$1,004</td> <td>\$1,004</td> </tr> </table>		Entire Project	Work for which firm was/is responsible	\$1,004	\$1,004	<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p> <p>Mickey Shiver Deputy District Administrator (407) 828-2241</p>
Entire Project	Work for which firm was/is responsible					
\$1,004	\$1,004					
<p><u>Scope of Entire Project</u></p> <p>Reedy Creek Improvement District's new Fire Station was designed to meet the increased demands placed on the district's Department of Emergency Services by the continued growth of Walt Disney World Resorts. The facility is self-sustaining and augments the district's 24-hour fire, rescue and emergency medical services.</p> <div data-bbox="581 1142 1393 1465" data-label="Image"> </div>						
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>Architecture and Interior Design</p>						
<p><u>Firm's Personnel</u></p> <p>Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal</p>						

FORM 5
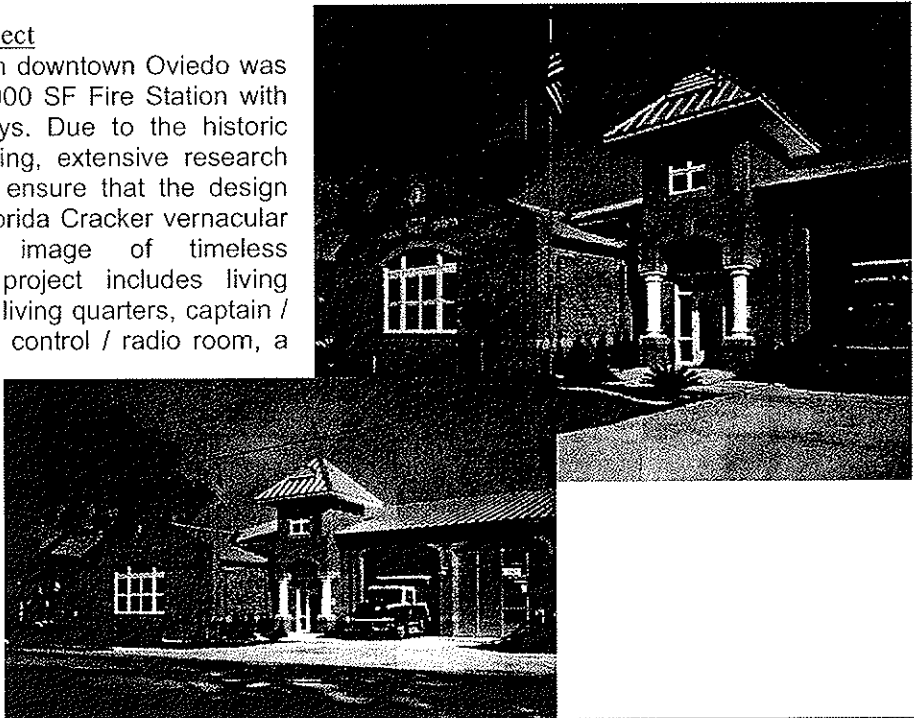
<p>5. <u>Project Name & Location</u></p> <p>Oviedo Fire Station No. 2 Oviedo, Florida</p> <p><u>Project Manager:</u> Carlos Barrios, AIA</p>		<p>Project Owners Name & Address</p> <p>City of Oviedo 400 Alexandria Blvd. Oviedo, FL 32765</p>
<p>Completion Date (Actual or Estimated) 1997</p>		
<p>Estimated Cost (In Thousands)</p>		<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p> <p>Bobby Wyatt (407) 971-5640</p>
<p>Entire Project</p> <p>\$1,004</p>	<p>Work for which firm was/is responsible</p> <p>\$1,004</p>	
<p><u>Scope of Entire Project</u></p> <p>A historic building in downtown Oviedo was converted to a 10,000 SF Fire Station with three drive-thru bays. Due to the historic nature of the building, extensive research was undertaken to ensure that the design honored the Old Florida Cracker vernacular to achieve an image of timeless architecture. The project includes living quarters with 8-unit living quarters, captain / officer's quarters, a control / radio room, a living room</p>		
		
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>Architecture and Interior Design</p>		
<p><u>Firm's Personnel</u></p> <p>Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal</p>		

FORM 5

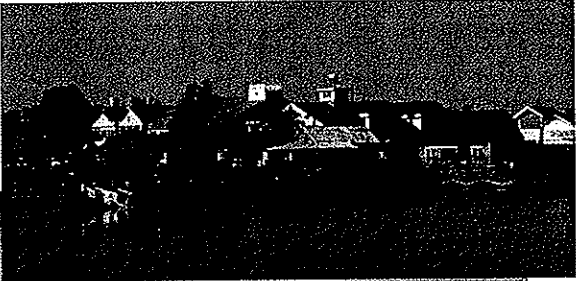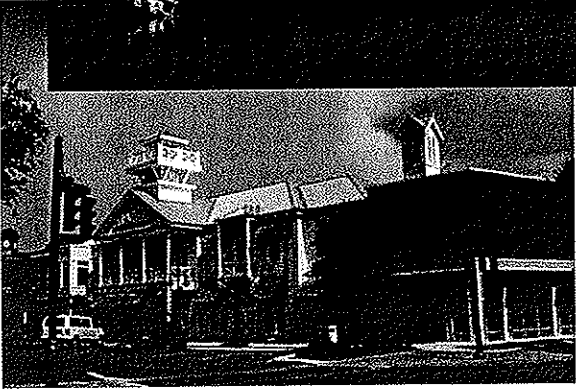
6. <u>Project Name & Location</u> The Villages Lake Sumter Landing at The Villages, Florida <u>Project Manager:</u> Ray Acosta, AIA, Principal		Project Owners Name & Address The Villages 1100 Main Street The Villages, FL 32159 United States of America				
Completion Date (Actual or Estimated) 2004						
<u>Estimated Cost (In Thousands)</u> <table border="1"> <tr> <td>Entire Project</td> <td>Work for which firm was/is responsible</td> </tr> <tr> <td>\$70,000</td> <td>\$70,000</td> </tr> </table>		Entire Project	Work for which firm was/is responsible	\$70,000	\$70,000	<u>Project Owner's Contact Person, Title, & Telephone Number</u> Tracy Mathews (352) 753-6239
Entire Project	Work for which firm was/is responsible					
\$70,000	\$70,000					
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) 28 Building Village that includes: Commercial Office, Retail, Restaurant, Movie Theaters, Civic Center						
 						
<u>Nature of Firm's Responsibility in Project</u> Master Planning, Architecture (Architect of Record), Interior Design						
<u>Firm's Personnel</u> Carlo Barrios, AIA -- Principal-In-Charge Tim Baker, AIA -- Design Principal						

<p>7. <u>Project Name & Location</u></p> <p>Prototype Fire Stations #28, #29, and #30 Orange County, FL</p> <p><u>Project Manager:</u> Tim Baker, AIA</p>		<p>Project Owners Name & Address</p> <p>Orange County Capital Projects Department 500 E South Street, Suite 500 Orlando, FL 32801</p>
<p>Completion Date (Actual or Estimated) 2000</p>		<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p> <p>Jody Strickland, Project Manager (407) 836-0050</p>
<p>Estimated Cost (In Thousands)</p>		
<p>Entire Project</p> <p>N/A</p>	<p>Work for which firm was/is responsible</p> <p>N/A</p>	
<p><u>Scope of Entire Project</u></p> <p>The design layout of the fire stations was made to maximize floorplan space. The room locations have been determined so that their individual functions and inter-relationships may complement each other as a whole. This results in an overall floor plan that is logical, practical, and efficient. The area of the floor plan, including the two-bay Apparatus Room but not including the patio, is 6,000 square feet and is one-story in height. We have worked with Orange County, Florida in developing the original fire station prototype for the two and three bay stations. We completed Fire Station # 70, Fire Station # 28 and Fire Station # 29 in Orange County.</p>		
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>concept design, programming and planning</p>		
<p><u>Firm's Personnel</u></p> <p>Carlo Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal</p>		

FORM 5


ILLUSTRATIVE WORK

Work by firm or joint venture members or outside key consultants which best illustrate current qualifications relevant to the County's project that have been/is being accomplished by personnel that shall be assigned to the County's project. List no more than ten (10) projects.

8. <u>Project Name & Location</u> Orange County Sheriff's Complex Orlando, Florida <u>Project Manager: Ray Acosta, AIA</u>		Project Owners Name & Address Orange County Department of Capital Projects 400 E. South Street Suite 500 Orlando, FL 32801
Completion Date (Actual or Estimated) December 2002 (Phase I)		
Estimated Cost (In Thousands)		<u>Project Owner's Contact Person, Title, & Telephone Number</u>
Entire Project \$7,400	Work for which firm was/is responsible \$388 (design fee)	Mr. Jody Strickland Project Manager (407) 836-0050
<u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Forensic Laboratory, High Security, Training Facility, Credit Union		
<u>Nature of Firm's Responsibility in Project</u> (Please give quantitative indications wherever possible) Baker Barrios Architects, Inc. provided comprehensive planning, architecture and interior design services for the total conversion and renovation of a 220,000 SF, 2-story abandoned Montgomery Ward Store on Colonial Drive in Orlando. The multi-phased project is the new Central Complex for the Orange County Sheriff's Office and houses offices, a laboratory, a credit union and training facility.		
		
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Carlos Barrios, AIA – Principal-In-Charge Ray Acosta, AIA – Project Manager		


FORM 5

ILLUSTRATIVE WORK
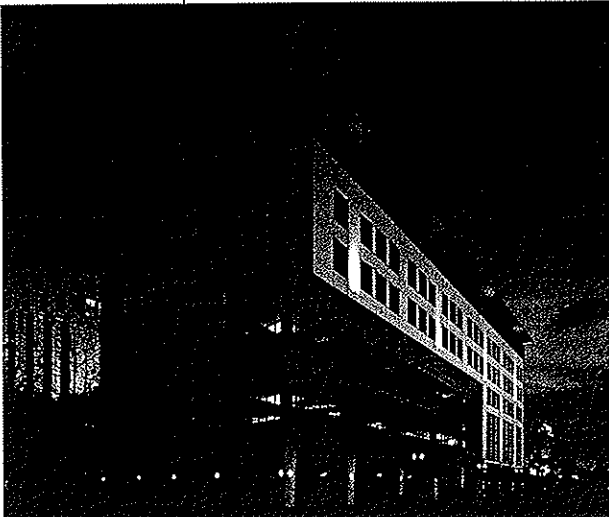
<p>9. <u>Project Name & Location</u></p> <p>801 N Orange Orlando, Florida</p> <p><u>Project Manager:</u> Jeff McComas, AIA</p>		<p>Project Owners Name & Address</p> <p>Uster Properties, Inc. 801 N Orange Avenue Suite 530 Orlando, FL 32801</p>
<p>Completion Date (Actual or Estimated)</p> <p>2006</p>		
<p>Estimated Cost (In Thousands)</p>		<p><u>Project Owner's Contact Person, Title, & Telephone Number</u></p>
<p>Entire Project</p> <p>\$16,400</p>	<p>Work for which firm was/is responsible</p> <p>\$16,400</p>	<p>Craig Ustler, Principal (407) 839-1070</p>
<p><u>Scope of Entire Project</u> (Please give quantitative indications wherever possible) Administrative Offices This eight-story urban mixed-use project is a key architectural feature in the city's expanding downtown. The building houses 96,000 SF of office space, and 16,500 SF of retail and restaurant space, as well as a 364-car parking garage to serve this rapidly developing area.</p>		
<p><u>Nature of Firm's Responsibility in Project</u></p> <p>Master Planning, Programming, Architectural Design, Construction Documents and Construction Administration</p>		
<p><u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u></p> <p>Carlos Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal Scott Martin, LEED AP – Project Designer Michael Houseman, AIA, LEED AP – Project Director</p>		

FORM 5

ILLUSTRATIVE WORK
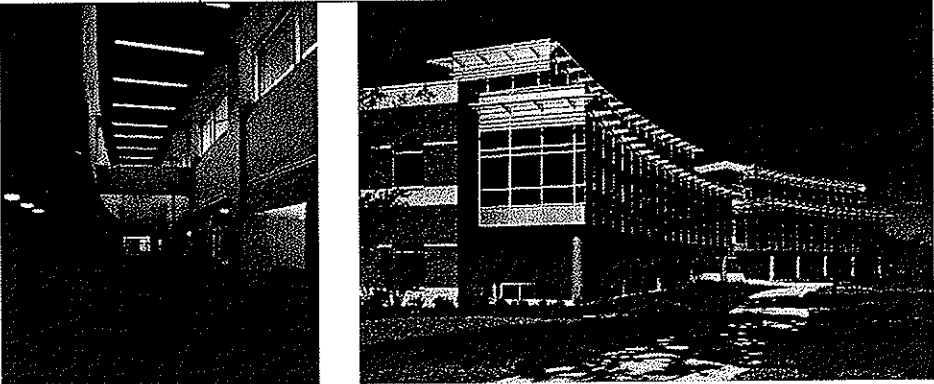
<u>10. Project Name & Location</u> Education and Human Services Building University of North Florida Jacksonville, Florida <u>Project Manager: Mike Houseman, AIA, LEED AP</u>		<u>Project Owners Name & Address</u> University of North Florida College of Education and Human Services 1 UNF Drive Jacksonville, FL 32224				
<u>Completion Date (Actual or Estimated)</u> 2009						
<u>Estimated Cost (In Thousands)</u> <table border="1"> <tr> <td><u>Entire Project</u></td> <td><u>Work for which firm was/is responsible</u></td> </tr> <tr> <td>\$21,000</td> <td>\$21,000</td> </tr> </table>		<u>Entire Project</u>	<u>Work for which firm was/is responsible</u>	\$21,000	\$21,000	<u>Project Owner's Contact Person, Title, & Telephone Number</u> Larry Daniel, Dean (904) 620-2520
<u>Entire Project</u>	<u>Work for which firm was/is responsible</u>					
\$21,000	\$21,000					
<u>Scope of Entire Project</u> 98,000 SF, 3-story classroom and office building with specialized research labs. LEED Design Silver.						
<u>Nature of Firm's Responsibility in Project</u> Comprehensive planning, architecture and interior design, construction documents, construction administration and LEED Design Services.						
<u>Firm's Personnel (Name/Project Assignment) That Worked on the Stated Project that Shall Be Assigned to the County's Project</u> Carlos Barrios, AIA – Principal-In-Charge Tim Baker, AIA – Design Principal Scott Martin, LEED AP – Project Designer Jeff McComas – Project Architect						

Tab G

FORM 6**VOLUME OF WORK**

Prime Consultant's volume of work performed for the Sumter County Board of County Commissions
As a prime consultant and as a sub consultant – currently and previously

Not Applicable – We have not performed any work for the Sumter County Board of County Commissions as a prime consultant or as a sub consultant.

Name of Project (include continuing contracts)	Prime or Sub	Total Contracted Fee Amount	Approximate date of award of contract

Tab H

FORM 7

ADDITIONAL INFORMATION



Firm Profile

Baker Barrios Architects, Inc., was **incorporated in 1993** in Orlando, Florida with the vision of establishing a legacy based on creative excellence, innovative solutions and long-term relationships. Since its inception, Baker Barrios Architects, Inc. has grown from a local professional design firm in Orlando, Florida to a cohesive network of offices in Tampa and Atlanta.


The firm's operating principals, along with our dedicated staff of over 60 professionals provide full-service architectural, interior design and construction administration services. Our staff of well-trained and experience professionals listen to the client's needs and desires, and then translate these goals into a projects design. Baker Barrios Architects, Inc. provides clients with a proven track record in the coordination of production, master planning, visual and creative design, design quality and the provision of quality control while maintaining the project's construction budget. Our high level of involvement and follow-through to the project's completion ensures that the Owner's objectives are met and the integrity of design is maintained even after Owner/Tenant occupancy.

Baker Barrios Architects, Inc. attributes its success to a core philosophy that is carried throughout every aspect of the organization: **Our business is service.**

Project Management

Our approach to expediting and executing projects is based on the BBA **Teamworks** concept. The **Teamworks** method relies on the establishment of a strong project leader (PM), Mike Houseman, who serves as the principal point of communication, authority and accountability.

Our **Teamworks** workshops are not a single kick-off session, rather a series of multiple collaborative sessions that nurture creative solutions and interaction with Sumter County, the Fire Services Department, Consultants and the Construction Manager. Beginning at the first "kick-off" session we will work together to begin this process of developing a high level of trust and comfort that enhances the flow of ideas. During this process we brainstorm, discuss, verify, modify, delete and incorporate information into the design of your project. The process is one of always moving forward, shortening the project design duration due to correct decision-making.

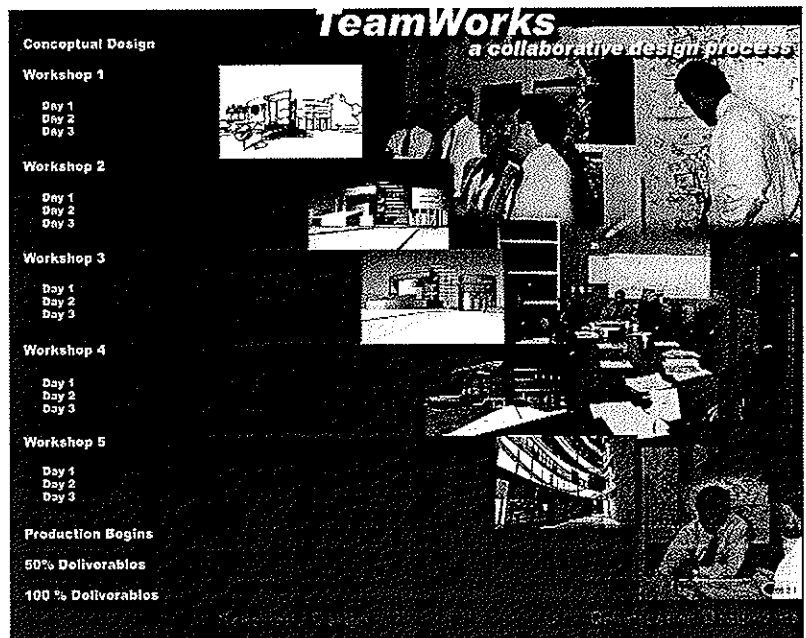

In tandem with our **Teamworks** sessions, we utilize our computer generated design, rendering and modeling technologies to incorporate and visually reflect the design decisions made during those workshops. Our clients' planning and project management departments, user groups and other stakeholders as well as the construction manager and consultants find that the **Teamworks** application of those technologies facilitate understanding and decision making. Our software technologies allow all involved in the workshops to clearly understand the project scope, design and building system details that produce more accurate costs and tighter schedules.

This process will be of great benefit in preparing cost models and/or estimates to establish an initial construction budget and to determine whether the design is still within the pre-established budget.


FORM 7 ADDITIONAL INFORMATION

Total Quality Assurance Program


BBA's Total Quality Assurance (TQA) Program ensures that our work is complete, reliable, and of sound quality. The BBA TQA program - overseen by our Technical Director, Carlos Barrios, AIA, who has over 30 years of project quality assurance/quality control experience - requires that all drawings and related documents are reviewed for completeness, referencing, coordination and constructability before being released from our office. BBA's TQA Program enhances quality control throughout the entire process. Once documents are completed they're submitted for further revision for constructability and completion.

The Total Quality Assurance Program focuses on six keys to quality and checking:

1. Create Workplan and cartoon set
2. Comprehensive checklists
3. Office standards and lessons learned
4. TEAM-CHECK (REDI-CHECK)
5. Independent review
6. Empowerment and accountability of Project Manager and each team member

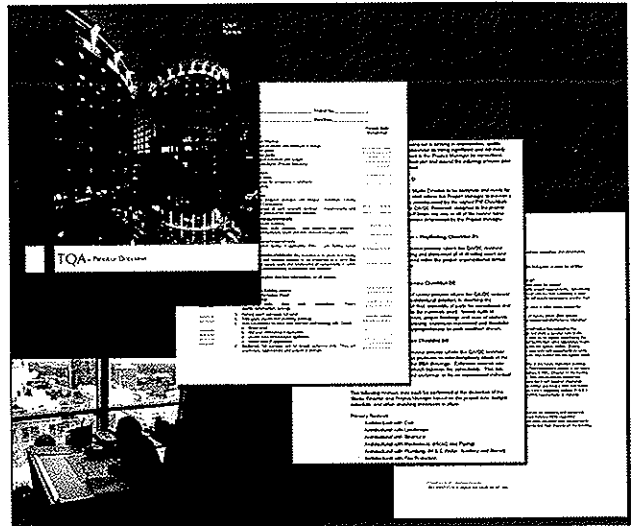

Quality Assurance is embraced as a team concept, which helps ensure a high quality product.



Design Ability

Baker Barrios Architects was awarded Central Florida's Best Architecture Firm by the Orlando Business Journal in 2007.

Our architecture and interior design studios work in tandem to ensure that all buildings are constructed for their life cycle and goals. We provide expertise and leadership in creating buildings and environments that uniquely respond to our clients' needs. By listening to what the client really needs and desires, and translating those goals into a project's budget and occupancy milestone, we develop environments that accommodate new technologies, expansions, and effective and flexible workplace design that promote durability, cost effectiveness and future growth.



MBE Certified

BBA is dedicated to providing clients with the highest quality of service in the field of Architecture and Interior Design. As part of this commitment, the company continually seeks to create a truly diverse employee base and work environment in order to ensure that the most innovative design solutions are made available to our clients. It is BBA's policy to strive to promote the creative and professional growth of this varied and highly talented workforce and this superior work environment. Baker Barrios Architects, Inc. (BBA) is currently certified as a Minority Owned Business Enterprise with the City of Orlando.



FORM 7
ADDITIONAL INFORMATION

Schedule and Cost Control

Budget control for your project will start with the initial programming effort. This effort is all about finding a balance between the needs of potential users, the quality required by Sumter County and the funds available. With each modification to the program and during the pre-design process, cost estimates are re-generated to understand the impact on the project budget. Once the program is agreed upon, our team will begin the process of breaking down the project budget into its component parts, i.e., the exterior envelope, the mechanical system, etc. Each project component can be tracked separately. This will allow for thoroughness in both project and cost management. The component budget is tracked by quantity and by unit cost throughout the design process. At each phase, the design is repeatedly analyzed by both the design team and the construction manager. Our understanding of the local construction market, with up-to-date price information will allow the design team to develop designs that will stay within the budget.


Project	Original Construction Budget	Final Project Cost	Original Duration of Schedule	Final Duration of Schedule	Dollar Amount of Change Orders
Allied Health & Science Valencia Community College	\$19,469,088	\$18,000,000	390 days	365 days	\$1,968,449 savings
Psychology University of Central Florida	\$12,479,536	\$10,414,507	424 days	484* days <i>*Owner requested changes</i>	\$2,065,029 savings
Education and Human Services Building University of North Florida	\$21,194,717	\$17,140,724 (estimated project is in construction)	359 days	N/A - in construction	\$3,967,422 savings
C. W. Bill Young Hall University of South Florida	\$9,099,000	\$10,909,700*	730 days	820* days <i>*Owner requested changes</i>	\$1,810,000
OUC Reliable Orlando Utilities Commission	\$40,093,412	\$34 million	398 days	510 days	\$390,000 savings

FORM 7

ADDITIONAL INFORMATION

Sustainable Design

Of increasing importance to clients is our familiarity and expertise with sustainable design. Designing a LEED certified building does not need to be complicated. Our approach to designing "Green" buildings is a holistic design, management and construction process. BBA conducts "Green" workshops as part of our Teamworks process, in order to identify sustainable design opportunities. BBA is a member of the U.S. Green Building Council and has LEED 2.0 Accredited Professionals on staff.

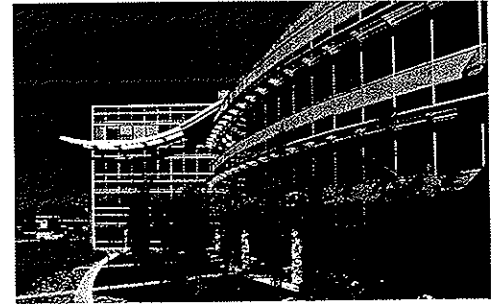

Our clients in the effort to achieve LEED certified buildings include:

- **Discovery Tech Center II** – Gold Level Core & Shell
- **Orlando Utilities Commission** – Gold Level
- **Valencia Community College, Allied Health & Science** - Gold Level
- **University of North Florida, Education and Human Services Building** - Silver Level
- **Barona Administration Building and Tribal Services Center** – LEED Certification
- **Department of Homeland Security, US Citizen and Immigration Services** – LEED Certification
- **Hensel Phelps Southeast District Office** – Gold Level
- **University of Central Florida, Morgridge International Reading Center** – Silver Level
- **MYX Café** – LEED Certification
- **Dr. P. Phillips Performing Arts Center** - LEED
- **Corus Group, LLC Exterior Renovation** - Gold Level
- **GAI Office Building** – LEED Certification

Testimonials / Reference Letters

Baker Barrios Architects, Inc. attributes its success to a core philosophy that is carried throughout every aspect of the organization: **Our business is service.**

We endeavor to service our client's needs and our client's often recognize this by giving us repeat work. We have continued this tradition with all of our clients.

The following pages showcase letters of recommendation for Baker Barrios Architects, Inc.

"We are pleased to once again have Baker Barrios Architects join the development team of one of our projects. We have a long-standing relationship and I'm confident that their team of architects and designers will deliver a design that Taurus will be proud of."

Jeff K. McFadden, SIOR
Taurus Southern Investments Managing Partner

FORM 7
ADDITIONAL INFORMATION



Sheriff Kevin Beary
COUNTY SHERIFF'S OFFICE


Telephone: 407-254-7000

P.O. Box 1440, Orlando, Florida 32802-1440
Visit us on the Internet: <http://www.ocso.com>

Mr. Carlos Barrios
Baker Barrios Architects
300 S. Orange Avenue
Suite 900
Orlando, FL 32801

Dear Mr. Barrios:

Over the past five years, you and your staff have been tasked with designing and implementing the design of the new Sheriff's Central Operations Center. During this time we have relied on the training and expertise of your firm heavily. My staff and I have been very pleased with the outcome of your work as we complete the third and final phase. During all three phases we have been able to rely on Baker Barrios Architects develop solutions to our space problems and provide use with functional and attractive space to serve the needs of the Citizens and guests Orange County. The solutions were not always easy to achieve as we were renovating an existing building that is over forty years old, but you and your capable staff never failed meet our needs. I highly would recommend Baker Barrios Architects to anyone who is in need of architectural services.

Sincerely,

Kevin Beary
Sheriff of Orange County



The First Agency in Orange County to Receive Both
International and State Accreditation



"The Osceola County Building and Development Department would like to compliment Baker Barrios Architects, Inc. for its consistency on all of its construction drawings reviewed for Osceola County projects.

Baker Barrios' superior standards for excellence shows. Because of your firm's consistency in producing construction drawings without need for AHJ comments our job is made easier and in turn keeps project costs down.

Baker Barrios is a pleasure to work with. We look forward to working with you on future endeavors and are pleased to recommend your firm for future projects in Osceola County."

Wayne Smith
Commercial Plans Review, Osceola County
Building and Development Department

"West Point is a national treasure; our standards for construction are very high, which the public rightly demands and expects. We hold BBA in extremely high regard and trust them implicitly. Without reservation, I would strongly recommend their services to anyone and would stake my own reputation on their success. BBA has transformed the way in which the West Point Association of Graduates manages privately-funded construction at the United States Military Academy.

The total value of projects managed for the West Point Association of Graduates by BBA exceeds \$100 million. In every case, we have always met or come under the initial project budget. BBA has saved our Association and West Point literally millions of dollars."

Greg Louks
formerly with West Point Association of Graduates



PROPERTY MANAGEMENT DEPARTMENT

37 Vickhill Street, NE
Marietta, Georgia 30066-1164
Phone: (770) 570-3100 Fax: (770) 520-2148

John A. Reida
DIRECTOR

Allen Kruonberger
Property Manager
Cobb County Property Management
27 Waddell Street
Marietta, GA 30060

Mr. Travis Vickers
Principal
Baker Barrios Architects, Inc.
730 Peachtree St.
Suite 300
Atlanta, GA 30308

Re: Cobb County Fire Station 5 Architectural and Interior Design Services

Dear Travis:

On behalf of Cobb County Property Management I want to extend our gratitude to you and Baker Barrios Architects. Your firm has provided extraordinary architecture and interior design services for the Cobb County Fire Station 5 project. We have thoroughly enjoyed the collaborative design process and the degree of personal attention and service we have received from your firm.


Throughout the Fire Station 5 project, we have been impressed by your firm's ability to think outside the box during programming, create 3D renderings that gave an impressive preview of the building being designed, and the extensive attention to detail during the construction phase.

We have found your architects and interior designers to be very professional and we appreciate the Principal involvement throughout the entire process. You and your team listen, respond and follow through. Your team has successfully helped us achieve the vision we want, within our budget.

After such a successful project as Cobb County Fire Station 5 we would highly recommend your firm's services for any future projects.

Sincerely,

Cobb County Property Management,


Allen Kruonberger
Property Manager

Cc: Bryan Schroeder

Cobb County ...
Employs the Best!
An Equal Opportunity Employer

Architects

FORM 7
ADDITIONAL INFORMATION



OFFICE OF THE DEAN
College of Education and Human Services

UNIVERSITY of
NORTH FLORIDA

June 24, 2009

Mr. Tim Baker, AIA, Principal
Mr. Carlos Barrios, AIA, Principal
Baker Barrios Architects
189 S. Orange Avenue - Suite 1700
Orlando, FL 32801

Dear Messrs. Baker and Barrios:

I would like to express my sincere appreciation to your firm for the excellent work you have done in the design and project management of our new College of Education and Human Services building at UNF. The new facility is all that we had dreamed it would be, and the closeness of the finished product to the original design is uncanny. The communication that your firm established among our College building team, the UNF Facilities Planning Office, Ajax Construction, and your own team was exemplary. You have certainly lived up to your corporate motto, "our business is service."

Tim and Carlos, I further appreciate the direct attention that each of you took in our project. Having had both of you to participate in the early charrettes convinced us all of the full firm's commitment to the project, and, Carlos, your periodic visits to update us and discuss our satisfaction with the project have been greatly appreciated. It has been my privilege to get acquainted with both of you.

There are many features of the building that are impressive. The use of natural lighting, curved hallways, spacious lobbies, and smart design of classrooms are particularly noteworthy. The balance of glass and brick on the building exterior gives it a professional look that is just right for our College.

While there are many persons in your firm who I am sure have contributed to the success of our work, I would like to call attention to the work of a few individuals whose particular contributions have been particularly instrumental to the project:

- Mike Houseman and Jessica Randolph did an exceptional job on the interior design and selection of furnishings. Jill is a true "detail person" and an outstanding expert in her field. Her attention to very specific requests we had were especially appreciated. We have heard many wonderful comments about the color schemes in the building, and the furnishings are absolutely fabulous. The building has a soothing ambience that is very well suited to our work and fitting for our instructional needs.

Bedework H. Smith, III - UNF Director, Jacksonville, FL 32224-1650
Tel: 904.620.7520 Fax: 904.620.7527 www.unf.edu/cedhs
Equal Opportunity/Equal Access/Affirmative Action Institution

"We are very pleased with the work completed by Baker Barrios Architects. They have provided us with a design that is highly functional, yet very appealing. We look forward to working with them on future projects."

Tonia Sellers, Managing Partner
Weissman, Nowack, Curry & Wilco, P.C.

"After nearly one year of occupancy, the design of our Phase II corporate office and operations center has been proven by the facts that our employees are happy. The building and parking capacity has continued to meet our high volume operations. Designed as a companion building, the site plan, architectural design, and interior plan has continued to exceed our expectations as they relate to high employee morale, our master plan and business operations and corporate image."

Steven Suiter
Former Director, Corporate Real Estate/Facilities, Convergys

- Rod Blakeslee was instrumental in some of our early thinking about furnishings and provided exceptional expertise in the design of the lighting in the building. The lighting methods selected allow for maximum lighting with a minimal number of fixtures and take advantage of the abundant natural lighting that the design of the building affords us.
- Wayne Dunkelberger provided us with excellent conceptual ideas and building renderings during the early part of the project. The elevation of the building is perfect for the site, and I am sure Wayne's expertise contributed to the impressive final product.
- Tyler Kirby took expressed appreciable interest in showcasing the project in your corporate materials. We look forward to seeing the work that she does in publicizing our wonderful building.

In sum, I think we can all be proud of the exceptional facility you have provided us. We have been told with some frequency by both campus colleagues and visitors that we have the most attractive building on campus. We always love to hear this, and I am sure that you do as well. Comments of this type are a testimony to the expertise in design and project management provided by Baker-Barrios. It is our good fortune that we selected your firm for this project.

Sincerely,

Larry G. Daniel

Larry G. Daniel, Ph. D.
Dean

cc: Zak Ovadia, Director, UNF Facilities Planning

**Baker
Barrios**

Architects

FORM 7

ADDITIONAL INFORMATION



Firm Profile

Baker Barrios Architects, Inc., was **incorporated in 1993** in Orlando, Florida with the vision of establishing a legacy based on creative excellence, innovative solutions and long-term relationships. Since its inception, Baker Barrios Architects, Inc. has grown from a local professional design firm in Orlando, Florida to a cohesive network of offices in Tampa and Atlanta.


The firm's operating principals, along with our dedicated staff of over 60 professionals provide full-service architectural, interior design and construction administration services. Our staff of well-trained and experience professionals listen to the client's needs and desires, and then translate these goals into a projects design. Baker Barrios Architects, Inc. provides clients with a proven track record in the coordination of production, master planning, visual and creative design, design quality and the provision of quality control while maintaining the project's construction budget. Our high level of involvement and follow-through to the project's completion ensures that the Owner's objectives are met and the integrity of design is maintained even after Owner/Tenant occupancy.

Baker Barrios Architects, Inc. attributes its success to a core philosophy that is carried throughout every aspect of the organization: **Our business is service.**

Project Management

Our approach to expediting and executing projects is based on the BBA **Teamworks** concept. The **Teamworks** method relies on the establishment of a strong project leader (PM), Mike Houseman, who serves as the principal point of communication, authority and accountability.

Our **Teamworks** workshops are not a single kick-off session, rather a series of multiple collaborative sessions that nurture creative solutions and interaction with Sumter County, the Fire Services Department, Consultants and the Construction Manager. Beginning at the first "kick-off" session we will work together to begin this process of developing a high level of trust and comfort that enhances the flow of ideas. During this process we brainstorm, discuss, verify, modify, delete and incorporate information into the design of your project. The process is one of always moving forward, shortening the project design duration due to correct decision-making.

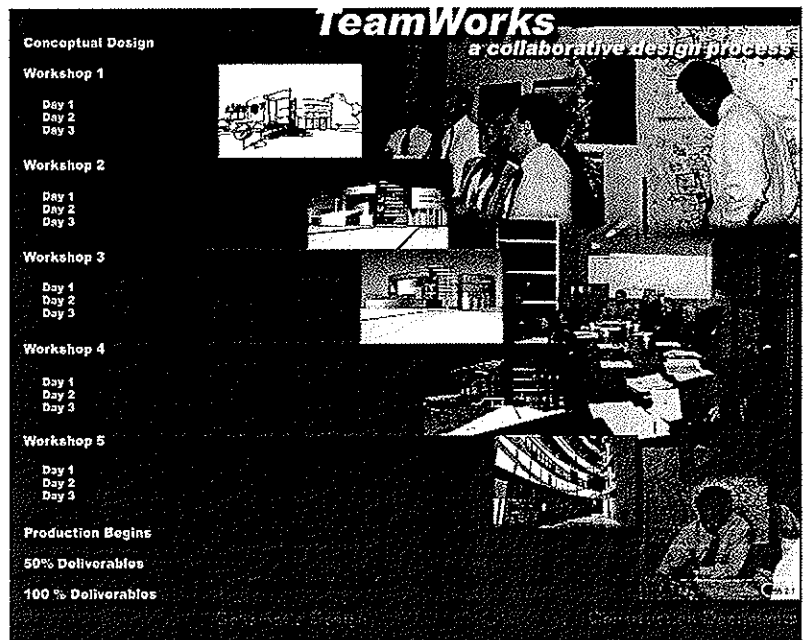

In tandem with our **Teamworks** sessions, we utilize our computer generated design, rendering and modeling technologies to incorporate and visually reflect the design decisions made during those workshops. Our clients' planning and project management departments, user groups and other stakeholders as well as the construction manager and consultants find that the **Teamworks** application of those technologies facilitate understanding and decision making. Our software technologies allow all involved in the workshops to clearly understand the project scope, design and building system details that produce more accurate costs and tighter schedules.

This process will be of great benefit in preparing cost models and/or estimates to establish an initial construction budget and to determine whether the design is still within the pre-established budget.
